

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 08 January 2018

Site Location: 4825 Glenbrook Road

Weather:

Very cold Low 19° High 28°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed	Askew, Tom	
Mantell, Dawn	Prate, Warren	Dusick, Brandon	
Marian, Jedidiah	Yorkshire, Bart	McCoy, Bill	
Matter, Phil			
Nelms, Bobby		Myers, Royce	
Oien, Joshua	LIFE STAR	Bagley, Robert	
Pilato, Bryan		Wainwright, Leroy	
Rider, Matthew	Vines, Doreen	Miller, Jonathan	
Rockwell, Margaret	Murdock, Mark	McGill, Andre	
Sprouse, Mark		Blaylock, Gary	
		Shavers, Dedareu	
Wunschel, Scott			
Peterlin, Joe	ACCUPERMIT	CHENC	
		Shott, Ken	
	Schmidt, James	CENAB	
	Williams, Angelo	Martin, JR	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

After some delays getting the site up and operational due to the extreme cold we began collecting soil samples. The sample team encountered what we believe to be a second concrete slab under soil boring locations 16 and 18 at approximately 2.5 feet BGS. SB-17 was not samples.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:**Instructions given by government personnel:****Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

R₃

20 1-8-17

0630 SAFETY BRIEF

0700 TRAFFIC SIGNS IN PLACE - RADIO CHECKS

0740 MINICAMS UP.

0818 DRAINS PUMPS RUNNING

1030 STARTING MID DAY CHALLENGE.

1058 MINICAMS BACK UP.

1120 TERN 3 DOWN RANGE "LEVEL 15"
SPROUSE, MANTZEL, OIGN.

1124 UNCOVERED BH16 STARTING SAMPLING

1142 0-2' COLLECTED.

1155 2-4' COLLECTED SUSPECTED HITTING
CEMENT PAD.

1246 BH"18 0-2' COLLECTED.

1280 2-4' @ bin concrete pad.

1304 BH16 & 18 COVERED w/ PLASTIC.

1310 TERMS CLEARED POS STARTING
END OF DAY CHECKS.

1400 SECURED DUE TO WEATHER

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 09 January 2018

Site Location: 4825 Glenbrook Road

Weather:

Cold Low 30° High 47°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed	Askew, Tom	
Mantell, Dawn	Prate, Warren	Dusick, Brandon	
Marian, Jedidiah	Yorkshire, Bart	McCoy, Bill	
Matter, Phil			
Nelms, Bobby		Myers, Royce	
Oien, Joshua	LIFE STAR	Bagley, Robert	
Pilato, Bryan		Wainwright, Leroy	
Rider, Matthew	Vines, Doreen	Miller, Jonathan	
Rockwell, Margaret	Haupt, Calvin	McGill, Andre	
Sprouse, Mark		Blaylock, Gary	
		Shavers, Dedareu	
Wunschel, Scott		Wooten, Mike	
Peterlin, Joe	ACCUPERMIT	CHENC	
		Shott, Ken	
	Schmidt, James	CENAB	
	Williams, Angelo	Martin, JR	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Parsons personnel installed well liners and caps in locations SB-07 and SB-10. The team also sealed soil boring locations 8,9,and 11 with concrete epoxy. The Sampling team completed SB-19 with refusal at 9 feet 11 inches.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors


DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Daily Contractor Quality Control Report												
Contract Number:	W912DY-09-D-0062											
Delivery Order Number:	0006											
Project Name:	4825 Glenbrook Rd. Remedial Action, Spring Valley FUDS.											
Project Number:	748272.03000											
Site Location:	Spring Valley, Washington, DC.											
Date:	1/9/2018											
Weather:	Mostly Sunny 27-47°F, wind 0-7 mph											
Field Instrument:	Arsine - (1) Down Range, HCL - (1) Down Range, HCN - (1) Down Range, (1) PID - Down Range, MiniCAMS, DAAMS											
Measurements:	All Non Detect.											
Calibrations:	Arsine and HCL – Fresh air zero calibration, HCN – Fresh Air and 10ppm HCN/Nitrogen Balance, PID - 100ppm isobutylene and fresh air.											
Activities Conducted:	Parsons team sampled Borehole 19. Teams collected 5 samples from intervals 0-2, 2-4, 4-6, 6-8, and 8-10. Samples submitted for headspace. Parsons team made repairs to truck gate.											
Summary:	Parsons team sampled Borehole 19. Teams collected 5 samples from intervals 0-2, 2-4, 4-6, 6-8, and 8-10. Samples submitted for headspace (see Soil COC for IDs). Parsons team made repairs to truck gate.											
Items Found:	None											
Contingency Plan Initiated:	No											
Air Monitoring:	MiniCAMMS , DAAMS											
IDW Generated:	PPE and Decon Water											
Waste Disposal:	None											
Departures from approved SSWP:	None											
Problems encountered/resolutions:	None											
Instructions given by government personnel:	None											
Attachments:	Sample Logs Daily QC Logs UXO Safety Log (Weekly) COC											
Signed by:												
Name (print):	Margaret											
Date:	1/9/2018											
Phone Number:	571-721-9804											
Copy sent to:	Scott Wunschel											

Pg

21 19-17

0630 SAFETY BRIEF.

0700 RADIO CHECKS.

0727 PDS UP @ 70'S MINICAMUS UP.

0855 DAMS PUMPS RUNNING.

1041 TEAM 1 DOWN RANGE, RIDER, OIGW
COURTNEY.

1043 GEO PROBE BH#19

1050 TEAM REPORTS PROBLEM @ 1.5" PVC
PIPE. MOVED BH#19 6" SOUTH

1129 BH#19 0-2' COLLECTED

1139 TEAM 1 CLEARED PDS.

1146 STARTING MID DAY CHALLENGE.

1209 MID DAY CHALLENGE COMPLETE.

1239 TEAM 3 DOWN RANGE, SPROUSE, MANTON, DILATO

1247 BH#19 2-4'

1300 BH#19 2-4' COLLECTED.

1321 4-6' COLLECTED. BH#19

1330 JOE POTERMAN DOWN RANGE.

1357 6-8' COLLECTED BH#19

1425 8-10' COLLECTED BH#19 Refusal @ 9'11"

1435 JOE POTERMAN CLEARED PDS.

1444 TEAM 3 CLEARED PDS.

1500 STARTING END OF DAY CHECKS

1700 SECURED *[Signature]*

PC
22

1-10-17

0630 SAFETY BRIEF.

0700 TRAFFIC SIGNS IN PLACE

0715 RADIO CHECKS.

0759 PDS UP

0806 MINICAMS UP

0828 DAMS PUMPS RUNNING.

0840 TEAM 1 DOWN RANGE "LEVEL B" RIDGE
GLEN, COURTNEY.

0850 STARTING GEO PROBE BH "20"

0918 COMPLETED 0-2' COMPOSITE COLLECTED.

0909 ADVANCING PROBE TO 4'

0933 COMPLETED 2-4' COMPOSITE COLLECTED.

0941 TEAM 1 REPORT REFUSAL @ 5'4".

0956 JOE PETERLIN DOWN RANGE "LEVEL B"

1008 4-6' COMPLETED & COMPOSITE COLLECTED.

1021 BH 19920 FILLED W/ BENTONITE.

1022 JOE PETERLIN CLEARED PDS.

1051 TEAM 1 CLEARED PDS.

1105 STARTING MID DAY CHALLENGE

1218 MID DAY COMPLETE.

1245 TEAM 3 DOWN RANGE, LEVEL B, SPARSE
MANTEL, PILATO.

1247 ADVANCING GEO PROBE IN BH "1"
0-2'

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 11 January 2018

Site Location: 4825 Glenbrook Road

Weather:

Mild Low 46° High 50°

Personnel on Site

PARSONS	ZES	ECBC	
Mantell, Dawn	Mangosh, Ed	Askew, Tom	
	Prate, Warren	Dusick, Brandon	
	Yorkshire, Bart	McCoy, Bill	
Matter, Phil			
Nelms, Bobby		Myers, Royce	
Oien, Joshua		Bagley, Robert	
Pilato, Bryan	LIFE STAR	Wainwright, Leroy	
Rider, Matthew	Alfaro, Walter	Miller, Jonathan	
Rockwell, Margaret	Haupt, Calvin	McGill, Andre	
Sprouse, Mark		Blaylock, Gary	
		Shavers, Dedareu	
Wunschel, Scott		Wooten, Mike	
Peterlin, Joe	ACCUPERMIT	CHENC	
		Shott, Ken	
	Schmidt, James	CENAB	
	Williams, Angelo	Martin, JR	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Sampling teams expect to complete location SB-02 and attempt to core through what we believe to be a second concrete pad under SB 16, 17 and 18. Site personnel performed end of week equipment maintenance.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCs)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

P₂

24 1-11-17

0630 SAFETY BRIEF

0700 TRAFFIC SIGNS IN PLACE

0724 MINICAMS UP

0740 RADIO CHECKS

0750 PDS UP 74°F

0854 TEAM 1 DOWN RANGE "LEVEL B" RIDGE, 0-10' MANTLE

0858 ADVANCING GEO PROBE IN BH#2 0-2'

0908 0-2' COMPLETED ADVANCING PROBE TO 2-4'

0918 2-4' COMPLETED ADVANCING PROBE 4-6'

0932 4-6' COMPLETED AUGURING HOLE

0952 JOE PETERLIN DOWN RANGE "LEVEL B"

0950 ADVANCING PROBE 6-8'

1012 6-8' COMPLETED AUGURING HOLE

1022 ADVANCING PROBE 8-10'

1045 8-10' COMPLETED, REFUSAL @ 10'

1048 JOE PETERLIN CLEARED PDS

1107 TEAM 1 CLEARED PDS

1108 STARTING MID DAY CHALLENGE

1155 MID DAY CHALLENGE COMPLETE

1302 TEAM 3 DOWN RANGE "LEVEL B"

1302 SPROUSE MANTLE, PDS TO

BACK FILLING BH#1 & BH#2 w/PORTLAND CEMENT.

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 16 January 2018

Site Location: 4825 Glenbrook Road

Weather:

Cold Low 29° High 40°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed	Askew, Tom	
Mantell, Dawn	Prate, Warren	Nguyen, Nam-Phuogn	
Marian, Jedidiah	Yorkshire, Bart	Copeland, Eric	
Matter, Phil			
Nelms, Bobby		Myers, Royce	
Oien, Joshua		Bagley, Robert	
Pilato, Bryan	LIFE STAR	Wainwright, Leroy	
Rider, Matthew	Vines, Doreen	Miller, Jonathan	
Rockwell, Margaret	Haupt, Calvin	McGill, Andre	
Sprouse, Mark		Blaylock, Gary	
Wunschel, Reina		Shavers, Dedareu	
Wunschel, Scott			
Peterlin, Joe	ACCUPERMIT	CHENC	
		Shott, Ken	
	Schmidt, James	CENAB	
	Williams, Angelo	Martin, JR	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Parsons sample teams completed samples from SB-16, they collected samples from depths 4-6, 6-8, 8-10, and 10-12. Sample teams also completed SB-17 and collected samples from depths 0-2, 2-4, 4-6, 6-8, 8-10, 10-12. Personnel continues to cut concrete at location SB-18 with the coring machine. The team did not get through the concrete on SB-18.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

26 1-16-17

0630 SAFETY BRIEF

0710 RADIO CHECKS, TRAFFIC SIGNS
IN PLACE.

0737 MINICAMS UP.

0803 DAMS PUMPS RUNNING.

0834 TEAM 3 DOWN RANGE. SPROUSE, OLSON
COURTNEY, PETERLIN0845 ADVANCING ECO PROBE IN RA#16
4-6'

0855 4-6' COMPLETED AND COLLECTED.

0905 ADVANCING ECO PROBE 6-8'

0923 6-8' COMPLETED AND COLLECTED

0932 ADVANCING PROBE 8-10'

0950 8-10' COMPLETED AND COLLECTED

0957 ADVANCING PROBE 10-12'

1006 10-12 COMPLETED, REFUSED @ 11'10"

1010 PETERLIN CLEARED PDS

1014 ADVANCING ECO PROBE RA#17 0-2'

1032 0-2' COMPLETED & COMPLETED


ADVANCING PROBE 2-4'

1045 TEAM 3 CLEARED PDS.

1103 STARTING MID DAY CHALLENGE

1145 MID DAY COMPLETE

1223 TEAM 3. DOWN RANGE COVER 5'

Daily Contractor Quality Control Report												
Contract Number:	W912DY-09-D-0062											
Delivery Order Number:	0006											
Project Name:	4825 Glenbrook Rd. Remedial Action, Spring Valley FUDS.											
Project Number:	748272.03000											
Site Location:	Spring Valley, Washington, DC.											
Date:	1/17/2018											
Weather:	Cloudy with morning snow 19-27°F, wind 0-14 mph											
Field Instrument:	Arsine - (1) Down Range, HCL - (1) Down Range, HCN - (1) Down Range, (1) PID - Down Range, MiniCAMS, DAAMS											
Measurements:	All Non Detect.											
Calibrations:	Arsine and HCL – Fresh air zero calibration, HCN – Fresh Air and 10ppm HCN/Nitrogen Balance, PID - 100ppm isobutylene and fresh air.											
Activities Conducted:	Parsons teams cored concrete at Borehole 18. Sent 5 samples to ECBC for low level analysis. Parsons team was unable to advance Geoprobe in Borehole											
Summary:	Parsons teams cored concrete at Borehole 18. Sent 5 samples to ECBC for low level analysis (See COC for IDs). Parsons team was unable to advance Geoprobe in Borehole											
Items Found:	None											
Contingency Plan Initiated:	No											
Air Monitoring:	MiniCAMMS , DAAMS											
IDW Generated:	PPE and Decon Water											
Waste Disposal:	None											
Departures from approved SSWP:	None											
Problems encountered/resolutions:	None											
Instructions given by government personnel:	None											
Attachments:	Sample Logs Daily QC Logs UXO Safety Log (Weekly) COC											
Signed by:												
Name (print):	Margaret Kockwen											
Date:	1/17/2018											
Phone Number:	571-721-9804											
Copy sent to:	Scott Wunschel											

Pg

28

1-17-18

0630 SAFETY BRIEF.

0651 RADIO CHECKS.

0920 MINICAMS UP, PDS UP

0933 DAMPS PUMPS RUNNING.

1014 TEAM 3 DOWN RANGE "LEVEL 2"

SPROUSE MANTER DELINTO.

1017 COREING BH #18

1135 CURED THROUGH TRYING TO REMOVE
CORE.

1155 TEAM 3 CLEARED PDS.

1205 STARTING MID DAY CHALLENGE

1305 MID DAY CHALLENGE COMPLETE.

1345 TRANSPORTED CURRINOY TO SIBBY
HOSPITAL FOR NON-WORK RELATED ISSUE.

1410 TEAM 1 DOWN RANGE "LEVEL 2"

RIDER OLEN MANTER.

1416 ATTEMPTING TO ADVANCE GEO PROBE
IN BH #18 4'6'.

1430 TEAM REPORTS COMMENT AT 4' IN BH #18

1515 TEAM 1 CLEARED PDS.

1530 STARTING END OF DAY CHECKS.

1550 CURRINOY RELEASED FOR HOSPITAL.

1700 SECURED



SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 18 January 2018

Site Location: 4825 Glenbrook Road

Weather:

Cold Low 25° High 42°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed	Askew, Tom	
Mantell, Dawn	Prate, Warren	Nguyen, Nam-Phuogn	
Marian, Jedidiah	Yorkshire, Bart	Copeland, Eric	
Matter, Phil			
Nelms, Bobby		Myers, Royce	
Oien, Joshua		Bagley, Robert	
Pilato, Bryan	LIFE STAR	Wainwright, Leroy	
Rider, Matthew	Alfaro, Walter	Miller, Jonathan	
Rockwell, Margaret	Haupt, Calvin	McGill, Andre	
Sprouse, Mark		Blaylock, Gary	
		Shavers, Dedareu	
Wunschel, Scott			
Peterlin, Joe	ACCUPERMIT	CHENC	
		Shott, Ken	
	Schmidt, James	CENAB	
	Williams, Angelo	Martin, JR	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site personnel began sampling the ten additional soil boring locations 21-30. Location SB-27 was completed. Site personnel performed end of week equipment maintenance and prepared the site for the possible site/government shut down.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCs)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

[illegible]

Rg

29 1-19-19

0630 SAFETY BRIEF

0700 RADIO CHECKS, TRAFFIC SIGN
IN PLACE.

0728 MINI CAMS UP.

0800 PDS UP @ 76°F MEDICAL IN PLACE.

0824 DAMS PUMPS RUNNING.

0923 TEAM 3 DOWN RANGE LEVEL 5, SPENSE
MANTELL, MARIAN, PETERLIN.

0932 ADVANCING GEO PROBE BH 27, 0'-2'

1003 0'-2' COMPLETE & COMPOSITE COLLECTED

1004 ADVANCING GEO PROBE 2'-4'

1017 2'-4' COMPLETE & COMPOSITE COLLECTED

1018 ADVANCING GEO PROBE 4'-6'

1030 4'-6' COMPLETE & COMPOSITE COLLECTED

ADVANCING GEO PROBE 6'-8'

1053 6'-8' COMPLETE & COMPOSITE COLLECTED.

1106 TEAM CLEARED PDS.

1111 STARTING MID DAY CHALLENGE

1126 MID DAY CHALLENGE COMPLETE.

CONFERENCE CALL @ 11:00

1700 SECURED



SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 22 January 2018

Site Location: 4825 Glenbrook Road

Weather:

Mild Low 51° High 62°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Mantell, Dawn	Prate, Warren		
	Yorkshire, Bart		
Matter, Phil			
Nelms, Bobby			
Oien, Joshua			
	LIFE STAR		
Rider, Matthew			
Rockwell, Margaret			
Sprouse, Mark			
Wunschel, Scott			
	ACCUPERMIT	CHENC	
		Shott, Ken	
	Schmidt, James	CENAB	
	Williams, Angelo	Martin, JR	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Parsons and Zimmer personnel worked to get the site back to an operational status. Equipment was brought on site, inspected and staged for possible sampling activities on Tuesday.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

30 1-22-18

0630 SAFETY BRIEF

0700 RADIO CHECKS TRAFFIC SIGHT
IN PLACE.

0730 PREPARE SITE FOR INTENSIVE
OPERATIONS.

1700 SECURED

[Handwritten signature]

Pg

31


1-23-18

0630 SAFETY BRIEF.

0700 RADIO CHECKS, Teams continuing Set up of the Site.

1100 ECBC Arrived on Site. Beginning Set up of PDS Equipment.

1700 Day Complete.

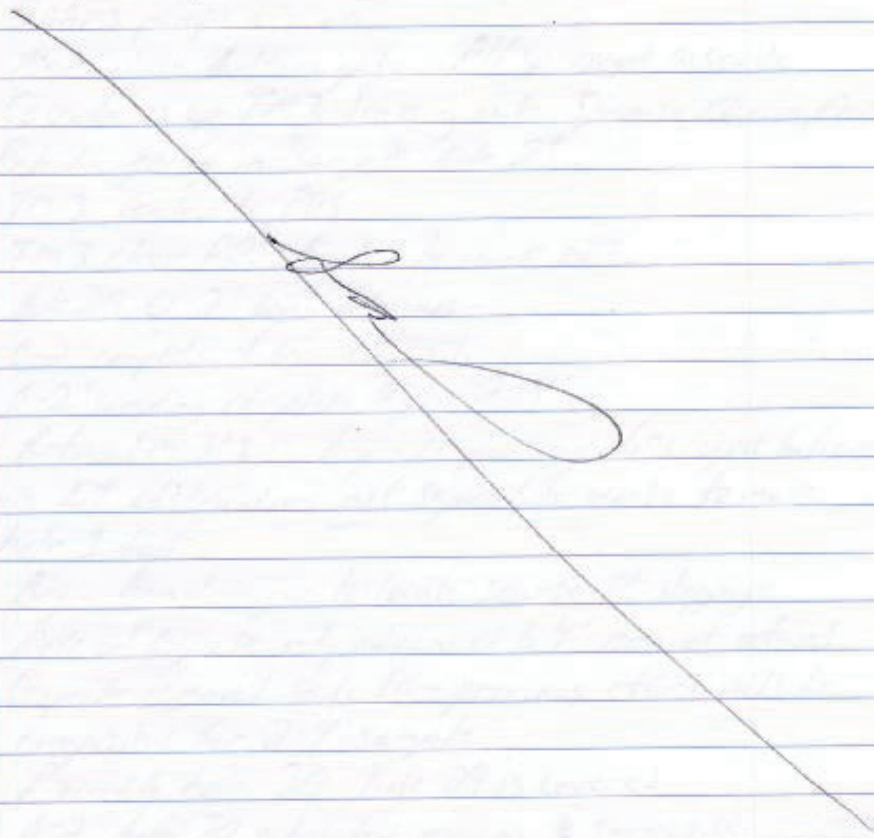

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 24 January 2018

Site Location: 4825 Glenbrook Road

Weather:

Mild Low 38° High 43°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed	Heard, Irving	
Mantell, Dawn	Prate, Warren	Copeland, Eric	
Marian, Jedidiah	Yorkshire, Bart	Perkins, Stephen	
Matter, Phil			
		Myers, Royce	
Oien, Joshua		McGill, Andre	
Pilato, Bryan	LIFE STAR	Wainwright, LeRoy	
Rider, Matthew	Alfaro, Walter	Bartosch, Ian	
Rockwell, Margaret	Brick, Thomas	Wooten, Mike	
Sprouse, Mark		Druyor, Chris	
Wunschel, Reina		Bagley, Robert	
Wunschel, Scott			
	ACCUPERMIT	CHENC	
		Shott, Ken	
	Schmidt, James	CENAB	
	Williams, Angelo	Martin, JR	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site personnel resumed sampling the ten-additional soil boring locations 21-30. Locations SB 24, 25, 26, 29 and 30 were done today.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

(32)

Jan 24, 2018 Wed.

cold, breezy 30's

- 0630 Daily safety & ops briefings. Dren OSHA physical. Helms out sick. ECBC on site prep for Geoprobe sampling.
- 0645 Traffic in place, no signs because of gusty winds
- 0700 Radio checks
- 0747 PDS up and at 76°/Mini CAMS up.
- 0757 DAAMS pumps are on
- 0810 Medical in bottom gate. All up except cascade.
- 0819 Cascade is up TM3 dressing out Sprouse, Marini, Mantell, Peterlin going in sample hole 29.
- 0836 TM3 headed to PDS.
- 0840 TM3 cker PDS headed to work zone.
- 0847 Hole 29 0-2' begin advance
- 0850 0-2' complete & begin composite
- 0902 0-2' sampling complete begin 2-4'.
- 0907 Refusal @ 3'8" begin compositing. Geologist believes we hit obstruction not SaproLife wants to move hole 1 foot.
- 0920 Begin hand-auger to locate source of stoppage.
- 0950 Retrieved Geoprobe only advanced to 4' now at refusal
- 0955 Geoprobe removed Soils from previous effort will be composited for 2-4' sample.
- 1004 Proceed to hole 30 hole 29 is covered
- 1010 0-2' hole 30 extracted moving to composite
cont'd

Pg

36

1-25-18

0630 SAFETY BRIEF

0700 RADIO CHECKS

0740 MINICAMS UP

0754 PDS UP @ 70+

0800 DAM PUMPS RUNNING

0821 TERM 3 DOWN RANGE SPROUSE,
MARION, MANTZEL "LEVEL B"0826 STARTING W/ BH "23" REMOVING
OVER BURDEN

0829 GEO PROBE ADVANCED TO 2'

0837 PETERLIN DOWN RANGE "LEVEL B"

0839 0-2' COMPLETED & COMPOSITE COLLECTED
ADVANCING GEO PROBE 2'-4'0841 2'-4' COMPLETED & COMPOSITE COLLECTED.
ADVANCING GEO PROBE 4'-6'0907 4'-6' COMPLETED & COMPOSITE COLLECTED
TERMIN ROTATORS MOST OF THE 4'-6'
WAS BURIED MATERIAL.

0909 ADVANCING GEO PROBE 6'-8'

0918 4'-8' COMPLETED & COMPOSITE COLLECTED.

1014 ADVANCING GEO PROBE 8'-10'

1015 Refusal @ 9"

1025 8'-10' COMPLETED & COMPOSITE COLLECTED

1030 BH "23" BACKFILLED W/ BENTONITE.

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 26 January 2018

Site Location: 4825 Glenbrook Road

Weather:

Mild Low 37° High 52°

Personnel on Site

PARSONS	ZES	ECBC	
Mantell, Dawn	Prate, Warren	Heard, Irving	
Marian, Jedidiah	Yorkshire, Bart	Copeland, Eric	
Matter, Phil		Perkins, Stephen	
Nelms, Bobby			
	LIFE STAR	Myers, Royce	
Pilato, Bryan		McGill, Andre	
Rider, Matthew	Alfaro, Walter	Wainwright, LeRoy	
Rockwell, Margaret	Vines, Doreen	Bartosh, Ian	
Sprouse, Mark		Smith, Ethan	
Wunschel, Reina		Druyor, Chris	
Wunschel, Scott		Wood, Frank	
Buckley, Sean	ACCUPERMIT	Wilson, Chris	
		CHENC	
		Shott, Ken	
	Schmidt, James	CENAB	
	Williams, Angelo		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site personnel continued sampling the ten-additional soil boring locations. Location SB-28 was completed today. Sample locations SB 21 and 22 were shifted one foot and completed. Sample team relocated SB-18 from the original 20 boring locations and cut out the concrete core. Site personnel performed end of week equipment maintenance.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:**Instructions given by government personnel:****Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

39

1-26-18

0630 SAFETY BRIEF.

0700 RADIO CHECKS. TRAFFIC SIGNS
IN PLACE.

0737 PDS UP @ 72'f

0750 MINICAMS UP.

0800 DAMS PUMPS RUNNING.

0827 TEAM 3 DOWN RANGE LEVEL B"
SPROUSE, MANTEL, PRATT.

0830 REMOVING OVERBURDEN FROM BH#28

0847 ADVANCING GEO PROBE IN BH#28
0'-2'0905 0'-2' COMPLETED & COMPOSITE COLLECTED.
ADVANCING GEO PROBE 2'-4'0925 2'-4' COMPLETED & COMPOSITE COLLECTED
REMOVING OVERBURDEN FROM BH#22.

NOTE BH#22 WAS MOVED 1' TOWARDS 4835.

0946 ADVANCING GEO PROBE IN BH#28 4'-6'

0951 REFUSAL FOR BH#28 @ 5' 1"

1000 4'-6' COMPLETED & COMPOSITE COLLECTED.

1005 ADVANCING GEO PROBE IN BH#22 0'-2'

NOTE: SEAN BULLOCKY DOWN RANGE LEVEL B"
@ 09:45.

1015 BH#22 0'-2' COMPLETED & COMPOSITE COLLECTED

1019 ADVANCING GEO PROBE 2'-4'

Pg

42 1-29-18

0630 SAFETY BRIEF

0750 RADIO CHECKS, TRAFFIC SIGNS
IN PLACE.

0745 MINICHAMPS UP

0800 DAMS PUMPS RUNNING.

0834 TEAM 3 DOWN RANGE "LEVEL B" SPERMIC
MATTER, COURTESY.0838 ADVANCING GEO PROBE IN BH#18
0'-2'

0848 0'-2' COMPLETE & COMPOSITE COLLECTED

0850 ADVANCING GEO PROBE 2'-4'

0859 0'-4' COMPLETE & COMPOSITE COLLECTED.
ADVANCING GEO PROBE 4'-6'0911 4'-6' COMPLETE & COMPOSITE COLLECTED.
ADVANCING GEO PROBE 6'-8'

0920 SEAN BACKLEY DOWN RANGE "LEVEL B"

0944 TAG TEAM REPORTS REFUSAL @ 7'11"

1010 6'-8' COMPLETE & COMPOSITE COLLECTED.

1017 SEAN BACKLEY CLEARED PDS

1018 BH#18 BACKFILLED w/ BENTONITE

1032 TEAM 3 CLEARED PDS.

1050 STARTING END OF DAY CHECKS

1700 SECURED



SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 30 January 2018

Site Location: 4825 Glenbrook Road

Weather:

Cold Low 33° High 36°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed	Heard, Irving	
Mantell, Dawn		Nichols, Doug	
Marian, Jedidiah	Yorkshire, Bart	Baker, Dawn	
Matter, Phil			
Nelms, Bobby		Landers, Brian	
Oien, Joshua	LIFE STAR	Fortier, John	
Pilato, Bryan		King, Bernard	
Rider, Matthew		Bartosh, Ian	
Rockwell, Margaret		Collins, Torrey	
Sprouse, Mark		McClellan, Dale	
Wunschel, Reina		Branson, Bradley	
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Williams, Angelo	Martin, JR	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site personnel continued packing up equipment in preparation for shutting down the PDS.

Decontaminated equipment was double bagged and sent to the federal property site for WPL / GPL analysis. ECBC personnel continued removing equipment from the PDS tent.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCs)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

[illegible]

Pg

43

130-18

0630

SAFETY BRIEF

0700

RADIO CHECKS.

1700

SECURED

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 31 January 2018

Site Location: 4825 Glenbrook Road

Weather:

Very cold Low 18° High 34°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed	Heard, Irving	
Mantell, Dawn	Prate, Warren	Nichols, Doug	
Marian, Jedidiah	Yorkshire, Bart	Baker, Dawn	
Matter, Phil			
Nelms, Bobby		Landers, Brian	
Oien, Joshua		Fortier, John	
Pilato, Bryan	LIFE STAR		
Rider, Matthew		Bartosh, Ian	
Rockwell, Margaret		Collins, Torrey	
Sprouse, Mark		McClellan, Dale	
Wunschel, Reina		Branson, Bradley	
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Williams, Angelo	Martin, JR	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site personnel completed packing up equipment in preparation for shutting down the PDS. ECBC personnel completed removing equipment from the PDS tent and the tent was removed. Parsons personnel completed removing equipment from the dress out trailer.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCs)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

44

1-31-18

0630 SAFETY BRIEF

0700 RADIO CHECKS TRAFFIC

SIGNS IN PLACE.

1700 SECURED

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 01 February 2018

Site Location: 4825 Glenbrook Road

Weather:

Coldold Low 29° High 53°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed	Heard, Irving	
Mantell, Dawn	Prate, Warren	Nichols, Doug	
Marian, Jedidiah	Yorkshire, Bart	Baker, Dawn	
Matter, Phil			
Nelms, Bobby		Landers, Brian	
		Fortier, John	
	LIFE STAR		
Rider, Matthew			
Rockwell, Margaret		Collins, Torrey	
Sprouse, Mark		McClellan, Dale	
Wunschel, Reina		Branson, Bradley	
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Williams, Angelo	Martin, JR	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site personnel relocated the dress out trailer to a position in which it can be picked up by the vender.
Parsons and Zimmer personnel will begin preparation of the soldier pile area along south property line.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCs)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

45

2-1-18

0630 SAFETY BRIEF

0700 RADIO CHECKS.

1300 TWO WEEK LOOK AHEAD.

1700 SECURED

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 05 February 2018

Site Location: 4825 Glenbrook Road

Weather:

Cold Low 35° High 38°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth			
Marian, Jedidiah	Yorkshire, Bart		
Nelms, Bobby			
	LIFE STAR		
Rockwell, Margaret			
Sprouse, Mark			
Wunschel, Reina			
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Williams, Angelo	Martin, JR	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site personnel continued preparation of the soldier pile area along south property line. Teams began cleaning out flowable fill from between soldier pile beams and creating a flat work area with clean backfill soil.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

R

46

2-5-18

0630

SAFETY BRIEF

0700

RADIO CHECKS.

1300

REMOVING BACKFILL NEAR
SOLDIER PILES.

1700

SECURED

[Handwritten signature/initials]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 05 February 2018

Site Location: 4825 Glenbrook Road

Weather:

Cold Low 35° High 38°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Marian, Jedidiah	Yorkshire, Bart		
Matter, Phil			
Nelms, Bobby			
Rider, Matthew	LIFE STAR		
Sprouse, Mark			
Wunschel, Reina			
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Williams, Angelo	Martin, JR	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site personnel continued preparation of the soldier pile area along south property line. Teams continued cleaning out flowable fill from between soldier pile beams and creating a flat work area with clean backfill soil. Personnel put GPL cleared equipment into kits and inventoried parts in preparation for turn in.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pa

47 2-6-18

0630 SAFETY BRIEF

0700 RADIO CHECKS

0830 REMOVING BACKFILL FROM
SOLDIER PILES

1300 REMOVING KNOWABLE FILL FROM
SOLDIER PILES.

1700 SECURED

~~Handwritten signature and initials~~

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 07 February 2018

Site Location: 4825 Glenbrook Road

Weather:

Cold Low 33° High 44°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Marian, Jedidiah	Yorkshire, Bart		
Matter, Phil			
Nelms, Bobby			
Rider, Matthew	LIFE STAR		
Sprouse, Mark			
Wunschel, Reina			
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Williams, Angelo	Martin, JR	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site personnel continued preparation of the soldier pile area along south property line. Teams continued cleaning out flowable fill from between soldier pile beams. Personnel dumped cleared soil from roll off boxes at the federal property site.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

79

48 2-7-18

0830 SAFETY BRIEF 2AD DELAY "OPM"

0900 RADIO CHECKS TRAFFIC SIGN UP

1330 WILLIAMS SCOTSMAN PICKED UP THE
DRESS OUT TRAILOR.

1700 SECURED

RM
SK

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 08 February 2018

Site Location: 4825 Glenbrook Road

Weather:

Very cold Low 26° High 36°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Marian, Jedidiah	Yorkshire, Bart		
Matter, Phil			
Nelms, Bobby			
Rider, Matthew	LIFE STAR		
Sprouse, Mark			
Wunschel, Reina			
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Williams, Angelo	Martin, JR	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site personnel continued preparation of the soldier pile area along south property line. Teams continued cleaning out flowable fill from between soldier pile beams and creating a flat work area with clean backfill soil. Soldier pile area inspected by Berkel & Company in preparation for pre-cast measurements.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Bryan Park Berkel & Company

Contractors

DAVEY ()

ACCUPERMIT (2)

ACI (0)

CPJ (0)

Problems encountered/resolutions:**Instructions given by government personnel:****Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

49

2-8-18

0630 SAFETY BRIEF

0700 RADIO CHECKS

0824 INSTALLING LAGERING.

1015 DAVID KLINE MICHAEL MANTHET &
THOMAS ROSSO, FROM ECBC ON SITE.

1100 CONFERENCE CALL

1310 RETURN ROP ON SITE

1500 TWO WEEK LOOK AHEAD.

1700 SECURED

A handwritten signature in dark ink, appearing to be 'R. J. Kline', is written across the lower half of the page. A long diagonal line is drawn from the bottom of the '1700 SECURED' entry, extending towards the bottom right corner of the page.

Pg

50

2-12-18

0630 SAFETY BRIEF.

0700 RADIO CHECKS TRAFFIC SIGNS
IN PLACE.

0840 SEAN RUCKING ON SITE THE
TEAM IS DUMPING FELLOES.

1035 WILLIAMS SEXTON MAINTENANCE
ON SITE TO REPLACE CIRCUIT
BREAKER.

1700 SECURED

A handwritten signature in dark ink, written diagonally across the lower half of the page. The signature is stylized and appears to be "R. J. Smith".

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 13 February 2018

Site Location: 4825 Glenbrook Road

Weather:

Cold Low 34° High 42°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matthew			
Wunschel, Scott	LIFE STAR		
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Williams, Angelo	Martin, JR	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site personnel continued preparation of the soldier pile area along south property line. Twelve truckloads of backfill soil were brought from the federal property site to continue creating the flat work area for Berkel & Company. One load of cleared soil was sent to the sub-title D landfill.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

51 2-13-18

0630 SAFETY BRIEF

0704 RADIO CHECKS, TRAFFIC SIGNS
IN PLACE.

0930 BRINGING IN CLEAN BACK FILL
FOR SOLDIER PILES.

1700 SECURED

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 20 February 2018

Site Location: 4825 Glenbrook Road

Weather:

Mild Low 52° High 75°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua			
Nelms, Bobby			
Rider, Matthew			
Wunschel, Scott			
	LIFE STAR		
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Williams, Angelo	Martin, JR	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Parsons personnel began an inventory of site GFE at the federal property site. Zimmer personnel began making improvements and repairs to the soil load out area and drum storage areas. An electrician from E.C. Ernst made repairs to the electrical system at the Fed site office trailers.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

54

2-20-19

0630 SAFETY BRIEF

0800 RADIO CHECKS.

1700 SECURE

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 21 February 2018

Site Location: 4825 Glenbrook Road

Weather:

Mild Low 48° High 74°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua			
Nelms, Bobby			
Rider, Matthew			
Wunschel, Scott	LIFE STAR		
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Williams, Angelo	Martin, JR	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site personnel continued inventories of site GFE at the federal property site and improvements and repairs to the soil load out area and drum storage areas.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

R

SS 2-21-18

0630 SAFETY BRIEF

0740 RADIO CHECKS

1700 SECURED

~~BR~~
~~SK~~

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 22 February 2018

Site Location: 4825 Glenbrook Road

Weather:

Mild Low 48° High 50°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua			
Nelms, Bobby			
Rider, Matthew			
Wunschel, Scott			
	LIFE STAR		
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Williams, Angelo	Martin, JR	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Parsons personnel continued inventories of site GFE at the federal property site. Zimmer personnel made repairs to the road and parking areas at the federal property site. Site personnel performed end of week clean up and maintenance.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

P₉

57 2-26-18

0630 SAFETY BRIEF.

0740 RADIO CHECKS.

1700 SECURED

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 26 February 2018

Site Location: 4825 Glenbrook Road

Weather:

Mild Low 47° High 53°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua			
Nelms, Bobby			
Rider, Matthew			
Wunschel, Scott			
	LIFE STAR		
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Williams, Angelo	Martin, JR	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site personnel continued inventories of site GFE at the federal property site and improvements and repairs to the soil load out area and drum storage areas.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

P₄

57 2-26-18

0630 SAFETY BRIEF.

0740 RADIO CHECKS.

1700 SECURED

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 28 February 2018

Site Location: 4825 Glenbrook Road

Weather:

Mild Low 42° High 51°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua			
Nelms, Bobby			
Rider, Matthew			
Wunschel, Scott			
	LIFE STAR		
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Williams, Angelo	Martin, JR	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site personnel reinstalled and turned on the water lines going to the AU ballfield. After the waterlines they continued inventories of site GFE at the federal property site and improvements and repairs to the soil load out area and drum storage areas.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

R

58 2-27-18

8638 SAFETY BRIEF NOTE: THE SITE
WAS CLOSED FOR FUNERAL ON 2-27-18

0733 RADIO CABLES

0800 THE TEAM IS WORKING TO RESTORE
WATER AT THE AN ATHLETIC FIELD

0940 DENNIS CROUSE W/CARA ON SITE

1110 DENNIS CROUSE OFF SITE

1700 SECURED

R
J

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 01 March 2018

Site Location: 4825 Glenbrook Road

Weather:

Mild Low 48° High 53°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil			
Oien, Joshua			
Nelms, Bobby			
Rider, Matthew			
Wunschel, Scott	LIFE STAR		
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Williams, Angelo	Martin, JR	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Parsons and Zimmer personnel worked at the 4825 and federal property sites preparing for forecasted high winds. Winds are forecasted to be in excess of 65 MPH. Site personnel performed end of week clean up and maintenance.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

74

59

3-1-18

0630 SAFETY BRIEF

0737 RADIO CHECKS

1500 TWO WEEK LOOK AHEAD.

1700 SECURED.

[Handwritten signature]

Pg

60

3-5-18

0630

SAFETY BRIEF

0736

RADIO CHECKS.

1015

BRYON BARNER & DAN NORRIS
ON SITE W/ INTERNS.

1130

BRYON BARNER & DAN NORRIS
W/ INTERNS OFF SITE.

1700

SECURED

A large handwritten signature, possibly 'J. J.', is written across the page, crossing over the 'SECURED' entry and extending diagonally across the lower half of the page.

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 06 March 2018

Site Location: 4825 Glenbrook Road

Weather:

Cold Low 30° High 46°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matthew			
Rockwell, Margaret			
	LIFE STAR		
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Williams, Angelo	Martin, JR	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Parsons and Zimmer personnel set up pumps and tested for Baker tank emptying (cancelled). Crews moved Sani-johns for easier site use and resecured them. Parsons personnel replaced bottom section of rope lights.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

61 3-6-18

0630 SAFETY BRIEF.

0710 RADIO CHECKS.

1700 SECURED

DR
SK

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 07 March 2018

Site Location: 4825 Glenbrook Road

Weather:

Cold Low 31° High 43°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matthew			
Rockwell, Margaret			
	LIFE STAR		
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Williams, Angelo	Martin, JR	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Parsons personnel removed excess geo cloth and hydraulic hammer from downrange. Crews cleaned out winter type equipment from under work trailers.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

P

62 3-7-18

1030 SAFETY BRIEF

0723 RADIO CHECKS

1700 SECURED

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 08 March 2018

Site Location: 4825 Glenbrook Road

Weather:

Cold Low 33° High 45°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matthew			
	LIFE STAR		
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Williams, Angelo	Martin, JR	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site personnel will perform end of week clean up and maintenance. Parsons and Zimmer crews will continue Wind Storm clean up at federal property site. Parsons personnel will replace silt fence at 4825 property.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

63

3-8-18

0630 SAFETY BRIEF.

0730 RADIO CHECKS

1100 CONFERENCE CALL.

1500 TWO WEEK WEEK LOOK AHEAD.

1700 SECURED.

[Handwritten signature]

Pg

64 3-12-18

0630 SAFETY BRIEF, KEN SHOTT ON SITE.

0751 RADIO CHECKS.

0800 THE TEAM IS WORKING AT PED
SITE.

1700 SECURED

A large, stylized handwritten signature, possibly reading 'R. Smith', is written across the page. A diagonal line is drawn from the top left of the signature area down towards the bottom right of the page.

P,

65 3-13-18

0630 SAFETY BRIEF.

0737 RADIO CHECKS.

0800 THE TEAM IS WORKING AT FED SIDE
TRAINING ECBC PEOPLE, BRING
MACHINE & GEO PROBE.

1609 BRAD A BARBER & DAN NORDIS,
ON SITE.

1700 SECURED

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 14 March 2018

Site Location: 4825 Glenbrook Road

Weather:

Cold Low 30° High 44°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matthew			
Rockwell, Margaret	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Williams, Angelo	Martin, JR	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Berkel delivered equipment in preparation for pre-cast concrete installation. Parsons and Zimmer assisted Berkel in prepping the soldier pile beams. Parsons crew completed silt fence replacement at federal property site.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

66

3-14-18

0630

SAFETY BRIEF.

0700

RADIO CHECKS.

0750

REKIG CONSTRUCTION ON SITE.

0910

REKIG PREPARE SOLDIER PICS


HW-1000 PERMIT ISSUED.

1045

REKIG CONSTRUCTION OFF SITE.

1700

SECURED



SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 15 March 2018

Site Location: 4825 Glenbrook Road

Weather:

Cold Low 32° High 53°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matthew			
	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Williams, Angelo	Martin, JR	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site personnel will perform end of week clean up and maintenance. Berkel will be on-site –delivering pre-cast concrete and beginning installation.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel (2)
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

67

3-15-18

0630 SAFETY BRIEF

0650 RADIO CHECKS

0700 BARBER CONSTRUCTION ON SITE & BRIEFED

1100 CONFERENCE CALL

1120 BRONX BARBER w/ CMA ON SITE

1220 CMA OFF SITE

1500 TWO WEEK LOOK AHEAD

1700 SECURED

Bob
SLD

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 19 March 2018

Site Location: 4825 Glenbrook Road

Weather:

Cold Low 35° High 54°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matthew			
	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Williams, Angelo	Martin, JR	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Parsons and Zimmer personnel continued working with Berkel personnel preparing the soldier piles for concrete installation, they welded the bottom supports onto the soldier piles. The pre-cast concrete delivery was cancelled due to truck issues.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel (4)
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCs)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

74

68

3.19.18

1630

SAFETY BRIEF.

0700

RADIO CHECKS. BERRER CONSTRUCTION
ON SITE

0800

STARTING HOT WORK IN H. DICES.

1300

BERRER CONSTRUCTION OFF SITE

1700

SECURED

R. J. S.

Pg

69

3-20-18

0636

SAFETY BRIEF.

0740

RADIO CHECKS, TRAFFIC SIGNS
IN PLACE, BORREL CONSTRUCTION
ON SITE.

0740

THE CONCRETE ON SITE.

0950


CONCRETE DOWNLOAD COMPLETE.

1210

FOR LIFT BUCKET 6021 VERT.

1230

SECURED SITE DUE TO WEATHER.

A large handwritten signature, possibly "R. G. J.", is written across the lower half of the page. The signature is written in a cursive, stylized font and is positioned diagonally across the page.

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 22 March 2018

Site Location: 4825 Glenbrook Road

Weather:

Cold Low 30° High 43°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matthew			
Rockwell, Margaret	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Williams, Angelo	Martin, JR	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 8:30

There was a two hour delay starting work due to weather. Parsons and Zimmer personnel will assisted Berkel Company with staging of pre-cast concrete panels. Site personnel performed end of week maintenance.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel (4)
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

70 3-22-18

0830 SAFETY BRIEF. THE SITE WAS
CLOSED 3-21-18 DUE TO SNOW.

1750 RADIO CHECKS. THE TEAMS ARE
REMOVING SNOW FROM THE
WALKWAYS AND WORK AREAS.

1800 SECURED

~~RE
SR~~

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 26 March 2018

Site Location: 4825 Glenbrook Road

Weather:

Cold Low 33° High 51°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matthew			
Rockwell, Margaret	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Williams, Angelo	Martin, JR	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Parsons and Zimmer personnel worked with Berkel personnel installing the precast concrete panels between the soldier piles. Site personnel also worked at the federal property site with Veolia to empty the 24-thousand-gallon water tank. Four tanker trucks were filled and sent for disposal. Personnel began cleaning the tank.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel (4)
DAVEY ()
ACCUPERMIT (2)
ACL (0)
CPJ (0)

Problems encountered/resolutions:**Instructions given by government personnel:****Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

71

3-26-18

0630 SAFETY BRIEF

0700 RADIO CHECKS.

0800 PERMIT CONSTRUCTION IN SITE
INSTALLING CONCRETE LAGGING.
THE TEAM IS PUMPING WATER AT
FEDERAL PROPERTY.

1700 SECURED.

[Handwritten signature]

Pg

72

3-27-18

0630 SAFETY BRIEF

0700 RADIO CHECKS.

0800 BURKE CONSTRUCTION WORKING

TO INSTALL CONCRETE LAGGING.

0820 SEAN BUCKLEY ON SITE. THE

TANK IS PRESSURE WASHLING

BURKE TANK

1700 SECURED

A handwritten signature in black ink, appearing to be 'R. S.', is written across the page. A long diagonal line is drawn from the bottom left towards the top right, passing through the signature.

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 28 March 2018

Site Location: 4825 Glenbrook Road

Weather:

Mild Low 52° High 61°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matthew			
	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Williams, Angelo	Martin, JR	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Parsons and Zimmer personnel completed installing the precast concrete panels between the soldier piles.
Site personnel also completed cleaning the baker tank.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found: None

New Equipment on Site: N/A

Visitors

Contractors

Berkel (4)
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

R

73 3-28-18

0630 SAFETY BRIEF

0700 RADIO CHECKS.

0800 BECKET CONSTRUCTION WORKING
TO INSTALL CONCRETE LAGGING
THE TEAM IS PRESSURE WASHING
BAKER TANK.

1700 SECURED

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 29 March 2018

Site Location: 4825 Glenbrook Road

Weather:

Mild Low 49° High 77°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rockwell, Margaret	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Williams, Angelo	Martin, JR	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Parsons and Zimmer personnel assisted Berkel Company with cleaning and demobilization of equipment. Site personnel performed end of week maintenance.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel (4)
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

R

74 3-29-18

0630 SAFETY BRIEF.

0700 RADIO CHECKS

0757 TRAFFIC SIGNS IN PLACE

0803 BARRIC CONSTRUCTION IN SITE
FOR EQUIPMENT PICKUP.

1000 BARRIC CONSTRUCTION OFF SITE.

1100 WEEKLY CONFERENCE CALL.

1118 CONFERENCE CALL COMPLETE.

1500 TWO WEEK LOOK AHEAD

1700 SECURED



P₂

76

43-18

0630

SAFETY BRIEF.

0700

RADIO CHECKS.

0830

ACI ON SITE TO REPLACE TEMPORARY
WATER LINE.

1345

TEMPORARY WATER LINE INSTALLATION
COMPLETE ACI OFF SITE.

THE TEAM IS MOVING DIRT
TO PROVIDE ACCESS TO THE ARSENIC
GRIDS.

1700

SECURED.

[Handwritten signature]

P₇

77 44-18

0630 SAFETY BRIEF.

0700 RADIO CHECKS

0800 THE TEAM IS MOVING DIRT

1700 SECURED

[Handwritten signature]

R₂

78 45-18

0630 SAFETY BRIEF

0700 RADIO CHECKS.

0800 TRAFFIC SIGNS IN PLACE.

THE TEAM IS MOVING DIRT IN
PREP FOR ARSENIC GRIDS.

1100 CONFERENCE CALL.

1430 SEAN PUCKLEY ON SITE.

1700 SECURED

[Handwritten signature]
[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 09 April 2018

Site Location: 4825 Glenbrook Road

Weather:

Mild Low 38° High 53°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Williams, Angelo	Martin, JR	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Parsons and Zimmer personnel continued training on the arsenic removal SOP. The team set up and performed dry runs of EPDS operations.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

79 4-9-18

0630 SAFETY BRIEF

0700 RADIO CHECKS

0900 THE TEAM IS WORKING AT
FEDERAL PROPERTY.

1700 SECURED

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 10 April 2018

Site Location: 4825 Glenbrook Road

Weather:

Mild Low 42° High 55°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Buhl, Jay	Martin, JR	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site personnel worked with the surveyor laying in the grids for arsenic removal. Additionally current elevations for each point were collected and recorded. Personnel trained on the set up and use of dust and arsenic monitors, monitors were checked for components and calibration.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

80

4-10-18

0630 SAFETY BRIEF

0700 RADIO CHECKS

0740 CPJ ON SITE TO SURVEY ARSENIC GRIDS.

1700 SECURED

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 11 April 2018

Site Location: 4825 Glenbrook Road

Weather:

Mild Low 41° High 58°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Buhl, Jay	Martin, JR	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Parsons and Zimmer personnel inspected drums in the storage area for identification markings as these can become degraded over time due to the sun. They also inspected for any other signs of damage. Personnel performed M-40 mask fit testing.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

81

4-11-18

0630 SAFETY BRIEF TODD STEELMAN
ON SITE FOR CONRAD.

0700 RADIO CHECKS. POSTING

0800 THE TEAM IS PROPPING FOR
DIGGING IN THE ARSONIC GRIDS.

1700 SECURED.

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 12 April 2018

Site Location: 4825 Glenbrook Road

Weather:

Mild Low 53° High 74°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Buhl, Jay		
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site personnel walked the fence line of the federal property checking for downed trees and the security buffer for the fence. Bushes and overhanging branches were noted for removal by the Parsons lawn maintenance contractor. Site personnel performed end of week maintenance.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

82

4-12-18

0630

SAFETY BRIEF.

0700

RADIO CHECKS.

0810

THE TEAM IS PROCEEDING
FOR ARSENIC GRID DIGS.

1100

CONFERENCE CALL.

1500

TWO WEEK LOOK AHEAD.

1700

SECURED

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 16 April 2018

Site Location: 4825 Glenbrook Road

Weather:

Mild Low 45° High 56°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil			
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
Rockwell, Margaret	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Owing, Angel		
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Between rainstorms parsons and Zimmer personnel brought over and set up equipment and supplies for the arsenic removal operation. The roll off box was not brought to the site due to DC holiday traffic restrictions.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

R₇

83 4-16-18

0630 SAFETY BRIEF.

0700 RADIO CHECKS

1230 THE TEAM IS WORKING TO
REMOVE OVERBURDEN FROM
GRID 50-10

1700 SECURED

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 17 April 2018

Site Location: 4825 Glenbrook Road

Weather:

Mild Low 40° High 50°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil			
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
Rockwell, Margaret	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
		Shott, Ken	
	Schmidt, James	CENAB	
	Owing, Angel		
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site personnel began arsenic soil removal from grid 50/-10. Three roll off boxes were filled with soil and associated samples were collected. Full roll off boxes are stored at the federal property site.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

[illegible]

P₂

84

4-17-18

0630 SAFETY BRIEF

0700 RADIO CHECKS. EYEWASH STATION CHANGED.

0920 ROLLOFF RB36776RT ON SITE.

1010 STARTING TO EXCAVATE ARSENIC GRID
50,-10.1035 DUST MONITOR READING 2.70g/m³1110 DUST MONITOR READING 3.80g/m³ROLLOFF RB36776RT FULL AND
COMPOSITE COLLECTED

1230 ROLLOFF RB36776RT OFF SITE.

1249 DUST MONITOR READING 3.10g/m³

1301 ROLLOFF 280155 ON SITE

1326 DUST MONITOR READING 2.30g/m³1355 DUST MONITOR READING 2.10g/m³1359 ROLLOFF 280155 IS FULL. NOTE: @ 13:13
VOC WAS COLLECTED.

1422 ROLLOFF 280155 OFF SITE.

1429 DUST MONITOR READING 2.30g/m³

1458 ROLLOFF 279892 ON SITE.

1505 DUST MONITOR READING 3.40g/m³

1513 VOC COLLECTED.

1537 DUST MONITOR READING 3.30g/m³

1559 ROLLOFF 279892 IS FULL

1700 SECURED



SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 18 April 2018

Site Location: 4825 Glenbrook Road

Weather:

Mild Low 38° High 62°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil			
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
Rockwell, Margaret	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
		Shott, Ken	
	Schmidt, James	CENAB	
	Owing, Angel		
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Parsons and Zimmer personnel continued arsenic soil removal from grid 50/-10. Three roll off boxes were filled with soil and associated samples were collected. Full roll off boxes are stored at the federal property site.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCs)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

[illegible]

Pa

85 418.18

0630 SAFETY BRIEF

0728 RADIO CHECKS TRAFFIC SIGNS
IN PLACE

0719 MX MINUTERS ARE UP & RUNNING

0828 ROLL OFF 279892 IS OFF SITE.

0846 DUST MONITOR READING 6.8 ug/m³

SEAN BUCKLEY ON SITE. ECR

LOCKED/TAGGED OUT ELECTRICAL PANELO
TO DISCONNECT THE PDS POWER.

0857 ROLL OFF 280191 ON SITE.

0911 DUST MONITOR READING 6.2 ug/m³

0913 VOC COLLECTED

0943 DUST MONITOR READING 7.3 ug/m³1024 DUST MONITOR READING 8.9 ug/m³

1030 ROLL OFF 280191 OFF SITE.

1100 ROLL OFF 279655 ON SITE

DUST MONITOR READING 8.4 ug/m³1201 DUST MONITOR READING 8.3 ug/m³

VOC COLLECTED.

1230 DUST MONITOR READING 8.2 ug/m³

1240 ROLL OFF 279655 IS FULL.

1300 DUST MONITOR READING 7.7 ug/m³

1318 ROLL OFF 279655 OFF SITE

1346 FUEL TRK ON SITE.

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 23 April 2018

Site Location: 4825 Glenbrook Road

Weather:

Mild Low 49° High 57°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
Rockwell, Margaret	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Buhl, Jay		
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site personnel completed arsenic soil excavation of grid 50/-10. Confirmation samples were collected and shipped to the appropriate lab for analyses. Site personnel moved construction matting and prepared grid 50/-30 for excavation.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found: None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCs)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

[illegible]

Pg

88

4-23-18

0630 SAFETY BRIEF.

0730 RADIO CHECKS TRAFFIC SIGNS IN PLACE.


0850 VOC COLLECTED FILLING ROLL OFF 274308

0937 ROLL OFF 274308 IS FULL.

0939 DUST MONITOR READING 8.3 ug/m³1200 COLLECTING SOIL SAMPLES FROM
GRID 50-10

1230 SAMPLING IN GRID 50-10 COMPLETE

1700 SECURED

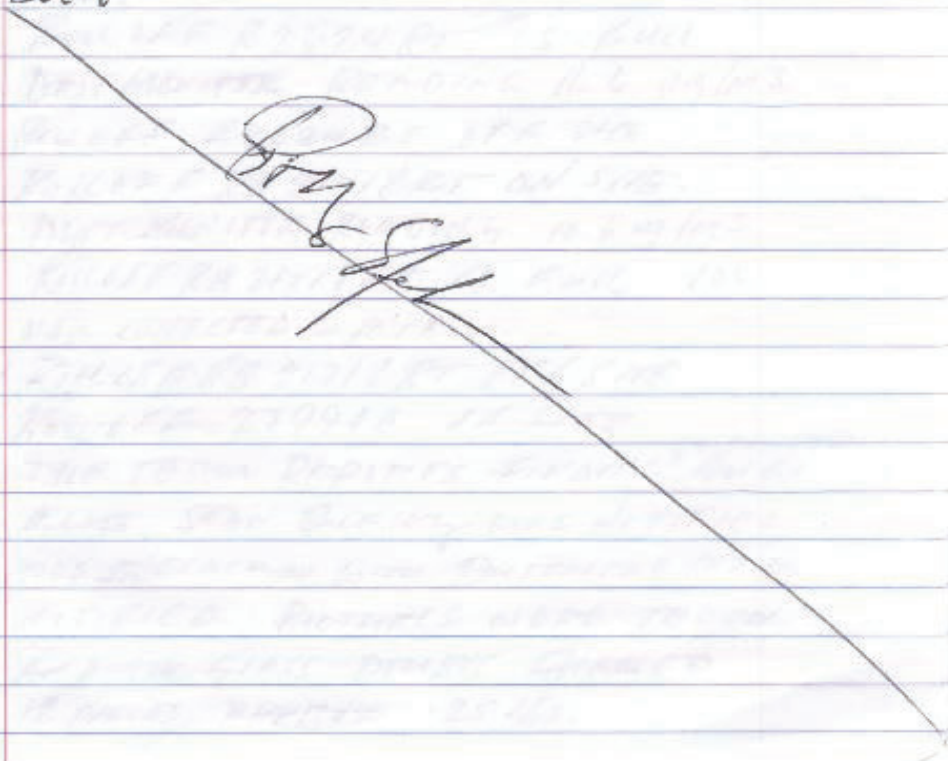

DTZ
SK

[illegible]

R₉

89 4-24-18

0630 SAFETY BRIEF.

0700 RADIO CHECKS

0800 DIEGING IN ARSENIC GRID 50-30
 ARSENIC MONITOR READS 10.1 UG/M³
 JOSH DIBON HAS THE TECH PERSONNEL
 ARSENIC MONITOR AND ED MANGOSCH
 THE OPERATOR MONITOR.

0828 VOC COLLECTED. FILLING ROLLOFF
 R2624 RT.

0918 ROLLOFF R2624 RT. IS FULL.
 DUST MONITOR READING 11.6 UG/M³

0930 ROLLOFF R2624 RT OFF SITE.

0955 ROLLOFF RB 21718 RT ON SITE.

1014 DUST MONITOR READING 10.6 UG/M³

1048 ROLLOFF RB 21718 RT IS FULL. VOC
 WAS COLLECTED @ 10:18

1104 ROLLOFF RB 21718 RT OFF SITE.

1128 ROLLOFF 279900 ON SITE.

1235 THE TEAM REPORTS FINDING ^{SUSPECTED} GLASS. SEAN BUCKLEY WAS NOTIFIED,
 TODD STEELMAN WITH BATTIMIRE CORP.
 NOTIFIED. PICTURES WERE TAKEN
 AND THE GLASS DOUBLE BAGGED.
 12 PICTOS APPROX. 125 LBS.

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 25 April 2018

Site Location: 4825 Glenbrook Road

Weather:

Mild Low 52° High 65°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
Rockwell, Margaret	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Williams, Angelo		
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Parsons and Zimmer personnel continued arsenic soil removal from grid 50/-30. Three roll off boxes were filled with soil and associated samples were collected. Full roll off boxes are stored at the federal property site.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:**Instructions given by government personnel:****Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

[illegible]

Pg

91

4-25-18

Light rain

0630 SAFETY BRIEF.

0728 RADIO CHECKS.

0800 TRAFFIC SIGNS IN PLACE.

0822 DIGGING IN GRID 50-30 VOC COLLECTED.

FILLING ROLLOFF 279900 DUST
MONITOR READING 12.8 ug/m³

0905 ROLLOFF 279900 IS FULL

0915 ROLLOFF 279900 OFF SITE.

0950 ROLLOFF R 2649RT ON SITE

0959 VOC COLLECTED 15.15

1036 DUST MONITOR 13.1 ug/m³

1100 ROLLOFF R2649RT IS FULL

1112 ROLLOFF R2649RT OFF SITE.

1136 ROLLOFF R25084RT ON SITE.

1320 DUST MONITOR READING 40 ug/m³

VOC COLLECTED.

1410 ROLLOFF R25084RT IS FULL.

1424 ROLLOFF R25084RT OFF SITE.

1449 ROLLOFF 279888 ON SITE

1454 VOC COLLECTED. DUST MONITOR
READING 2.0 ug/m³.

1530 ROLLOFF 279888 IS FULL.

1541 ROLLOFF 279888 OFF SITE.

1700 SECURED



SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 26 April 2018

Site Location: 4825 Glenbrook Road

Weather:

Mild Low 53° High 69°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
Rockwell, Margaret	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Williams, Angelo		
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site personnel completed arsenic soil excavation of grid 50/-30. Confirmation samples were collected and shipped to the appropriate lab for analyses. Site personnel performed end of week clean up and maintenance.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:**Instructions given by government personnel:****Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

[illegible]

R

9Z 4-26-18

0630 SAFETY BRIEF

0725 RADIO CHECKS

0800 TRAFFIC SIGNS IN PLACE.

0813 ROLL OFF 279982 ON SITE

DUST MONITOR READING 1.9 UG/M³

0828 VOC COLLECTED

0903 ROLL OFF 279982 IS FULL.

0920 ROLL OFF 279982 OFF SITE.

0950 ROLL OFF R25924RT ON SITE

DUST MONITOR READING 5.1 UG/M³

0954 VOC COLLECTED

1045 ROLL OFF R25924RT IS FULL

1100 CONFERENCE CALL

1222 ROLL OFF R25924RT OFF SITE

1230 STARTED SAMPLING FOR ARSENIC IN

GRID 501-30 @ 12:17 AND ALL SAMPLES
COLLECTED AT THIS TIME.

1700 SECURED



SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 30 April 2018

Site Location: 4825 Glenbrook Road

Weather:

Mild Low 40° High 71°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth			
Matter, Phil	Prate, Warren		
	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
Rockwell, Margaret	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Williams, Angelo		
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site personnel made preparations for excavation of Grid 30, -30, they relocated construction mats, moved EPDS, and restocked PPE supplies.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

[illegible]

169

93 4-30-18

0630 SAFETY BRIEF.

0700 RADIO CHECKS.

0800 THE TEAM IS PREP'ING
FOR THE NEXT ARSENIC GRID
DIGS.

1700 SECURED.

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 01 May 2018

Site Location: 4825 Glenbrook Road

Weather:

Warm Low 52° High 78°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
Rockwell, Margaret	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Williams, Angelo		
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site personnel began arsenic soil removal from grid 30/-30. Two roll off boxes were filled with soil and associated samples were collected. Full roll off boxes are stored at the federal property site. Site personnel moved the north end of the privacy fence that surrounds the site trailer. The fence was moved to accommodate AU projects.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:**Instructions given by government personnel:****Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

[illegible]

Pg

94

5-1-18

0630 SAFETY BRIEF.

0700 RADIO CHECKS

0710 INSPECTED FIRE EXTINGUISHERS
AND EYE WASH.

0824 ROLLOFF R021127RT ON SITE

0850 DUST MONITOR READING 24.4 ug/m³
SPAN BUCKLEY ON SITE.0900 VOC COLLECTED FILLING ROLLOFF
R021127RT, DRUMS IN GRIP-30-130.

0935 ROLLOFF R021127RT FULL

0952 ROLLOFF R021127RT OFF SITE.

1017 ROLLOFF 278356 ON SITE.

1033 VOC COLLECTED.

1120 ROLLOFF 278356 IS FULL.

1124 ROLLOFF 278356 OFF SITE.

1250 ROLLOFF 279887 ON SITE.

1700 SECURED

A large, stylized handwritten signature in black ink, written over the bottom portion of the log. The signature appears to be 'Ry' followed by a large, sweeping flourish.

[illegible]

Pg

95 5-2-18

0630 SAFETY BRIEF

0700 RADIO CHECKS

0800 TRAFFIC SIGNS IN PLACE

0807 VOC COLLECTED, FILLING ROLL OFF
279887 FROM GRID -30/-300828 DUST MONITOR READING 11.7 UG/M³

0852 ROLL OFF 279887 IS FULL

0906 ROLL OFF 279887 OFF SITE

0942 ROLL OFF 274314 ON SITE

0951 VOC COLLECTED

0953 DUST MONITOR READING 46.8 UG/M³

1053 ROLL OFF 274314 IS FULL

1105 ROLL OFF 274314 OFF SITE

1145 ROLL OFF R25738RT ON SITE

1240 VOC COLLECTED. DUST MONITOR
READING 16.7 UG/M³

1312 ROLL OFF R25738RT IS FULL

1330 ROLL OFF R25738RT OFF SITE

1404 ROLL OFF 274582 ON SITE

1412 VOC COLLECTED, FILLING ROLL OFF
274582

1437 ROLL OFF 274582 IS FULL

1700 SECURED



[illegible]

R

95 5-3-18

0630 SAFETY BRIEF

0729 RADIO CHECKS

0819 Rolloff 274502 OFF SITE.

0849 Rolloff RB37384RT ON SITE.

0900 VOC COLLECTED, FILLING Rolloff

0937 Rolloff RB37384RT IS FULL.

0956 Rolloff RB37384RT OFF SITE.

1027 Rolloff RB21724RT ON SITE.

1032 DUST MONITOR READING 22.3 UG/M3

1057 VOC COLLECTED. FILLING Rolloff

1120 Rolloff RB21724RT IS FULL.

1133 Rolloff RB21724RT OFF SITE.

1155 Rolloff 280192 ON SITE

1243 DUST MONITOR READING 11.4 UG/M3

1249 VOC COLLECTED. FULL Rolloff 280192.

1321 Rolloff 280192 IS FULL

1333 Rolloff 280192 OFF SITE.

1352 Rolloff RB36774RT ON SITE.

1402 VOC COLLECTED FILLING Rolloff

DUST MONITOR READING 32.4 UG/M3

1437 Rolloff RB36774RT IS FULL.

1439 TWO WEEK LOOK AHEAD.

1502 Rolloff RB36774RT OFF SITE

1700 SQUADS



[illegible]

Pg

96

5-7-18

0630 SAFETY BRIEF.

0740 RADIO CHECKS

0745 SEAN BUCKLEY ON SITE.

0800 TRAFFIC SIGNS IN PLACE.

0839 Rolloff R25692 RT ON SITE

0846 DUST MONITOR READING 13.9 $\mu\text{g}/\text{m}^3$

0849 VOC COLLECTED.

0928 Rolloff R25692 RT IS FULL.

0945 Rolloff R25692 RT OFF SITE.

1015 Rolloff 279968 ON SITE.

1034 VOC COLLECTED

DUST MONITOR READING 9.4 $\mu\text{g}/\text{m}^3$.

1111 Rolloff 279968 IS FULL.

1126 Rolloff 279968 OFF SITE.

1150 ROLLER COMPACTOR ON SITE

1200 Rolloff 274806 ON SITE.

1300 VOC COLLECTED. DUST MONITOR
READING 12.6 $\mu\text{g}/\text{m}^3$

1339 Rolloff 274806 IS FULL

1349 Rolloff 274806 OFF SITE.

1414 STARTING CONFIRMATION SAMPLING
ON SOUTH WALL OF GRID -301-30.1424 COMPLETED CONFIRMATION SAMPLING
ON THE WEST WALL. GRID -301-30

[illegible]

Pg

98

5-8-18

0630 SAFETY BRIEF.

0700 RADIO CHECKS. TRAFFIC SIGNS IN PLACE.

0813 DUST MONITOR READING 10.309/M3.

0821 ROLL OFF 274345 ON SITE.

0830 OVER EXCAVATING GRID 501-10.

BOTTOM ONLY FOR ARSENIC. "FLOOR"

0833 VOC COLLECTED

0904 ROLL OFF 274345 IS FULL.

0915 ROLLOFF 274345 OFF SITE

0944 ROLLOFF R25359 RT ON SITE.

0953 VOC COLLECTED. CONTINUE TO

OVER EXCAVATE GRID 501-10 FOR ARSENIC.


"Bottom only" "FLOOR"

1035 ROLL OFF R25359 RT IS FULL.

1309 GRID 501-10 FLOOR SAMPLE COLLECTED.

D 8'6"

1700 SECURED



2

99

5-9-18

0630 SAFETY BRIEF

0650 RADIO CHECKS. THE TEAM WILL

BE WORKING AT FEDERAL PROPERTY.

1240 THE TEAM CONTINUES TO

DUMP ROLL OFFS.

1710 SECURED

[Handwritten signature]

R

100

5-10-18

0630

SAFETY BRIEF.

0725

RADIO CHECKS. THE TOWN

IS WORKING @ FEDERAL PROPERTY
DUMPING/LINING ROLL OFFS.

1100

WEEKLY CONFERENCE CALL.

1700

SECURED

[Signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 14 May 2018

Site Location: 4825 Glenbrook Road

Weather:

Hot Low 61° High 85°

Personnel on Site

PARSONS	ZES	ECBC	
Matter, Phil	Mangosh, Ed		
Oien, Joshua	Prate, Warren		
Nelms, Bobby	Yorkshire, Bart		
Rider, Matt			
	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Buhl, Jay	Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site personnel worked at the federal property site loading cleared soil for shipment to the sub-title D landfill. Personnel also placed new liners in several roll off boxes. In the afternoon the site team worked at the 4825 Glenbrook site moving construction mats and prepping the area to begin excavation of grid 10/-10.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:**Instructions given by government personnel:****Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

R

1 5-14-18

0630 SAFETY BRIEF.

0700 RADIO CHECKS.

0800 THE TEAM ARE WORKING AT REDOTAC
LOADING BUMP TRUCKS, SOIL FOR
LAND FILL.

1330 THE TEAM IS WORKING PREPARING
FOR ARSENIC GRIDS!

1700 SECURED

By
SK

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 15 May 2018

Site Location: 4825 Glenbrook Road

Weather:

Hot Low 66° High 91°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
Rockwell, Margaret	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Buhl, Jay	Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site personnel continued working at the federal property site loading cleared soil for shipment to the subtitle D landfill, two trucks were sent out. Personnel also dumped 7 roll off boxes for later shipment and placed new liners in 10 empty roll off boxes.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:**Instructions given by government personnel:****Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

2

5-15-18

0630

SAFETY BRIEF

1700

PHOTO CHECKS SAFETY/SECURITY
WALK FOR 482548.

0800

THE TEAM IS WORKING AT FEDERAL
PROPERTY.

1700

SECURED

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 16 May 2018

Site Location: 4825 Glenbrook Road

Weather:

Hot Low 70° High 78°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
Rockwell, Margaret	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Artoaga, Carlols	Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Parsons and Zimmer personnel worked at the 4825 Glenbrook site, approximately 800 gallons of water was pumped from grid 50/-10. After water was removed personnel began excavation of an additional one foot from the floor of the grid and collected a confirmation sample.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

3

5-16-18

0630 SAFETY BRIEF.

1657 RADIO CHECKS.

0751 TRAFFIC SIGNS IN PLACE.

0800 PUMPING WATER FROM GRID

50/-10 APPROX: 800 GALLONS.

1016 Rolloff 280191 ON SITE.

1019 VOC COLLECTED. FILLING ROLL OFF
280191 W/soil FROM GRID 50/-10.

1110 ROLL OFF 280191 IS FULL AND OFF SITE.


1135 ROLL OFF 274169 ON SITE.

1242 VOC COLLECTED. FILLING ROLL OFF 274169
W/soil FROM GRID 50/-10.

1331 ROLL OFF 274169 IS FULL & OFF SITE.

1349 GRID CONFIRMATION FLOOR SAMPLE @
10'4" 50/-10.1437 PUMPING WATER FROM GRID 30/-30
APPROX 400 GALS.

1700 SECURED

A handwritten signature in dark ink, appearing to be "D. J. Smith", is written across the lower half of the page. A diagonal line is drawn from the bottom left corner of the page, passing under the signature and extending towards the bottom right.

[illegible]

Pg
4

5-17-18

0630 SAFETY BRIEF

0800 RADIO CHECKS TRAFFIC SIGNS IN PLACE.

0850 SOAK BACKLOG ON SITE. PUMPED

WATER FROM GRID 30/30 APPROX 250 GALS.

1100 CONFERENCE CALL

1300 SECURED

[Handwritten signature]

R₇

5 5-21-18

0630 SAFETY BRIEF

0748 RADIO CHECKS.

1124 COMPLETED 5 LOADS OF WATER
PUMPING APPROX 850 GPM CA.

1546 COMPLETED 3 LOADS OF WATER
PUMPING APPROX 850 GPM CA.

1700 SECURED

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 22 May 2018

Site Location: 4825 Glenbrook Road

Weather:

Warm, with chance of rain Low 65° High 80°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
Rockwell, Margaret	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Buhl, Jay	Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site personnel participated in a Parsons internal Safety and health audit conducted by Greg Ertel. Parsons and Zimmer personnel continued working at the 4825 Glenbrook site pumping water from the excavations of grids 50/-10 and 30/-30. Four loads of water for a total of 3,050 gallons was pumped and transferred to the federal property site for storage. Parsons PM / geologist inspected grids 50/-10 and 30/-30 to ascertain if bedrock had been reached.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Jenny Prince (Parsons)

Greg Ertel (Parsons)

Contractors

Berkel ()

DAVEY ()

ACCUPERMIT (2)

ACI (0)

CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

[illegible]

Pg
6

5-22-18

- 0630 SAFETY BRIEF, GREG ERTTEL AND
0 JENNY PRINCE ON SITE FOR AUDIT
0740 RADIO CHECKS.
0800 TRAFFIC SIGNS IN PLACE.
1131 COMPLETED PUMPING WATER FROM
GRIDS 50/10 + 50/30 APPROX 3050 GALS.
1311 VOC COLLECTED STARTED FILLING
Rou OFF 279693 W/STIL.
1331 Rou OFF 279693 FULL.
1340 Rou OFF 279693 OFF SITE
1400 Rou OFF 280155 ON SITE.
1406 VOC COLLECTED FILLING Rou OFF 280155
1445 Rou OFF 280155 OFF SITE
1800 Jenny Prince and Greg Erttel completed
audit.
1700 SECURED

By 

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 23 May 2018

Site Location: 4825 Glenbrook Road

Weather:

Warm, Low 67° High 80°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
Rockwell, Margaret	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Buhl, Jay	Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Parsons and Zimmer personnel again worked at the 4825 Glenbrook site pumping water from the excavations of grids 50/-10 and 30/-30. Seven loads of water for a total of 5,500 gallons was pumped and transferred to the federal property site for storage. After pumping water the team excavated an additional foot of soil from the bottom, south wall and west wall of grid 30/-30. Three loads of cleared soil were sent to the subtitle-D landfill from the federal property site.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors


Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Daily Contractor Quality Control Report					
Contract Number:	W912DY-09-D-0062				
Delivery Order Number:	0006				
Project Name:	4825 Glenbrook Rd. Remedial Action, Spring Valley FUDS.				
Project Number:	748272.03000				
Site Location:	Spring Valley, Washington, DC.				
Date:	5/23/2018				
Weather:	Partly Cloudy 61-80°F, wind 0-15mph				
Field Instrument:	GilAir3 (1), Thermo Scientific HDR Dust Monitor				
Measurements:	All Non Detect.				
Calibrations:	GilAir3				
Summary:	Crews pumped 5,500 gal of water from grids 50, -10 and 30, -30. Crews over-excavated soil from Grid 30, -30 in preparation for metals confirmation sampling. Collected 1 composite and 1 VOC sample. Collector perimeter dust sample.				
Items Found:	None				
Contingency Plan Initiated:	No				
Air Monitoring:	Air Chek, Thermo Scientific HDR				
IDW Generated:	PPE and Decon Water				
Waste Disposal:	None				
Departures from approved SSWP:	None				
Problems encountered/resolutions:	None				
Instructions given by government personnel:	None				
Attachments:	Sample Logs Daily QC Logs UXO Safety Log (Weekly) COC				
Signed by:					
Name (print):	Margaret Rockwell				
Date:	5/23/2018				
Phone Number:	571-721-9804				
Copy sent to:	Scott Wunschel				

R

7 5-23-18

0630 SAFETY BRIEF

0750 RADIO CHECKS TRAFFIC SIGNS
IN PLACE.0800 PUMPING WATER FROM GRIDS
50/10 AND 30/30.1410 COMPLETED DUMPING WATER APPROX
5500 GALS FROM GRIDS 50/10 & 30/301422 VIC COLLECTED ROLL OFF 274544
POND FILLER W/ SOIL FROM GRID
30/30.

1451 COMPOSITE COLLECTED. ROLL OFF 274544 FUEL.

1700 SECURED



SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 24 May 2018

Site Location: 4825 Glenbrook Road

Weather:

Warm, Low 63° High 83°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
Rockwell, Margaret	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Buhl, Jay	Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site personnel collected the associated confirmation samples for the bottom of grid 30/-30, the north wall of 30/-10 and the east wall of 10/-30. After sampling the team dumped cleared roll off boxes at the federal property site. Site personnel performed end of week clean up and maintenance.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:**Instructions given by government personnel:****Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

[illegible]

Pg 8

5-24-18

0630 SAFETY BRIEF

0750 RADIO CHECKS TRAFFIC SIGNS IN PLACE.

0811 ROLL OFF 274544 OFF SITE.

0821 PUMPING WATER FROM GRID 30/30.

0916 TAKING CONFIRMATION SAMPLES FROM
GRID 30/30.

1100 WEATHER ADVISORY CALL.

1700 STOPPED


J. S. L.

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 29 May 2018

Site Location: 4825 Glenbrook Road

Weather:

Warm, possible rain Low 68° High 83°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
Rockwell, Margaret	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Buhl, Jay		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Parsons and Zimmer personnel continued working at the 4825 Glenbrook site pumping water from the excavations of grids 50/-10 and 30/-30. Six loads of water for a total of 4,550 gallons was pumped and transferred to the federal property site for storage. Three roll off boxes of cleared soil was dumped and the boxes lined with new roll off liners.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

7/9

5-29-18

0630 SAFETY BRIEF.

0750 RADIO CHECKS.

0752 TRAFFIC SIGNS IN PLACE.

0800 PUMPING WATER FROM GRID 50/-10.

1347 APPROX. 4600 GALS WERE PUMPED
FROM GRID 50/-10.

1410 THE TEAM IS WORKING AT FEDERAL
PROPERTY DUMPING ROLLOPS.

1700 SECURED

[Signature]

#9

10 5-30-18

0630 SAFETY BRIEF

0755 RADIO CHECKS TRAFFIC SIGNS IN PLACE.
SEAN BUCKLEY ON SITE.

0800 PUMPING WATER FROM GRID 50/A.

1015 CENAB GEOLOGIST ON SITE INSPECTING
GRID 50/A

1023 LIGHTNING HOLD

1100 OFF LIGHTNING HOLD.

1237 THE TEAM IS WORKING AT FEDERAL
PROPERTY PUMPING RECOVER.

1700 SECURED



D. J. [unclear]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 31 May 2018

Site Location: 4825 Glenbrook Road

Weather:

Warm, possible thunder storms Low 71° High 85°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rockwell, Margaret	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Buhl, Jay		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site personnel collected water samples from the full baker tank at the federal property site. Water samples were picked up by ECBC for analyses. After sampling the team dumped cleared roll off boxes at the federal property site. Site personnel performed end of week clean up and maintenance.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

David King (CENAB)

Contractors

Berkel ()

DAVEY ()

ACCUPERMIT (2)

ACI (0)

CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg,

11 5-31-18

0630 SAFETY BRIEF

0800 RADIO CHECKS. THE TEAM IS

SAMPLING WATER AT FEDERAL PROPERTY.

1110 CONFERENCE CALL

1710 SECURED

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 04 June 2018

Site Location: 4825 Glenbrook Road

Weather:

Mild Low 55° High 79°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
Rockwell, Margaret	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Buhl, Jay	Whitten, Ricky	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Parsons and Zimmer personnel continued working at the 4825 Glenbrook site pumping water from the excavation of grid 30/-30. Seven loads of water for a total of 5,950 gallons was pumped and transferred to the federal property site for storage.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

David King (CENAB)

Contractors

Berkel ()

DAVEY ()

ACCUPERMIT (2)

ACI (0)

CPJ (0)

Problems encountered/resolutions:**Instructions given by government personnel:****Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	<i>To be included if investigation is using CSS protocols</i>
Dig Sheet	Y/N	<i>To be included at least once every week during intrusive investigation</i>
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	<i>To be included weekly during field activities</i>
Property Management Summary	Y/N	<i>Include complete property inventory once every month</i>
Photographs	Y/N	

Pg

12 6-4-18

0630 SAFETY BELT

0755 RADIO CHECKS TRAFFIC SIGNS IN FORCE.

0800 PUMPING WATER.

1710 SECURED

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 05 June 2018

Site Location: 4825 Glenbrook Road

Weather:

Mild Low 57° High 77°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
Rockwell, Margaret	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Buhl, Jay	Whitten, Ricky	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Parsons and Zimmer personnel continued working at the 4825 Glenbrook site pumping water from the excavations of grids 50/-10 and 30/-30. Seven loads of water for a total of 5,950 gallons was pumped and transferred to the federal property site for storage. An additional Baker tank was delivered and set up at the federal property site.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPI (0)

Problems encountered/resolutions:**Instructions given by government personnel:****Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

13 4-5-18

0630 SAFETY BRIEF

0750 RAPID CHECKS TRAFFIC SIGNS OP.

0800 PUMPING WATER.

1700 SECURED.

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 06 June 2018

Site Location: 4825 Glenbrook Road

Weather:

Mild Low 59° High 71°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
Rockwell, Margaret	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Buhl, Jay	Whitten, Ricky	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Parsons and Zimmer personnel continued working at the 4825 Glenbrook site pumping water from the excavations of grids 50/-10 and 30/-30. An additional Baker tank was delivered and set up at the federal property site. After the water was pumped from the excavations the team began backfilling grids 50/-10, 50/-30 and 30/-30 with clean fill from the federal property site.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:**Instructions given by government personnel:****Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

79

14 6-6-18

0630 SAFETY BRIEF

0750 RADIO CHECKS TRAFFIC SIGNS UP

0844 DUMPING STONE TO BACKFILL

GRID 30/30

1700 SECURED

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 07 June 2018

Site Location: 4825 Glenbrook Road

Weather:

Mild Low 59° High 78°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Buhl, Jay	Whitten, Ricky	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Parsons and Zimmer personnel continued working at the 4825 Glenbrook site backfilling grids 50/-10, 50/-30 and 30/-30 with clean fill from the federal property site. Site personnel performed end of week clean up and maintenance.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

15 6-7-18

0630 SAFETY BRIEF

0750 RADIO CHECKS TRAFFIC SIGNS UP

0815 JACK FILLING GRID 30/30

1100 CONFERENCE CALL

1700 SECURED

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 11 June 2018

Site Location: 4825 Glenbrook Road

Weather:

Mild, possible rain Low 57° High 61°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Buhl, Jay	Whitten, Ricky	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Parsons and Zimmer personnel continued working at the 4825 Glenbrook site pumping water from the excavation of grid 50/-10. Five loads of water for a total of 4,150 gallons was pumped and transferred to the federal property site for storage. After pumping the team worked at the federal property site dumping cleared roll off boxes, three boxes were dumped and relined.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPI (0)

Problems encountered/resolutions:**Instructions given by government personnel:****Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

R

16 6-11-18

0630 SAFETY BRIEF

0750 RADIO CHECKS TRAFFIC SIGNS UP

0820 PUMPING WATER FROM GRID 50/10

1700 SECURED

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 12 June 2018

Site Location: 4825 Glenbrook Road

Weather:

Mild, possible rain Low 66° High 78°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil			
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Buhl, Jay	Whitten, Ricky	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Parsons and Zimmer personnel continued working at the 4825 Glenbrook site pumping water from the excavation of grid 50/-10. Two loads of water for a total of 1,620 gallons was pumped and transferred to the federal property site for storage. After pumping the team began bringing in soil from the federal property site and backfilling the hole. Six loads of backfill soil was transferred to the 4825 site. One load of cleared soil was transferred to the sub-title D landfill. The toilet was replaced at the federal property site.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

17 6-12-18

0630 SAFETY BRIEF

0750 RADAR CHECKS TRAFFIC SIGN UP.

0815 PUMPING WATER FROM GRID 50-10.

1230 DAVEY LAWN SERVICE @ FEDERAL PROPERTY.

1815 BACK FILLING GRID 50-10.

1700 SECURED

By [Signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 13 June 2018

Site Location: 4825 Glenbrook Road

Weather:

Mild, possible scattered showers Low 67° High 87°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Buhl, Jay	Whitten, Ricky	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Parsons and Zimmer personnel continued working at the 4825 Glenbrook site backfilling grid 50/-10. After backfilling the team moved construction matting and began excavation of grid 10/-10.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

R


18 6-13-18

0630 SAFETY BRIEF

0755 ROAD CREWS TRAFFIC SIGNS UP.

0820 BACK FILLING GRID 50/10.

1700 Secured.

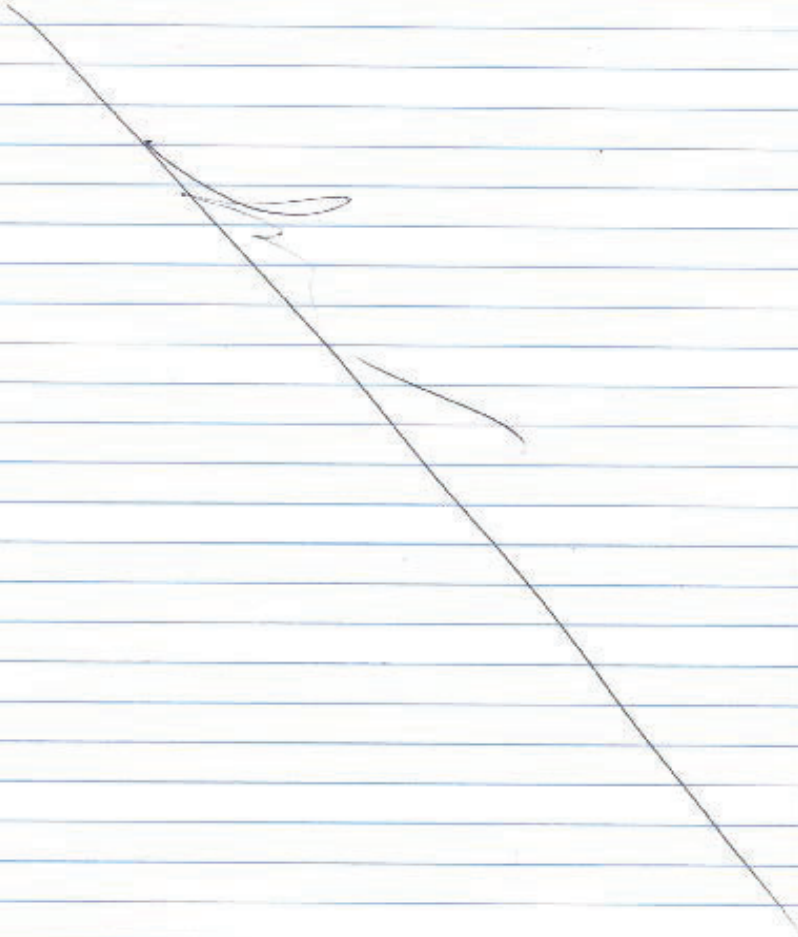

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 14 June 2018

Site Location: 4825 Glenbrook Road

Weather:

Mild, possible scattered showers Low 70° High 84°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Buhl, Jay	Whitten, Ricky	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Parsons and Zimmer personnel continued excavation of grid 10/-10. Site personnel performed end of week clean up and maintenance.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

R

19

6-14-18

0630 SAFETY BRIEF

0710 RECALIBRATE THE PERIMETER BUST MONITOR.

0750 RADIO CHECKS. TRAFFIC SIGNS UP.

0810 REMOVING OVER BURDEN FROM GRID 18-10
AREA "E"

1026 ROLLOFF 274308 ON SITE.

1038 VOC COLLECTED

1250 ROLLOFF 274308 OFF SITE.

1322 ROLLOFF RB 21718RT ON SITE.

1331 VOC COLLECTED

1420 ROLLOFF RB 21718RT OFF SITE

1444 ROLLOFF 279892 ON SITE.

1448 VOC COLLECTED.

1459 COMPOSITE COLLECTED.

1700 SECURED



Handwritten signature and a large diagonal line crossing out the bottom half of the page.

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 18 June 2018

Site Location: 4825 Glenbrook Road

Weather:

Hot and humid Low 69° High 96°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Buhl, Jay	Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Parsons and Zimmer personnel continued excavation of grid 10/-10. Three roll off boxws were filled and the associated soil samples were collected. Site activities were affected by the WBGT work/rest cycles.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

R

20

6-19-18

0636 SAFETY BRIEF
0750 RADIO CHECKS TRAFFIC SIGNS UP.
0820 ROLL OFF 279892 OFF SITE. DIGGING GRID 10-20
0825 WBET @ 89.6 WORK/REST 50/50
0850 ROLL OFF R2649 RT ON SITE
0935 VOC COLLECTED
1009 WBET @ 93.0 WORK/REST 25/75
1013 ROLL OFF R2649 RT OFF SITE.
1120 ROLL OFF R2624 RT ON SITE
1134 VOC COLLECTED
1237 ROLL OFF R2624 RT OFF SITE.
1436 ROLL OFF 279888 ON SITE
1433 VOC COLLECTED
1513 COMPOSITE SAMPLE COLLECTED
1700 SECURED

B. J. Smith

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 19 June 2018

Site Location: 4825 Glenbrook Road

Weather:

Hot and humid Low 76° High 91°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
Rockwell, Margaret	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Buhl, Jay	Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Parsons and Zimmer personnel continued excavation of grid 10/-10. Three roll off boxes were filled and the associated soil samples were collected. Site activities were affected by the WBGT work/rest cycles and afternoon thunder storms. Parsons HVAC contractor made inspection and repairs to the AC units at the federal property site.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

[illegible]

R

21 6-19-18

0630 SAFETY BRIEF.

0750 RADIO CHECKS TRAFFIC SIGNS UP.

0810 Rolloff 279888 OFF SITE.

0840 Rolloff 279900 ON SITE.

0850 VOB COLLECTED. DIGGING GRID 10-10

0853 WRT @ 92.6 WORK/REST 25/75

0940 Rolloff 279900 OFF SITE.

1010 Rolloff 274314 ON SITE.

1013 VOB COLLECTED.

1100 Rolloff 274314 OFF SITE

1245 Rolloff 279982 ON SITE.

1314 LIGHTNING HOLD

1348 OFF LIGHTNING HOLD.

1403 LIGHTNING HOLD

1617 OFF LIGHTNING HOLD

1700 SECURED



The bottom half of the page is crossed out with a large diagonal line. A handwritten signature, which appears to be 'J. R. [unclear]', is written across the middle of the page, partially obscured by the diagonal line.

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 20 June 2018

Site Location: 4825 Glenbrook Road

Weather:

Hot and humid Low 71° High 86°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
Rockwell, Margaret	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Buhl, Jay	Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Parsons and Zimmer personnel pumped 650 gallons of water from grid 10/-10 then completed excavation. After the excavation was complete confirmation samples were collected. ECBC was on site removing the MINICAMS shed from 4825 and transferring it to PSB.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACL (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

P₉

22 6-20-18

0630 SAFETY BRIEF

0700 RADIO CHECKS TRAFFIC SIGNS UP
ECBC ON SITE TO MOVE MINICAMS SHED.

0716 Roll off 279982 OFF SITE.

0730 PUMPING WATER FROM GRID 10-10.


1113 Roll off R25924 RT ON SITE
FILLING W/SPILLS FROM GRID 10-10.

1120 VOC COLLECTED.

1157 COMPOSITE SAMPLE COLLECTED.

1259 CONFIRMATION SAMPLING FOR GRID
10-10 COMPLETED.

1700 STORED.

A handwritten signature in black ink, appearing to read "B. J. Smith", is written diagonally across the lower half of the page. The signature is written over a large, thin diagonal line that spans from the left margin to the right margin.

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 21 June 2018

Site Location: 4825 Glenbrook Road

Weather:

Hot and humid Low 75° High 83°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
Rockwell, Margaret	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Buhl, Jay	Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Parsons and Zimmer personnel worked at the 4825 site moving backfill material from the staging area down to the work area. The team also worked at the federal property site lining empty roll off boxes. Site personnel performed end of week clean up and maintenance. The roll off truck was sent out for repairs due to a faulty hydraulic line.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACL (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

R

23 6-21-18

0630 SAFETY BRIEF

0700 RADIO CHECKS TRAFFIC SIGNS UP

0745 PPE DRAMS 424/425 H2O DRUM 659

LIDS FOR FEDERAL PROPERTY

0820 MOVING SPECS (CLEAN) FROM UPPER
TO LOWER LEVEL.

1100 CONFERENCE CALL.

1500 SECURED

A large, stylized handwritten signature in black ink, slanted diagonally across the page.

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 25 June 2018

Site Location: 4825 Glenbrook Road

Weather:

Hot and humid Low 72° High 83°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
Rockwell, Margaret	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Buhl, Jay	Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Parsons and Zimmer personnel completed moving backfill material from the staging area down to the work area then installed additional silt fencing. Personnel moved construction matting and prepped the area for the next arsenic grid excavation. The team also built and tested a new sifting barrel funnel in anticipation of renewed CACM excavation in the fall.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACL (0)
CPJ (0)

Problems encountered/resolutions:**Instructions given by government personnel:****Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

R

24 6-25-18

0630 SAFETY BRIEF

0700 RADIO CHECKS

1700 SECURED

~~CONFIDENTIAL~~

Pg

25 6-26-18

0630 SAFETY BRIEF.

0659 RADIO CHECKS TRAFFIC SIGNS UP.

TEAMS WORKING AT FEDERAL PROPERTY

1700 SECURED

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 27 June 2018

Site Location: 4825 Glenbrook Road

Weather:

Hot and humid Low 69° High 79°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil			
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
Rockwell, Margaret	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Buhl, Jay	Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Parsons and Zimmer personnel pumped 2,900 gallons of water from grid 10/-10.. After the pumping was complete the team began backfilling the excavation.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

26 6-27-18

0630 SAFETY BRIEF.

0710 RADIO CHECKS TRAFFIC SIGNS UP.

PUMPING WATER FROM GRID 10/10

0937 SAFETY WALK AT FED PROPERTY

1320 BACKFILLING GRID 10/10

1700 SECURED

By [Signature]

R
H

27 6-28-18

0630 SAFETY BRIEF

0700 RADIO CHECKS TRAFFIC SIGNS DP

BACKFILLING GRID 10-10.

1700 SECURED

~~RECEIVED~~

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 02 July 2018

Site Location: 4825 Glenbrook Road

Weather:

Hot and humid Low 77° High 99°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
Rockwell, Margaret	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James	CENAB	
	Buhl, Jay	Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Parsons and Zimmer personnel continued excavation of grid -10/-30. The team reported that an odor was encountered in the HTW excavation of Grid -10,-30 at a little before 11:00 am. We were able to identify that the odor was coming from the saprolite which was competent but not rock hard (i.e. we were not in AUES related fill or disturbed soil). We sampled what we thought was the source of the odor based on our observations. This sample will be analyzed by ECBC as described in the attached email. If clear for agent and ABPs Parsons will ship the sample to the commercial lab for VOCs and TICs, SVOCs and TICs, Pesticides and PCBs, Metals, Explosives, Cyanide, Fluoride, and Iodide analysis. Parsons covered the area in question with plastic and halted operations pending soil sampling data.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

28

7-2-18

- 0630 SAFETY BRIEF
 0700 RADIO CHECKS TRAFFIC SIGNS UP.
 0719 FUELING EQUIPMENT.
 0750 WBET @ 87.6 WORK/REST 75/75 FOR LIGHT MOB "D".
 0805 ROLL OFF RB36776 RT ON SITE.
 0817 VOC COLLECTED WBET @ 98.3 WORK/REST
 25/75 FOR LIGHT WORK.
 0900 DIGGING GRID -10-30.
 0950 ROLL OFF RB36776 RT OFF SITE.
 1000 ROLL OFF 274582 ON SITE
 1010 VOC COLLECTED.
 1025 WBET @ 98.0
 1037 THE TEAM REPORTS A SMELL RESEMBLING
 CACM. WORK WAS STOPPED THE
 ROLL OFF COVERED. THE TEAM WAS MOVED
 UP TO THE BREXID TRAILER. NO SYMPTOMS
 REPORTED.
 1049 THE SITE MANAGER AND USACE NOTIFIED
 1105 SEAN BUCKLEY NOTIFIED
 1205 SEAN BUCKLEY ON SITE.
 1245 GRAB SAMPLES FROM GRID -10-30.
 1340 GRID -10-30 WAS MITIGATED.
 1700 SECURED



[illegible]

Pc

29

7-3-18

0630 SAFETY BRIEF

0700 RADIO CHECKS

1140 MEETING W/ SEAN DUCKLEY

1410 SECURED

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 05 July 2018

Site Location: 4825 Glenbrook Road

Weather:

Hot and humid Low 75° High 92°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth			
	Prate, Warren		
Nelms, Bobby			
Rockwell, Margaret	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
		CENAB	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

A skeleton crew of Parsons and Zimmer personnel came in for a half day to collect water samples from one of the 24,000-gallon Baker tanks. The samples were collected, packaged and shipped to the laboratory for analysis.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

[illegible]

Pg
30

7-5-18

0630 SAFETY BRIEF

0700 THE TEAM IS TAKING WATER SAMPLES.

1200 SECURED

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 09 July 2018

Site Location: 4825 Glenbrook Road

Weather:

Hot and humid Low 70° High 89°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
		CENAB	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Parsons and Zimmer personnel worked at the federal property site emptying cleared roll off boxes and lining boxes. Six loads of cleared soil were dumped and staged.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

R₂

31 7-9-18

0630 SAFETY BRIEF.

0810 THE TEAM IS WORKING AT
FEDERAL PROPERTY DUMPING REARDS

0930 GET OUT WET GLOVES.

1130 CONFERENCE CALL DISCUSSING SAMPLING
RESULTS FROM GRID 10-30.

1700 SECURED

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 10 July 2018

Site Location: 4825 Glenbrook Road

Weather:

Hot and humid Low 69° High 92°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James		
	Artcagu, Carlos		
		CENAB	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Parsons and Zimmer personnel worked at the 4825 Glenbrook Rd site backfilling grid -10/-30. The grid was lined with geo-textile cloth backfilled and compacted.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pm

32 7-10-18

0630 SAFETY BRIEF

0710 RADIO CHECKS

0740 TRAFFIC SIGNS UP.

0819 ROLL OFF 274582 OFF SITE.

0825 BACKFILLING GRID -10-30 w/CLEAN

BUFFAL

1910 SECURED

BT
SL

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 11 July 2018

Site Location: 4825 Glenbrook Road

Weather:

Hot and humid Low 69° High 89°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James		
	Williams, Bobby		
		CENAB	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site personnel laid down construction matting to the back of the site then began excavation of grid 70/00. Two roll-off boxes were filled.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

7/9

33 7-11-18

0630 SAFETY BRIEF

0700 RADIO CHECKS TRAILER SIGNS UP
OPTION SITE TO REACQUIRE GRID CORNERS.
TO 10 AND 90-10

0740 PLACING CONSTRUCTION MATS IN PREP
TO DIG ARSENIC GRIDS.

1250 ROLLOFF 279968 ON SITE.

1300 VOC COLLECTED.

1340 ROLLOFF 279968 IS FULL

1355 ROLLOFF 279968 OFF SITE.

1420 ROLLOFF 279892 ON SITE.

1425 VOC COLLECTED.

1450 WBETE 92.3 WORK/REST 75/25
LEVEL "D" LIGHT.

1509 ROLLOFF 279892 IS FULL

1700 SECURED

TH
5/5

[illegible]

R

34 7-12-18

0630 SAFETY BRIEF.

0655 RADIO CHECKS TRAFFIC SIGNS UP.

0725 THE WIMPAN'S SIDE BARRICADE WAS MOVED

0810 ROLLOFF 279892 OFF SITE.

WBSGT @ 72.9

0838 ROLLOFF RB36774 RT ON SITE.

0900 VOC COLLECTED.

1004 WBSGT @ 83.1

1023 ROLLOFF RB36774 RT OFF SITE.

1045 ROLLOFF 279888 ON SITE.

1050 VOC COLLECTED.

1100 ROLLOFF 279888 OFF SITE.

1330 SAMPLING FOR GRID 7010 COMPLETED.

1510 END OF WEEK MAINTENANCE.

1700 SECURED

R
H

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 16 July 2018

Site Location: 4825 Glenbrook Road

Weather:

Hot and humid Low 74° High 95°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James		
	Williams, Bobby		
		CENAB	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site team began and completed excavation of grid 90/-10. Four roll off boxes were filled.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

[illegible]

Pg

35 7-16-18

0630 SAFETY BRIEF.

0710 RADIO CHECKS TRAFFIC SIGNS UP.

0759 WBGT @ 80.4

0815 ROLL OFF 279887 ON SITE.

0815 VOC COLLECTED. DIGGING GRID 90, -10

0845 WBGT @ 87.0

0920 ROLL OFF 279887 OFF SITE.

0947 ROLL OFF 274308 ON SITE.

1000 WBGT @ 91.3 WORK/REST 75/25

FOR LIAR WORK LEVEL "B".

1005 VOC COLLECTED.

1057 ROLL OFF 274308 OFF SITE.

1140 ROLL OFF 280192 ON SITE.

1236 VOC COLLECTED

1347 ROLL OFF 280192 OFF SITE.

1410 ROLL OFF RB21718RT ON SITE.

1417 VOC COLLECTED

1522 ROLL OFF RB21718RT OFF SITE.

1700 SECURED.



Boh

[illegible]

P₁

36 7-17-18

0630 SAFETY BRIEF.

0700 RADII CHECKS TRAFFIC SIGNS UP.

0830 SAMPLING GRID 90-10 COMPLETE.

0920 THE TEAM IS WORKING AT FEDERAL
PROPERTY DUMPING ROCCOFS.

1401 LIGHTNING HOLD.

1700 SECURED

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 18 July 2018

Site Location: 4825 Glenbrook Road

Weather:

Hot and humid Low 70° High 87°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
Rockwell, Margaret	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James		
	Williams, Bobby		
		CENAB	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site personnel spent the morning setting up an area to rinse off roll off boxes in preparation for turn in. After lunch the team continued to empty cleared roll off boxes. Two loads of cleared soil was shipped to the sub-title D landfill.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPI (0)

Problems encountered/resolutions:**Instructions given by government personnel:****Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

ST 7-18-18

0630 SAFETY BRIEF

0700 RADIO CHECKS

0800 THE TEAM IS WORKING AT FEDERAL
PROPERTY DUMPING AND CLEANING
TOLL OFFS

1530 MEETING W/ STAN BURTON, PHIL MARTIN
SCOTT WUNSCHER, BART YORKSHIRE AND
MARGARET RICKWELL. DATA FORWARDED

1700 SECURED

[Handwritten signature/initials]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 19 July 2018

Site Location: 4825 Glenbrook Road

Weather:

Hot and humid Low 69° High 85°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt			
Rockwell, Margaret	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James		
	Williams, Bobby		
		CENAB	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Two loads of cleared soil was shipped to the sub-title D landfill. Parsons and Zimmer personnel worked at the federal property site rinsing roll off boxes in preparation for turn in. Personnel performed end of week maintenance and clean up.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPI (0)

Problems encountered/resolutions:**Instructions given by government personnel:****Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

38

7-19-2018 Thursday

Sunny Hi 80's

- 0630 Daily safety & operations briefings
- 0700 Radio checks.
- 0738 Traffic control in place. Prepare for washing out rolloffs.
- 0800 Refrigerator @ Fed Prop died asked by Brenda Barber to buy another one. Site Manager along w/ Rider & Oien go for Home Depot.
- 0835 Checked on rolloff washing team @ Fed Prop.
- 1100 Weekly conference call.
- 1120 Call ended.
- 1200 Lunch
- 1230 Resume ops.
- 1300 ~~Bye~~ Dan Matte Rider had headache and left for the day.
- 1500 Begin end of work maintenance & vehicle inspections
- 1600 Guard on site
- 1700 End of day, all secure.

~~Philly report~~

nothing follows

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 23 July 2018

Site Location: 4825 Glenbrook Road

Weather:

Hot and humid Low 68° High 82°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rockwell, Margaret	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James		
	Williams, Angelo		
		CENAB	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site team worked at the federal property site rinsing roll off boxes in preparation for turn in.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
 DAVEY ()
 ACCUPERMIT (2)
 ACI (0)
 CPJ (0)

Problems encountered/resolutions:**Instructions given by government personnel:****Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

R

39

7-23-18

0630 SAFETY BRIEF

0700 RADAR CHECK

0715 LIGHTNING HOLD.

0805 OFF LIGHTNING HOLD. THE TORM
IS CLEARING ROLL OFFS.

1350 LIGHTNING HOLD

1420 OFF LIGHTNING HOLD.

1700 SECURED

~~Signature~~

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 24 July 2018

Site Location: 4825 Glenbrook Road

Weather:

Hot and humid Low 74° High 76°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James		
	Williams, Angelo		
		CENAB	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site team worked at the federal property site rinsing roll off boxes in preparation for turn in.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:**Instructions given by government personnel:****Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

P
6

40

7-24-18

0630

SAFETY BRIEF

0700

RADIO CHECKS

0810

THE TEAM IS CLEANING ROLL OFF'S

1700

SECURED

~~SK~~

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 25 July 2018

Site Location: 4825 Glenbrook Road

Weather:

Hot and humid Low 74° High 79°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rockwell, Margaret			
	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James		
	Williams, Angelo		
		CENAB	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site personnel spent the morning Excavating an additional foot from the north wall of grid 90/-10.

Personnel collected confirmation samples after excavating the additional area. After sampling Parsons and Zimmer personnel worked at the federal property site rinsing roll off boxes in preparation for turn in.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:**Instructions given by government personnel:****Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

[illegible]

PG

4/ 7-25-18

0630 SAFETY BRIEF

0700 RADIO CHECKS TRAFFIC SIGNS UP.

0930 COMPLETED SAMPLING GRID 90-10
NORTH WALL.

1000 THE TEAM IS CLEANING ROADS
AT FEDERAL PROPERTY.

1700 SECURED

~~PG~~

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 26 July 2018

Site Location: 4825 Glenbrook Road

Weather:

Hot and humid Low 72° High 86°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rockwell, Margaret			
	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James		
	Williams, Angelo		
		CENAB	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site team worked at the federal property site rinsing roll off boxes in preparation for turn in.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

42 7-26-18

0630 SAFETY BRIEF

0700 RADIO CHECKS. T6MM WORKING FOR

1110 CONFERENCE CALL

1330 WBUT @ 93.3 WORK/REST 25/75

1445 WBUT @ 100.4

1530 SECURED

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 30 July 2018

Site Location: 4825 Glenbrook Road

Weather:

Hot and humid Low 72° High 81°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James		
	Williams, Angelo		
		CENAB	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site team worked at the 4825-site backfilling and compacting grid 70/10. Due to the excavation of the grid and excessive rains the gravel behind one of the precast concrete sections poured out of the bottom. After the grid was backfilled the team replaced the gravel. Two truckloads of cleared soil went to the sub-title D landfill.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

R

43 7-30-18

0630 SAFETY BRIEF

0700 RADIO CHECKS. TRAFFIC SIGNS VP.

0800 BACKFILLING GRID 70, 70

1100 ECBC INSPECTING FIRE SUP PROBLEM
AT THE IAF'S.

1700 SECURED

Ry
H

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 31 July 2018

Site Location: 4825 Glenbrook Road

Weather:

Hot and humid Low 71° High 82°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James		
	Williams, Angelo		
		CENAB	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site team worked at the federal property site dumping cleared roll off boxes and rinsing the boxes in preparation for turn in. Four boxes were dumped and rinsed. Personnel made repairs to the privacy screening and silt fencing at the 4825 site.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

R

44 7-3-18

0630 SAFETY BRIEF

0700 RADIO CHECKS.

0800 THE TEAM IS WORKING AT FEDERAL
PROPERTY.

1700 SECURED

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 01 August 2018

Site Location: 4825 Glenbrook Road

Weather:

Hot and humid Low 75° High 87°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James		
	Williams, Angelo		
		CENAB	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site team worked at the federal property site dumping cleared roll off boxes and rinsing the boxes in preparation for turn in. Four boxes were dumped and rinsed. Three truckloads of cleared soil went to the sub-title D landfill.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

45 8-1-18

0630 SAFETY BRIEF.

0700 RADIO CHECKS.

0800 TEAM IS WORKING AT FEDERAL
PROPERTY DUMPING AND CLOTHING
ROW OFFS.

1700 SECURED

[Handwritten signature]

Pg

46 8-2-18

0630 SAFETY BRIEF

0650 RADIO CHECKS TRAFFIC SIGNS OP.

0724 ROLL OFF 274345 OFF SITE.

0820 BACK FILLING GRID 90-10.

1100 WEEKLY CONFERENCE CALL.

1220 AM POLICE REPORT A BOMB
THROWER HAD BEEN CAUGHT.

1406 LIGHTNING HOLD.

1800 SECURED FOR WEEKLY MAINTENANCE.



SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 06 August 2018

Site Location: 4825 Glenbrook Road

Weather:

Hot and humid Low 72° High 92°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James		
	Vargas, Brandon		
		CENAB	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site team worked at the federal property site dumping cleared roll off boxes and rinsing the boxes in preparation for turn in. Four boxes were dumped and rinsed. Personnel removed and stored equipment from the 4825 site.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Rg

47 8-6-18

1630 SAFETY BRIEF

0700 RADIO CHECKS

0800 THE TEAM IS WORKING AT FEDERAL
PROPERTY DUMPING AND CLEANING
ROLLERS

1505 LEARNING HOLD.

1710 SECURED

[Handwritten signature]

D

48

8-7-18

0630

JAREY BRIEF

0700

RADIO CHECKS TRAMPIC SIGNS UP.

1800

CLEANING EQUIPMENT FOR TURN IN.

1700

SECURED

~~D
48~~

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 08 August 2018

Site Location: 4825 Glenbrook Road

Weather:

Hot and humid Low 74° High 89°

Personnel on Site

PARSONS	ZES	ECBC	
Courtney, Kenneth	Mangosh, Ed		
Matter, Phil	Prate, Warren		
Oien, Joshua	Yorkshire, Bart		
Nelms, Bobby			
Rider, Matt	LIFE STAR		
Wunschel, Scott			
	ACCUPERMIT	CHENC	
	Schmidt, James		
	Vargas, Brandon		
		CENAB	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Site team worked at the federal property site cleaning up and breaking down the roll off rinse area. Several loads of rinsed roll off boxes were removed from the federal property site. Two rental vehicles were turned in and general clean up was performed.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT (2)
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

49

8-8-18

0630

SAFETY BRIEF


0700

RADIO CHECKS.

Ferrans & Zimmer personnel
clearing equipment & sending out Roll-off Boxes

1700

Day Complete.

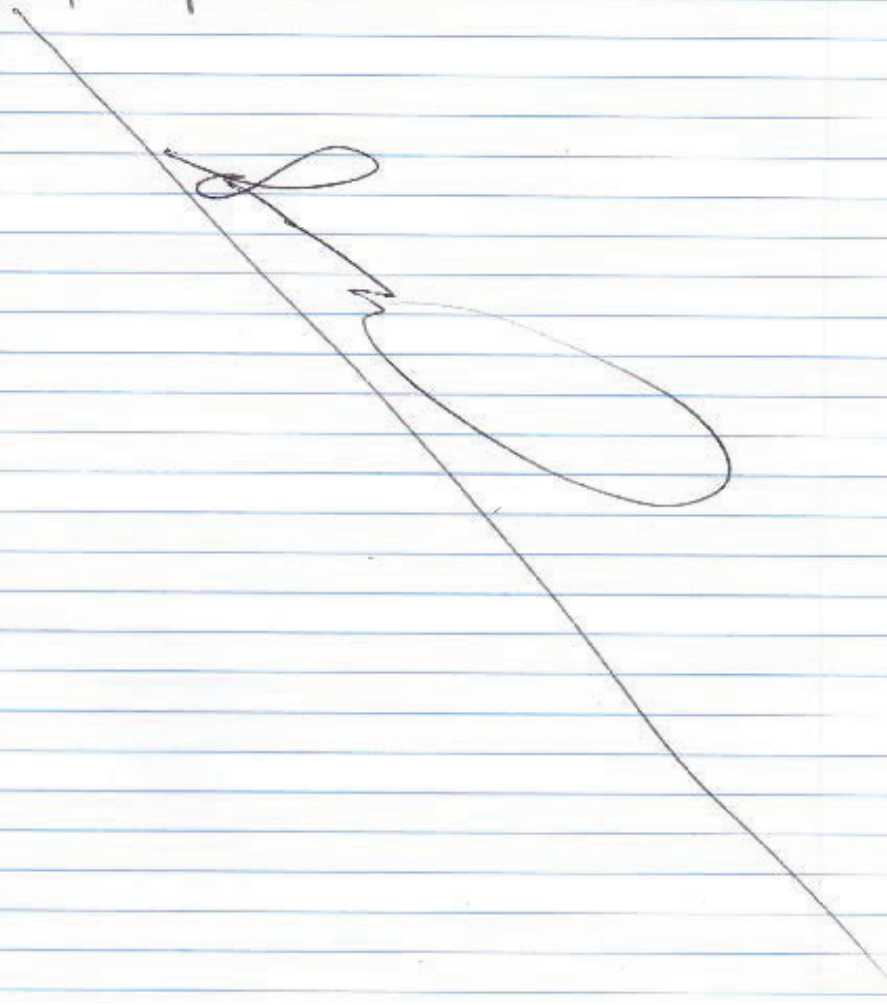

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 10 October 2018

Site Location: 4825 Glenbrook Road

Weather:

Overcast 74/82 degrees

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Prate, Warren	Brown, Matthew	
Castell, Lorna	Yorkshire, Bart	Duff, Todd	
Courtney, Kenneth			
Marion, Jedediah			
Matter, Phillip			
Moon, Dale	LIFE STAR		
Nelms, Bobby			
Oien, Joshus			
Rider, Matthew			
Rockwell, Margaret			
Schlosser, Ariel			
Wunschel, Reina			
Wunschel, Scott	ACCUPERMIT	CEHNC	
	Schmidt, James		
	Williams, Angelo	CENAB	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Arrival of 8 new personell, inprocessing them. ZES brought in stone for area around PDS tent, leveled area. Placed 4 ballast blocks on PDS tent flaps.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT ()
ACI (0)
CPJ (0)

Problems encountered/resolutions:**Instructions given by government personnel:****Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

50 10-10-18

0630 1st day BACK MFG SHUT DOWN

SAFETY BRIEF

0700 CHECKING PERSONNEL CERTIFICATIONS

1230 CONDUCTED SITE SPECIFIC TRAINING

AT FEDERAL PROPERTY

1700 SECURED

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 11 October 2018

Site Location: 4825 Glenbrook Road

Weather:

Partly cloudy, showers, 56/78, 5-10 mph winds

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Huffelfinger, Gerald	Brown, Matthew	
Castell, Lorna	Prate, Warren	Duff, Todd	
Courtney, Kenneth	Yorkshire, Bart		
Marion, Jedediah	Zimmer, Douglas		
Matter, Phillip			
Moon, Dale			
Nelms, Bobby			
Oien, Joshus			
Rider, Matthew			
Rockwell, Margaret	LIFE STAR		
Schlosser, Ariel			
Wunschel, Reina			
Wunschel, Scott	ACCUPERMIT	CEHNC	
	Schmidt, James		
	Williams, Angelo	CENAB	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Porta-count testing, mask fitting. Team assignments and gear set up. Review work plan, SSHP review.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT ()
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

P₉

51 10-11-18

0630 SAFETY BRIGAD

0730 ATTEMPTED TO SET UP PIRIA COUNT
WITHOUT SUCCESS.

1030 PINE ENVIRONMENT WILL SEND
A REPLACEMENT TOMORROW.

1700 SECURED

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 12 October 2018

Site Location: 4825 Glenbrook Road

Weather:

50/63 partly cloudy, winds 5-15 mph

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Huffelfinger, Gerald	Brown, Matthew	
Castell, Lorna	Prate, Warren	Duff, Todd	
Marion, Jedediah	Yorkshire, Bart		
Matter, Phillip	Zimmer, Douglas		
Moon, Dale			
Nelms, Bobby			
Oien, Joshua			
Rider, Matthew			
Rockwell, Margaret			
Schlosser, Ariel	LIFE STAR		
Wunschel, Reina			
Wunschel, Scott			
	ACCUPERMIT	CEHNC	
	Schmidt, James		
	Williams, Angelo	CENAB	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Review work plan, SSHP, AHA's and other pertinent documents. Continued mask fitting and ordered 2 new small Interspiros.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT ()
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

P₆

52

10-12-18

0630

SAFETY BRIEF.

0700

RADIO CHECKS.

0930

RECEIVED PORTAL UNIT, STARTING
FIT TESTING

1400

TEAMS PPE DRESS OUT,

1700

SECURED

BR
SK

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 15 October 2018

Site Location: 4825 Glenbrook Road

Weather:

57/70 rain, winds 5-10 mph

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Huffelfinger, Gerald	Brown, Matthew	
Castell, Lorna	Prate, Warren	Duff, Todd	
Courtney, Kenneth	Wright, David	Framarini, Trevor	
Marion, Jedediah	Yorkshire, Bart	Henderson, Amos	
Matter, Phillip	Zimmer, Douglas	Holland, Joe	
Moon, Dale		McGill, Andre	
Nelms, Bobby		Pettway, Jeffery	
Oien, Joshus		Smith, Ethan	
Rider, Matthew		Wainwright, Leroy	
	LIFE STAR	Wilson, Christopher	
Schlosser, Ariel			
Wunschel, Reina			
Wunschel, Scott	ACCUPERMIT	CEHNC	
	Schmidt, James		
	Williams, Angelo	CENAB	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

6 more mask fittings completed. 4 rolloffs came in. Set up stair lights. Training on proper drum marking.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT ()
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

P₄

53 10-15-18

0630 SAFETY BRIEF.

0700 RADIO CHECKS, FIRE TESTING.

1300 PDS WALK THROUGH WITH TOWNS.

1700 SECURED

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 16 October 2018

Site Location: 4825 Glenbrook Road

Weather:

48/61 overcast, winds 5-10 mph

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Huffelfinger, Gerald	Babcock, Kendall	
Castell, Lorna	Prate, Warren	Brown, Matthew	
Courtney, Kenneth	Wright, David	Duff, Todd	
Marion, Jedediah	Yorkshire, Bart	Framarini, Trevor	
Matter, Phillip	Breyman, Mark	Henderson, Amos	
Moon, Dale		Holland, Joe	
Nelms, Bobby		Kline, David	
Oien, Joshua		McGill, Andre	
Rider, Matthew		Pettway, Jeffery	
	LIFE STAR	Smith, Ethan	
Schlosser, Ariel		Wainwright, Leroy	
Wunschel, Reina		Wilson, Christopher	
Wunschel, Scott	ACCUPERMIT	CEHNC	
		Shott, Ken	
	Schmidt, James		
	Williams, Angelo	CENAB	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Removed clean backfill for Medical Monitoring tent and brought in gravel to level area. Removed ECU from PDS as it requires 3 phase power and we only have single phase. Training on hand tools and Stihl Rock Boss. Forklift removed from site.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT ()
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

24

54

10-16-18

0630

SAFETY BRIEF

0800

ROCK SAW AND POWERED HAND TOOL

1230

TRAINING AT FEDERAL PRISON

1230

CLOTHES/CLOTH OVER BROWN REMOVED

FOR POSITIONING THE MEDICAL
MONITORING TENT.

1440

SAMEL TREE BRANCHING VIEW FROM

TRAILOR WERE REMOVED.

FOR LIFT OFF SITE.

1700

SECURED

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 17 October 2018

Site Location: 4825 Glenbrook Road

Weather:

50/63 partly cloudy, winds 5-17 mph

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Breyman, Mark	Babcock, Kendall	
Castell, Lorna	Huffelfinger, Gerald	Brown, Matthew	
Courtney, Kenneth	Prate, Warren	Duff, Todd	
Marion, Jedediah	Wright, David	Framarini, Trevor	
Matter, Phillip	Yorkshire, Bart	Henderson, Amos	
Moon, Dale		Holland, Joe	
Nelms, Bobby		Kline, David	
Oien, Joshus		McGill, Andre	
Rider, Matthew		Pettiway, Jeffery	
	LIFE STAR	Smith, Ethan	
Schlosser, Ariel		Wainwright, Leroy	
Wunschel, Reina		Wilson, Christopher	
Wunschel, Scott	ACCUPERMIT	CEHNC	
		Shott, Ken	
	Schmidt, James		
	Williams, Angelo	CENAB	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Drum loading/manifesting training. Roll-off loading and unloading training. Pick up trash that has blown in at Federal Property. Instruction on proper way to line a roll-off, and lined 3 roll-offs. Installed air cylinder on Komatsu 35 and filled it and checked for leaks.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT ()
ACI (0)
CPJ (0)

Problems encountered/resolutions:**Instructions given by government personnel:****Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

B

55 10-17-18

1630 SAFETY BRIEF

0700 CONTINUE WITH SITE TRAINING
ECRC IS CONSIDERING THEIR
MEDICAL MONITORING TENT

1715 SECURED

A handwritten signature in dark ink, appearing to be 'B. H.', is written over a diagonal line that spans the lower half of the page. The signature is written in a cursive, somewhat stylized font.

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 18 October 2018

Site Location: 4825 Glenbrook Road

Weather:

44/55 partly cloudy, winds 5-15 mph

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Breyman, Mark	Babcock, Kendall	
Castell, Lorna	Heffelfinger, Gerald	Brown, Matthew	
Courtney, Kenneth	Prate, Warren	Duff, Todd	
Marion, Jedediah	Wright, David	Framarini, Trevor	
Matter, Phillip	Yorkshire, Bart		
Moon, Dale		Holland, Joe	
Nelms, Bobby			
Oien, Joshus		McGill, Andre	
Rider, Matthew		Pettitway, Jeffery	
	LIFE STAR	Smith, Ethan	
		Wainwright, Leroy	
Wunschel, Reina		Wilson, Christopher	
Wunschel, Scott	ACCUPERMIT	CEHNC	
		Shott, Ken	
	Schmidt, James		
	Williams, Angelo	CENAB	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Mr. Shott observed Zimmer excavation and drum filling procedures, no soil was dug. Removed Super Silt fence to make room for drum filling area. Assembled mitigation kit and went over its use with Mr. Shott. Replaced plastic around AU field water valves and trimmed grass around them. New excavator delivered to Fed Prop, Zimmer crew trained on it. Replaced broken sandbags around site.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT ()
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

79

56 10-18-18

0630 SAFETY BRIEF

0700 RADIO CHECKS

0800 EXCAVATOR TRAINING WITH 805 AND
TEAMS

1300 PREPINK AREA FOR OPERATIONS

1700 SECURED

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 19 October 2018

Site Location: 4825 Glenbrook Road

Weather:

55/65 clear, winds 5-10mph

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Breyman, Mark	Babcock, Kendall	
Castell, Lorna	Heffelfinger, Gerald	Brown, Matthew	
Courtney, Kenneth	Prate, Warren	Framarini, Trevor	
Marion, Jedediah	Wright, David	Holland, Joe	
Matter, Phillip	Yorkshire, Bart	McGill, Andre	
Moon, Dale	Rutana, Steve	Overton, Robert	
Nelms, Bobby	Zimmer, Doug	Pettway, Jeffery	
Oien, Joshus		Smith, Ethan	
Rider, Matthew		Wainwright, Leroy	
	LIFE STAR	Wilson, Christopher	
Schlosser, Ariel			
Wunschel, Reina			
Wunschel, Scott	ACCUPERMIT	CEHNC	
		Shott, Ken	
	Schmidt, James		
	Williams, Angelo	CENAB	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Continued training with Mr. Shott and teams. Set up water line heat traces. Building clean-up. Komatsu mechanic on site performing maintenance.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT ()
ACI (0)
CPJ (0)

Problems encountered/resolutions:**Instructions given by government personnel:****Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

R₄

57 10-19-18

0630 SAFETY BRIEF

0700 RADIO CHECKS

0800 PREP'ING SITE FOR IMPITWINE BAS.

1130 DISH MAINTENANCE ON SITE

1530 RISK MAINTENANCE OFF SITE

1700 SECURED

[Handwritten signature]

Pg

58

10-22-18

0630 SAFETY BRIEF

0700 TRAFFIC SIGN IN PLACE RADIO CHARGES

0900 TRAINING: TEAM DRESS OUT IN LEVEL 'B'
PROCESS THRU PDS, DRAM FILLING SIMULATION,
HOW TO RESPOND TO ALARMS WHILE
EVACUATING

1700 SECURED

[Handwritten signature]

Pg

59 10-23-18

0630 SAFETY BRIEF

0700 RADIO CHECKS

0900 THE SITE IS SET UP FOR LEVEL 8

TRAINING - "RESCUE DOWNED OPERATOR"

1130 RISK MAINTENANCE ON SITE

1430 RISK MAINTENANCE OFF SITE

1700 SECURED

[Handwritten signature]

R
G

40 10.24-18

0630 SAFETY BRIEF

0700 RADIO CHECKS

0900 SITE SETUP FOR LEVEL "B" TRAINING

AND REMOVING OVERBORDEN FROM
SPONS PILE IN FRONT OF THE POS.

1330 MIDDAY CHAMUNGE COMPLETE

STARTING LEVEL "B" TRAINING, COLLECTING

VIC'S AND COMPOSING SAMPLE TRAINING.

1700 SECURED

[Handwritten signature]

R

61 10-25-18

0630 SAFETY BRIEF.

0700 RHD 10 CMC CS.

10840 Team 3 began removing clean backfill soil from
around the CACM spoils pile.

1035 Roll off Box is full of backfill, preparing to swap.

1045 Performing Roll off swap.

1130 Lunch Break.

1200 Tim 3 dumping Roll offs at Fed. Tim 2 excavating
backfill at 4825 G3.

1430 Team Training w/ Sures & OESS.

1630 Site clean up.

1700 Day Complete.

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062

Delivery Order: TO 0006

Date: 26 October 2018

Site Location: 4825 Glenbrook Road

Weather:

48/54 cloudy, winds 5-10 mph

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Breyman, Mark	Brown, Matthew	
Castell, Lorna	Heffelfinger, Gerald	Duff, Todd	
Courtney, Kenneth	Prate, Warren	Framarini, Trevor	
	Wright, David	Holland, Joe	
Matter, Phillip	Yorkshire, Bart	McGill, Andre	
Moon, Dale	Rutana, Steve	Owens, Julius	
Nelms, Bobby		Pettway, Jeffery	
Oien, Joshus		Smith, Ethan	
Rider, Matthew	LIFE STAR	Wainwright, Leroy	
Rockwell, Margaret	Vines, Doreen	Wilson, Christopher	
Schlosser, Ariel	Alfaro, Walter		
Wunschel, Reina	ACCUPERMIT	CEHNC	
Wunschel, Scott	Schmidt, James	Shott, Ken	
	Williams, Angelo	CENAB	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Full set-up, vitals taken, monitors out and running, mini-CAMS ringoff, CWM sample taken. New Baker tank arrives, 3 rollofs of clean backfill taken out.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Tom Rosso ECBC

Tim Blades ECBC

Contractors

Berkel ()

DAVEY ()

ACCUPERMIT ()

ACI (0)

CPJ (0)

Problems encountered/resolutions:**Instructions given by government personnel:****Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

10-26-18

P61
62

0650 Morning Safety Brief

0645 Site Set up

0705 Radio Checks.

0745 Turn 1 Remaining Backfill Soil + placing in Plot 11.


0930 Team mitigating Training w/ Surveys & DESS.

1035 Continue Remaining clean Backfill.

1130 Lunch

1630 End of day clean up.

1720 Day Complete.

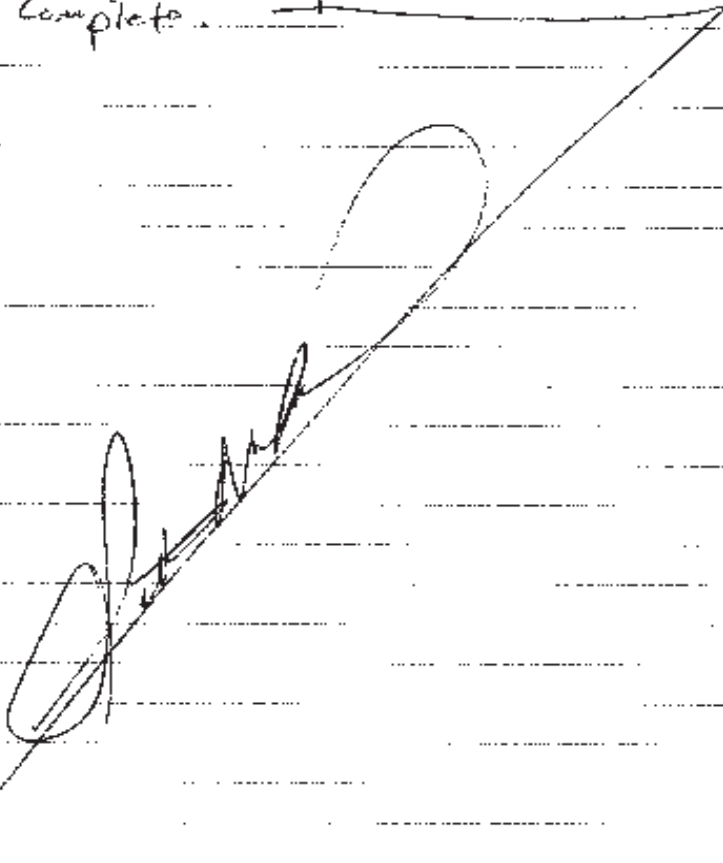

P₉

163 10.29.18

0630 SAFETY BRIEF

0700 RADIO CHECKS

0800 MINICAMS UP

0900 MEDICAL TENT & PDS UP

1007 ALL MINIBUS IN PLACE AND RAINING

1022 RIDER, COUNTRY & HEFFELFINGER

DOWN RANGE IN LEVEL 'B'

1045 COLLECTING VOC

1110 PPE CHECKS.

1130 SOIL DRUMS 1593-1604 FILLED, READY

FOR TRANSPORT.

1138 TEAM 2 CLEARED POS.

1155 STARTING MIDDAY CHALLENGE

1210 MIDDAY COMPLETE

1303 SOIL DRUMS 1593-1604 LOADED FOR FED PROPERTY.

1332 DIET, BUSCH & WRIGHT DOWN RANGE LEVEL 'B'

1401 PPE CHECKS COMPLETE.

1431 PPE CHECKS COMPLETE.

1457 WRIGHT CLEARED POS

1500 COMPOSITE COLLECTED.

1519 TEAM 1 CLEARED POS. SOIL DRUMS 1605-1624 FOR

1530 STARTING END OF DAY CHECK

1542 SOIL DRUMS 1605-1616 LOADED FOR

FED PROPERTY.

1710 SECURED




Pg

64

10-30-18

0630 SAFETY BRIEF

0700 RADIO CHECKS.

0738 TEAM 2 DOWN RANGE FOR SET UP.

0745 MINICAMS UP

0820 KOMATSU 'K' BOTTLE CHARGED TO 900 PSI.

0825 SOIL DRUMS 1617-1622 LOADED

FOR FEDERAL PROPERTY.

0835 MONITORS ARE SET UP & EXCLUSION
ZONE ESTABLISHED.

0838 TEAM 2 CLEARED PDS.

0840 DRAMS PUMPS RUNNING

0844 TEAM 3 DOWN RANGE LEVEL 'B'.

0854 VIL COLLECTED.

0913 PPE CHECKS.

1000 PPE CHECKS

1025 SOIL DRUMS 1623-1640 FILLED

1034 TEAM 3 CLEARED PDS.

1109 SOIL DRUMS 1623-1634 LOADED

FOR FEDERAL PROPERTY.

1142 SOIL DRUMS 1635-1648 LOADED FOR
FEDERAL PROPERTY.

1216 MID DAY COMPLETE

1300 TEAM 1 DOWN RANGE LEVEL 'B'.

1304 TEAM 1 REPAIR HCL MONITOR ALARMING.

1311 REPLACED THE BATTERY / HCL MONITOR

WORKING PROPERLY.

1321 PPE CHECKS.

1339 PPE CHECKS.

1417 SOIL DRUMS 1641-1655 FILLED.

Pg

66 10-31-18

0630 SAFETY BRIEF.

0700 RADIO CHECKS.

0740 MINICAMS UP

0750 PUMPS PUMP'S RUNNING. ALL MONITORS
IN PLACE. MEDICAL IN PLACE.

0810 TEAM 2 DOWN RANGE LEVEL "B".

0819 VOC COLLECTED

0840 PPE CHECKS

0912 PPE CHECKS.

0943 SOIL DRUMS 1656-1670 FILLED.

1012 SOIL DRUMS 1656-1670 LOADED FOR
FEDERAL PROPERTY.

0947 TEAM 2 CLEARED PDS

1058 PPE CHECKS.

1124 SOIL DRUMS 1671-1685 FILLED

1129 TEAM 3 CLEARED PDS.

1150 STARTING MIDDAY CHAUNGLE

1152 SOIL DRUMS 1671-1685 LOADED FOR
FEDERAL PROPERTY.

1205 MIDDAY COMPLETE

1252 TEAM 1 DOWN RANGE LEVEL "B".

1323 PPE CHECKS.

1353 PPE CHECKS

1407 SOIL DRUMS 1686-1700 FILLED.

1409 COMPOSITE COMPLETED

1430 TEAM 1 CLEARED PDS.

1440 STARTING END OF DAY CHECKS.

1509 SOIL DRUMS 1676-1700 & PPE 427
LOADED FOR FEDERAL PROPERTY.

D
9

11-1-18

1630 SAFETY BRIEF

1700 RADIO CHECKS

1800 THE TEAMS ARE WORKING AT
FEDERAL PROPERTY. NON-INTRUSIVE
NO MEDICAL SUPPORT.

1900 CONFERENCE CALL

1700 SECURED

By [Signature]
[Signature]

79

69

11-2-18

0630 SAFETY BRIEF

0730 RADIO CHECKS.

0743 SETUP TOTAL DOWN RANGE "1"

0740 MINICAMS UP

0800 DAMMS DUMPS IN PLACE AND RUNNING

0806 SETUP COMPLETE, TEAM 1 CLEARED PDS

0819 VOC COLLECTED. NOTE: TEAM 2 DOWN
RANGE LEVEL "B" @ 0811.

0840 PPE CHECKS.

0908 PPE CHECKS.

0933 SOIL DUMMS 1701-1718 FILLED.

0953 TEAM 2 CLEARED PDS.

1018 SOIL DUMMS 1701-1715 LOADED FOR FEDERAL
PROPERTY.

1033 TEAM 3 DOWN RANGE LEVEL "B"

1054 PPE CHECKS.

1115 PPE CHECKS.

1136 SOIL DUMMS 1719-1732 FILLED.

1142 TEAM 3 CLEARED PDS.

1155 STARTING MIDDAY CHALLENGE.

1210 MINICAMS BACK UP

1218 SOIL DUMMS 1716-1730 LOADED FOR
FEDERAL PROPERTY.

1300 TEAM 1 DOWN RANGE LEVEL "B"

1329 INTRUSIVE OPS SUSPENDED DUE TO HEAT STRESS.

1333 SOIL DUMMS 1731-1736 FILLED, COMPOSITE
SAMPLE COLLECTED.

1343 TEAM 1 CLEARED PDS.

1344 TEAM 3 DOWN RANGE TO MITIGATE SPILLS.

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062
 Delivery Order: TO 0006
 Date: 5 November 2018
 Site Location: 4825 Glenbrook Road

Weather: _____
 50/53 rain, winds 0-5 mph

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Breyman, Mark	Babcock, Kendall	
Castell, Lorna	Heffelfinger, Gerald	Duff, Todd	
Courtney, Kenneth	Prate, Warren	Harris, Brian	
Marion, Jediaiah	Rutana, Steve	Manthei, Michael	
Matter, Phillip	Wright, David	McGill, Andre	
Moon, Dale	Yorkshire, Bart	Miller, Don	
Nelms, Bobby		Overton, Robert	
Oien, Joshus		Pettway, Jeffery	
Rider, Matthew	LIFE STAR	Privett, Arlita	
Rockwell, Margaret	Alfaro, Walter	Wainwright, Leroy	
Schlosser, Ariel	Anderson, Monique	Wilson, Christopher	
Wunschel, Reina			
Wunschel, Scott		CEHNC	
	ACCUPERMIT	Shott, Ken	
	Schmidt, James		
	Williams, Angelo	CENAB	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive operations today; steady, increasing rain led us to end the day at 10:30AM. By noon over 1.5" of rain had fallen on site.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT ()
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

R.

71 11-5-18

1630 SAFETY BRIEF STEADY RAIN

1700 RADIO CHECKS.

1745 MINICAMS UP

1800 INTRUSIVE OPERATION SUSPENDED
DUE TO RAIN.

1130 SECURED

Ry
8/2

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062
 Delivery Order: TO 0006
 Date: 6 November 2018
 Site Location: 4825 Glenbrook Road

Weather: _____
 47/67 rain/thunderstorms

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Breyman, Mark	Babcock, Kendall	
Castell, Lorna	Heffelfinger, Gerald	Duff, Todd	
Courtney, Kenneth	Prate, Warren	Harris, Brian	
Marion, Jediaiah	Rutana, Steve	Manthei, Michael	
Matter, Phillip	Wright, David	McGill, Andre	
Moon, Dale	Yorkshire, Bart	Miller, Don	
Nelms, Bobby			
Oien, Joshus		Pettitway, Jeffery	
Rider, Matthew		Priviett, Arlita	
	LIFE STAR	Wainwright, Leroy	
Schlosser, Ariel	Alfaro, Walter	Wilson, Christopher	
Wunschel, Reina	Anderson, Monique		
Wunschel, Scott			
		CEHNC	
	ACCUPERMIT	Shott, Ken	
	Schmidt, James		
	Williams, Angelo	CENAB	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Once again heavy rain, no intrusive operations. Site secured at 1030.

End of Day: 1030

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
	Berkel ()
	DAVEY ()
	ACCUPERMIT ()
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

P₄

72 11-6-18

0630 SAFETY BRIEF

0700 RADIO CHECKS

0704 PDS OP

0755 TEAM 3 DOWN RANGE FOR SETUP

1010 STARTING END DAY CHECKS

1030 THE SITE HAS STOPPED/SUSPENDED
INTRUSIVE OPERATION DUE TO HEAVY
RAIN.

1700 SECURED

~~P₄ 5/2~~

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062
 Delivery Order: TO 0006
 Date: 7 November 2018
 Site Location: 4825 Glenbrook Road

Weather: _____
 48/63 Partly sunny, winds 5-10 mph

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Breyman, Mark	Babcock, Kendall	
Castell, Lorna	Heffelfinger, Gerald	Duff, Todd	
Courtney, Kenneth	Prate, Warren	Harris, Brian	
Marion, Jediaiah	Rutana, Steve	Manthei, Michael	
Matter, Phillip	Wright, David	McGill, Andre	
Moon, Dale	Yorkshire, Bart	Miller, Don	
Nelms, Bobby		Pettitway, Jeffery	
Oien, Joshus		Priviett, Arlita	
Rider, Matthew		Wainwright, Leroy	
	LIFE STAR	Wilson, Christopher	
Schlosser, Ariel	Dunnivant, Delany		
Wunschel, Reina	Gumbs Vines, Doreen		
Wunschel, Scott			
		CEHNC	
	ACCUPERMIT	Shott, Ken	
	Schmidt, James		
	Williams, Angelo	CENAB	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Turned off water to AU athletic field and bled lines. Set up heat trace lines on same, and tested them.
 Filled 41 soil drums from spoils pile.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
	Berkel ()
	DAVEY ()
	ACCUPERMIT ()
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

R

73 11-7-18

0630 SAFETY BRIEF.

0700 RADIO CHECKS.

0735 MINICAMS UP

0752 TEAM 3 DOWN RANGE FOR SETUP.

0820 DAAMS RUNNING.

0829 TEAM 3 CLEARED POS.

0834 TEAM 1 DOWN RANGE LEVEL "B".

0845 VOC COLLECTED.

0904 PPE CHECKS.

0932 PPE CHECKS.

0940 MINICAMS REPORT 5.8 FOR CT AT ^{"PHASE 1"}
THE DRUM FILLING "A" POINT.

0944 SECOND CYCLE FOR CT ALL CLEAR.

1004 SOIL DRUMS 1737-1751 FILLED.

1019 TEAM 1 CLEARED POS.

1047 SOIL DRUMS 1737-1751 LOADED FOR
FEDERAL PROPERTY.

1100 TEAM 2 DOWN RANGE LEVEL "B".

1129 PPE CHECKS.

1142 SOIL DRUMS 1752-1756 FILLED.

1152 TEAM 2 CLEARED POS. STARTING
MID DAY CHALLENGE

1159 TEAM 1 DOWN RANGE MID "A"

1215 MINICAMS UP

1232 TEAM 1 CLEARED POS.

1308 TEAM 3 DOWN RANGE LEVEL "B".

1337 PPE CHECKS.

1358 PPE CHECKS.

1410 SOIL DRUMS 1757-1770 FILLED

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062
 Delivery Order: TO 0006
 Date: 8 November 2018
 Site Location: 4825 Glenbrook Road

Weather: _____
 43/57 partly sunny, winds 5-10 mph

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Breyman, Mark	Babcock, Kendall	
Castell, Lorna	Heffelfinger, Gerald	Duff, Todd	
Courtney, Kenneth	Prate, Warren	Harris, Brian	
Marion, Jediaiah	Rutana, Steve	Manthei, Michael	
Matter, Phillip	Wright, David	McGill, Andre	
Moon, Dale	Yorkshire, Bart	Miller, Don	
Nelms, Bobby		Pettitway, Jeffery	
Oien, Joshus		Priviett, Arlita	
Rider, Matthew		Wainwright, Leroy	
	LIFE STAR	Wilson, Christopher	
Schlosser, Ariel	Brooke, Bailey		
Wunschel, Reina	Gumbs Vines, Doreen		
Wunschel, Scott			
		CEHNC	
	ACCUPERMIT	Shott, Ken	
	Schmidt, James		
	Williams, Angelo	CENAB	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Filled 42 drums from spoils pile. 12 Parsons employees tested and certified on CPR/First Aid/AED.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT ()
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

P₆

75 11-8-18

- 0630 SAFETY BRIEF SUNNY POTHIS
ON SITE FOR CPR/FIRST AID TRAINING.
- 0700 RADIO CHECKS.
- 0722 TEAM 1 DOWN RANGE FOR SETUP
- 0745 SOIL DRUMS 1772-1776, AQ 660, ~~BER 429~~ 559
LOADED FOR TRANSPORT TO FEDERAL PROPERTY.
- 0744 MUXICAMS UP.
- 0800 DAAMS PUMPS RUNNING. TEAM 1 COMPLETED
SETUP & CLEARED PDS.
- 0815 TEAM 2 DOWN RANGE LEVEL "B".
- 0828 VOC COLLECTED.
- 0840 PPE CHECKS.
- 0903 PPE CHECKS.
- 0935 SOIL DRUMS 1777-1791 FILLED
- 0945 TEAM 2 CLEARED PDS.
- 1013 SOIL DRUMS 1777-1791 LOADED FOR
FEDERAL PROPERTY.
- 1027 TEAM 3 DOWN RANGE LEVEL "B".
- 1059 PPE CHECKS.
- 1100 CONFERENCE CALL
- 1127 PPE CHECKS.
- 1145 SOIL DRUMS 1792-1803 FILLED.
- 1152 TEAM 3 CLEARED PDS. STARTING MIDWAY
- 1210 SOIL DRUMS 1792-1803 BEING LOADED
FOR FEDERAL PROPERTY.
- 1318 TEAM 1 DOWN RANGE LEVEL "B"
- 1350 PPE CHECKS.
- 1420 PPE CHECKS.
- 1506 SOIL DRUMS 1804-1818 FILLED

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062
 Delivery Order: TO 0006
 Date: 9 November 2018
 Site Location: 4825 Glenbrook Road

Weather: _____
 46/66 overcast, rain, slight breeze

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Breyman, Mark	Babcock, Kendall	
Castell, Lorna	Heffelfinger, Gerald	Duff, Todd	
Courtney, Kenneth	Prate, Warren	Harris, Brian	
Marion, Jediah	Rutana, Steve	Manthei, Michael	
Matter, Phillip	Wright, David	McGill, Andre	
Moon, Dale	Yorkshire, Bart	Miller, Don	
Nelms, Bobby		Pettway, Jeffery	
Oien, Joshus		Privett, Arlita	
Rider, Matthew		Wainwright, Leroy	
	LIFE STAR	Wilson, Christopher	
Schlosser, Ariel	Brooke, Bailey		
	Gumbs Vines, Doreen		
Wunschel, Scott		CEHNC	
	ACCUPERMIT	Shott, Ken	
	Overton, Robert		
	Williams, Angelo	CENAB	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Komatsu 35 has mechanical issues cannot keep engine running, excavator is parked in drum filling area and is blocking us from removing excess clean backfill off of spoils pile. Crew sent home at 1300, part is not in stock for excavator will be repaired Tuesday next week.

End of Day: 1300

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
	Berkel ()
	DAVEY ()
	ACCUPERMIT ()
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Komatsu 35 excavator fuel pump shut-off relay broken, new part ordered. Due for repair Tuesday 13th.

Instructions given by government personnel:**Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

P₄

TL 11-9-18

0630 SAFETY BRIEF

0705 RADIO CHECKS

0744 MINICAMS UP.

0700 THE KOMATSU 35 WILL NOT START.

THE KOMATSU MAINTENANCE IS ENROUTE.

1120 KOMATSU MAINTENANCE ON SITE.

STARTING END OF DAY CHECKS FOR
MONITORING.

1210 KOMATSU MAINTENANCE OFF SITE

1300 SECURED

[Signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062
 Delivery Order: TO 0006
 Date: 13 November 2018
 Site Location: 4825 Glenbrook Road

Weather: _____
 43/48 overcast, 5-10 mph winds

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Breyman, Mark	Duff, Todd	
Castell, Lorna	Heffelfinger, Gerald	Harris, Brian	
Courtney, Kenneth	Prate, Warren	Manthei, Michael	
Marion, Jediah	Rutana, Steve	McGill, Andre	
Matter, Phillip	Wright, David	Miller, Don	
Moon, Dale	Yorkshire, Bart	Pettway, Jeffery	
Nelms, Bobby		Privett, Arlita	
Oien, Joshus		Tucker, Robin	
Rider, Matthew		Tucker, Willie	
Rockwell, Margaret	LIFE STAR	Wainwright, Leroy	
Schlosser, Ariel	Alfaro, Walter		
Wunschel, Reina	Anderson, Monique		
Wunschel, Scott		CEHNC	
	ACCUPERMIT	Shott, Ken	
	Arteiger, Carlos		
	Williams, Angelo	CENAB	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Pumped 1150 gallons of water out of excavation area. Komatsu 35 was repaired and put back into service. Removed clean excess backfill off of Glenbrook Road side of spoils pile. Repaired 2 rolloff covers at Federal Property.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT ()
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Komatsu 35 excavator fuel pump shut-off relay broken, new part ordered. Due for repair Tuesday 13th.

Instructions given by government personnel:**Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

2
79 11-13-18
630 SAFETY BRIEF
700 RADIO CHECKS.
742 MINICAMS UP.
800 PDS UP THE TOWER IS PUMPING
WATER FROM EXCAVATION.
1025 RISH MAINTENANCE ON SITE
1055 RISH MAINTENANCE COMPLETE FIX.
1122 MID DAY COMPLETE
1230 REMOVING CLEAN OVERBURDEN FROM
THE SPOILS PILE IN FRONT OF PDS.
1502 RETURN TO FEDERAL PROPERTY.
1700 SECURED

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062
 Delivery Order: TO 0006
 Date: 14 November 2018
 Site Location: 4825 Glenbrook Road

Weather: _____
 38/46 overcast

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Breyman, Mark	Duff, Todd	
Castell, Lorna	Heffelfinger, Gerald	Harris, Brian	
Courtney, Kenneth	Prate, Warren	Manthei, Michael	
Marion, Jediaiah	Rutana, Steve	McGill, Andre	
Matter, Phillip	Wright, David	Miller, Don	
Moon, Dale	Yorkshire, Bart	Pettway, Jeffery	
Nelms, Bobby		Privett, Arlita	
Oien, Joshus		Tucker, Robin	
Rider, Matthew		Tucker, Willie	
Rockwell, Margaret	LIFE STAR	Wainwright, Leroy	
Schlosser, Ariel	Alfaro, Walter		
Wunschel, Reina	Anderson, Monique		
Wunschel, Scott		CEHNC	
	ACCUPERMIT	Shott, Ken	
	Arteiger, Carlos		
	Williams, Angelo	CENAB	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Monitored digging 25 drums filled, finished the spoils pile. Begin set up for removal of clean backfill over area 1.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT ()
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Komatsu 35 excavator fuel pump shut-off relay broken, new part ordered. Due for repair Tuesday 13th.

Instructions given by government personnel:**Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

[illegible]

Pg

79 11-14-18

0630 SAFETY BRIEF

0700 RADIO CHECKS

0742 MINICAMS UP.

0800 DAMS PUMPS RUNNING.

0816 TEAM 3 DOWN RANGE LEVEL "B".

0827 VOC COLLECTED.

0845 PPE CHECKS.

0913 PPE CHECKS.

0945 PPE CHECKS.

1009 SOIL DRUMS 1819-1833 FILLED.

1026 TEAM 3 CLEARED PDS

SOIL DRUMS 1819-1833 LOADED FOR
FEDERAL PROPERTY. PPE DRUMS 430/431.
AND SCR 560.

1122 MIDDAY CHALLENGE COMPLETE

1159 TEAM 1 DOWN RANGE.

1233 PPE CHECKS.

1305 SOIL DRUMS 1834-1840 FILLED.

1309 COMPOSITE SAMPLE COLLECTED.

1321 TEAM 1 CLEARED PDS.

1417 SOIL DRUMS 1834-1840 LOADED FOR
FEDERAL PROPERTY.

1500 MEETING W/ CROW TO DISCUSS PATH
FORWARD TO REMOVE CLEM NET BORDEN.

1700 SECURED

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062
 Delivery Order: TO 0006
 Date: 15 November 2018
 Site Location: 4825 Glenbrook Road

Weather: _____
 33/41 partly cloudy

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Breyman, Mark	Duff, Todd	
Castell, Lorna	Heffelfinger, Gerald	Harris, Brian	
Courtney, Kenneth	Prate, Warren	Manthei, Michael	
Marion, Jediah	Rutana, Steve	McGill, Andre	
Matter, Phillip	Wright, David	Miller, Don	
Moon, Dale	Yorkshire, Bart	Pettway, Jeffery	
Nelms, Bobby		Privett, Arlita	
Oien, Joshus		Tucker, Robin	
Rider, Matthew		Tucker, Willie	
Rockwell, Margaret	LIFE STAR	Wainwright, Leroy	
Schlosser, Ariel	Alfaro, Walter		
Wunschel, Reina	Anderson, Monique		
Wunschel, Scott		CEHNC	
	ACCUPERMIT	Shott, Ken	
	Arteiger, Carlos		
	Williams, Angelo	CENAB	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Ice on roads early in AM, held up roll-off truck for a few hours. Clean backfill removal, filled 4 rolloffs, dumped 3 roll-offs.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT ()
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Komatsu 35 excavator fuel pump shut-off relay broken, new part ordered. Due for repair Tuesday 13th.

Instructions given by government personnel:**Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg
80

11-15-18

0630 SAFETY BRIEF

0700 RADIO CHECKS.

0800 STRAINING Removal of CIGAR
OVER BIRDEN IN AREA 1

1038 ROLL OFF ROLL

1142 ROLL OFF SITE.

1240 FILLED 2nd ROLL OFF AND OFF SITE.

1409 3rd ROLL OFF FULL AND OFF SITE.

1502 4th ROLL OFF FULL AND OFF SITE.

1700 SECURED

Bry
Shaw

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062
 Delivery Order: TO 0006
 Date: 16 November 2018
 Site Location: 4825 Glenbrook Road

Weather: _____
 32/41 cold, icy; winds 10-20 mph

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Breyman, Mark	Duff, Todd	
Castell, Lorna	Heffelfinger, Gerald	Harris, Brian	
Courtney, Kenneth	Prate, Warren	Manthei, Michael	
Marion, Jediah	Rutana, Steve	McGill, Andre	
Matter, Phillip	Wright, David	Miller, Don	
Moon, Dale	Yorkshire, Bart	Pettway, Jeffery	
Nelms, Bobby		Privett, Arlita	
Oien, Joshus		Tucker, Robin	
Rider, Matthew		Tucker, Willie	
Rockwell, Margaret	LIFE STAR	Wainwright, Leroy	
Schlosser, Ariel	Alfaro, Walter		
Wunschel, Reina	Anderson, Monique		
Wunschel, Scott			
		CEHNC	
	ACCUPERMIT	Shott, Ken	
	Arteiger, Carlos		
	Williams, Angelo	CENAB	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Pumped 3100 gallons of water. Continued removal of clean backfill from area 1. Lined 2 roll-offs.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
	Berkel ()
	DAVEY ()
	ACCUPERMIT ()
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Komatsu 35 excavator fuel pump shut-off relay broken, new part ordered. Due for repair Tuesday 13th.

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

11-16-18

30 SAFETY BRIEF

0 RADIO CHECKS.

100 PUMPING WATER FROM EXCAVATION

1st LOAD TO FEDERAL PROPERTY.

2nd LOAD TO FEDERAL PROPERTY.

16 3rd LOAD TO FEDERAL PROPERTY.

4 4th LOAD TO FEDERAL PROPERTY.

0 REMOVING CLEAN OVERBURDEN FROM AREA 1.

70 FULL ROLL OFF TO FEDERAL PROPERTY.

00 SECURED

BSH
S
H

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062
 Delivery Order: TO 0006
 Date: 19 November 2018
 Site Location: 4825 Glenbrook Road

Weather: _____
 37/57 overcast

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Breyman, Mark	Druyor, Dana	
Castell, Lorna	Heffelfinger, Gerald	Duff, Todd	
Courtney, Kenneth	Prate, Warren	Harris, Brian	
Marion, Jediaiah	Rutana, Steve	Manthei, Michael	
Matter, Phillip	Wright, David	McGill, Andre	
Moon, Dale	Yorkshire, Bart	Miller, Don	
Nelms, Bobby		Pettitway, Jeffery	
Oien, Joshus		Priviett, Arlita	
Rider, Matthew	LIFE STAR	Tucker, Willie	
Rockwell, Margaret	Alfaro, Walter	Wainwright, Leroy	
Schlosser, Ariel	Anderson, Monique		
Wunschel, Reina			
Wunschel, Scott		CEHNC	
	ACCUPERMIT	Shott, Ken	
	Schmidt, James		
	Williams, Angelo	CENAB	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

4 roll-offs filled, lined and dumped. Built barrel yard at Federal Property for expected upcoming increase in soil drums.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT ()
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

72 11-19-18

0630 SAFETY BRIEF

0700 RADIO CHECKS.

0730 REMOVING CLEAN WORK BURDEN FROM AREA 1.

0807 1ST ROLL OFF IS FULL AND OFF SITE.

1011 2ND ROLL OFF IS FULL AND OFF SITE.

0356 3RD ROLL OFF IS FULL AND OFF SITE.

1700 SECURED.

ETA



SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062
 Delivery Order: TO 0006
 Date: 20 November 2018
 Site Location: 4825 Glenbrook Road

Weather: _____
 34/52 partly cloudy

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Breyman, Mark	Druyor, Dana	
Castell, Lorna	Heffelfinger, Gerald	Duff, Todd	
Courtney, Kenneth	Prate, Warren	Harris, Brian	
Marion, Jediaiah	Rutana, Steve	Manthei, Michael	
Matter, Phillip	Wright, David	McGill, Andre	
Moon, Dale	Yorkshire, Bart	Miller, Don	
Nelms, Bobby		Pettitway, Jeffery	
Oien, Joshus		Priviett, Arlita	
Rider, Matthew		Tucker, Willie	
Rockwell, Margaret	LIFE STAR	Wainwright, Leroy	
Schlosser, Ariel	Alfaro, Walter		
Wunschel, Reina	Anderson, Monique		
Wunschel, Scott		CEHNC	
	ACCUPERMIT	Shott, Ken	
	Overton, Robert		
	Schmidt, James	CENAB	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

3 roll-offs of clean backfill removed, 3 rolloffs dumped and lined.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT ()
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

73 11-20-18

0630 SAFETY BRIEF

0710 RADIO CHECKS.

0718 Roll off off site. This was filled
on 11-19-18. Removing clean over Borden area 2

1013 Roll off full and off site. 1st

1320 Roll off is full and off site 2nd

1401 JAR 561/562 LOADED FOR FEDERAL
PROPERTY.

1453 Roll off is full and off site 3rd.

1700 SECURED

BR
H

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062
 Delivery Order: TO 0006
 Date: 21 November 2018
 Site Location: 4825 Glenbrook Road

Weather: _____
 29/50 partly sunny, breezy

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Prate, Warren		
Castell, Lorna	Wright, David		
Courtney, Kenneth	Yorkshire, Bart		
Marion, Jedidiah			
Matter, Phillip			
Moon, Dale			
Nelms, Bobby			
Oien, Joshus			
Rider, Matthew	LIFE STAR		
Rockwell, Margaret			
Schlosser, Ariel			
Wunschel, Reina			
Wunschel, Scott		CEHNC	
	ACCUPERMIT	Shott, Ken	
		CENAB	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Prepare site for Thanksgiving holiday. Strapped down all drums, police call, wrap and power heat trace line to 4835 property. Fueled all excavators and secured loose areas of perimeter fence covering.

End of Day: 1130

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A


Visitors	Contractors
_____	Berkel ()
_____	DAVEY ()
_____	ACCUPERMIT ()
_____	ACI (0)
_____	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

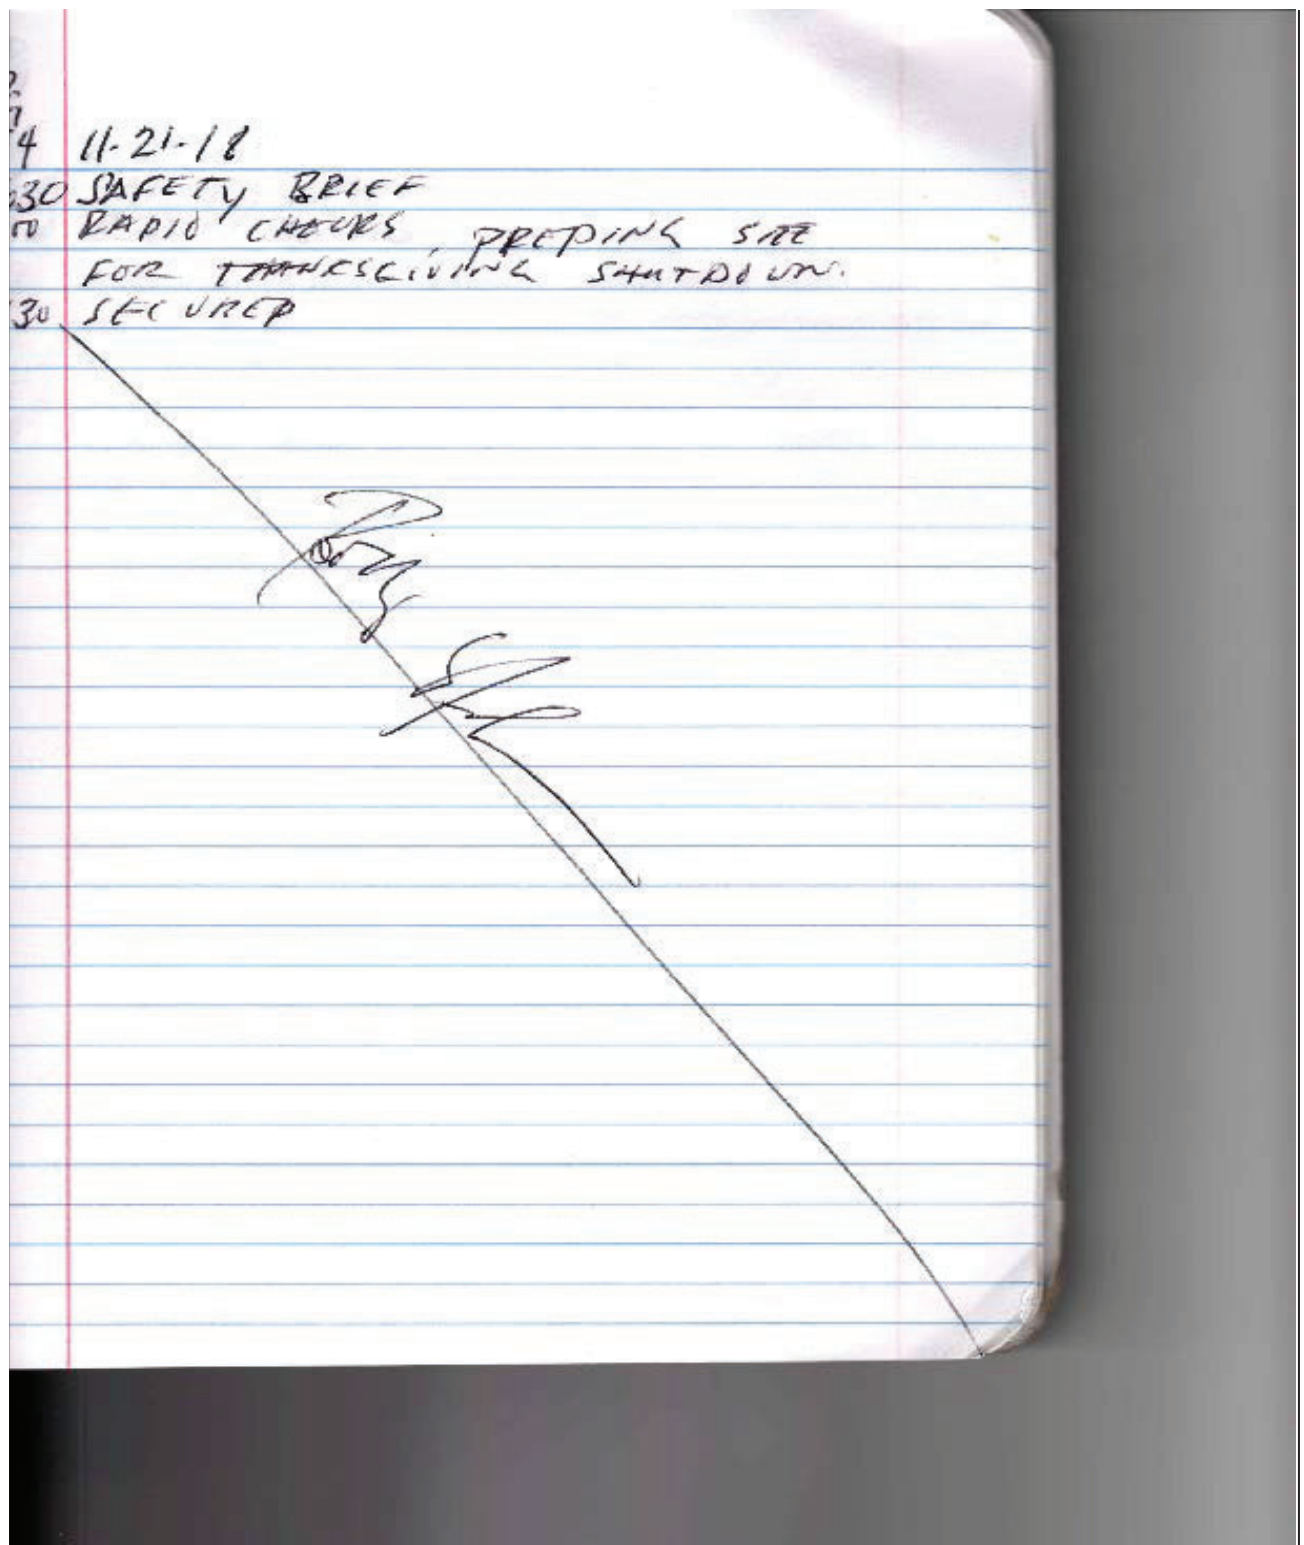

4

11-21-18

30 SAFETY BRIEF

30 RADIO CHECKS PREPINS SAE
FOR TRANSMISSION SHUTDOWN.

30 SECURED

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062
 Delivery Order: TO 0006
 Date: 26 November 2018
 Site Location: 4825 Glenbrook Road

Weather: _____
 46/50 rainy 5-10 mph winds

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Breyman, Mark	Dusick, Brandon	
Castell, Lorna		Brown, Matthew	
Courtney, Kenneth	Prate, Warren		
Marion, Jedidiah	Rutana, Steve		
Matter, Phillip	Wright, David		
Moon, Dale	Yorkshire, Bart		
Nelms, Bobby			
Oien, Joshus			
Rider, Matthew			
Rockwell, Margaret	LIFE STAR		
Schlosser, Ariel	Alfaro, Walter		
Wunschel, Reina	Anderson, Monique		
Wunschel, Scott			
		CEHNC	
	ACCUPERMIT	Shott, Ken	
	Williams, Angelo		
	Schmidt, James	CENAB	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

ECBC travel day. Pumped 2000 gallons of water, weight drums for shipment average. Separated drums for HAZ shipment in early December. No intrusive operations today.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
	Berkel ()
	DAVEY ()
	ACCUPERMIT ()
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

ECBC never showed up for operations today, as they called this a travel day after Thanksgiving.

Instructions given by government personnel:**Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

P₉

85 11-26-18

0630 SAFETY BRIEF ECBC TRAVEL DAY.

0700 RADIO CHECKS.

1120 PUMPING WATER FROM AREA 1
EXCAVATION APPROX 2000 GAL.

1350 THE TEAMS WORKING AT FEDERAL
PROPERTY

1700 SECURED.

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062
 Delivery Order: TO 0006
 Date: 27 November 2018
 Site Location: 4825 Glenbrook Road

Weather: _____
 32/44 winds 5-20 mph

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Breyman, Mark	Askew, Thomas	
Castell, Lorna	Heffelfinger, Gerald	Baker, Dawn	
Courtney, Kenneth	Prate, Warren	Bartash, Ian	
Marion, Jediaiah	Rutana, Steve	Brown, Matthew	
Matter, Phillip	Wright, David	Doyle, Satchell	
Moon, Dale	Yorkshire, Bart	Dusick, Brandon	
Nelms, Bobby		McGill, Andre	
Oien, Joshua		Miller, Don	
Rider, Matthew		Pettitway, Jeffery	
Rockwell, Margaret	LIFE STAR	Wainwright, Leroy	
Schlosser, Ariel	Alfaro, Walter		
Wunschel, Reina	Anderson, Monique		
Wunschel, Scott		CEHNC	
	ACCUPERMIT	Shott, Ken	
	Williams, Angelo		
	Schmidt, James	CENAB	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Cutting retaining wall with Stihl Rock Boss saw. Sampled the water in 2 Baker tanks. Pumped 1150 gallons of water from excavation area. Digging out in front of retaining wall to get a better angle to finish cutting the wall.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT ()
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

[illegible]

Pg.

96

11-27-18

630 SAFETY BRIEF

700 RADIO CHECKS.

740 START TO PUMP WATER FROM
AREA 1 EXCAVATION. PDS UP.800 FIRST LOAD WATER TO FEDERAL
PROPERTY. MINICAMS UP @ 07:35.0945 TEAM 1 DOWN RAIL MID "B" CUTTING
RETAINING WALL.

1147 STARTING MID DAY CAUTION.

1200 MID DAY COMPLETE

1337 ALL MONITORS ARE IN POSITION AND RUNNING

1343 TEAM 2 DOWN RAIL LOWER "B" RIDER
COURTESY WRIGHT.

1400 VOC COLLECTED.

1414 PPE CHECKS.

1430 PPE CHECKS.


1513 PPE CHECKS.

1541 COMPOSITE SAMPLE COLLECTED, SOIL
DRUMS 1744-1852 FILLED.

1543 TEAM 2 CHANGED PDS.

1530 STARTING END OF DAY CHECKS.

1700 SECURED



SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062
 Delivery Order: TO 0006
 Date: 28 November 2018
 Site Location: 4825 Glenbrook Road

Weather:
 31/42 5-25 mph winds

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Breyman, Mark	Askew, Thomas	
Castell, Lorna	Heffelfinger, Gerald	Baker, Dawn	
Courtney, Kenneth	Prate, Warren	Bartash, Ian	
Marion, Jediah	Rutana, Steve	Brown, Matthew	
Matter, Phillip	Wright, David	Doyle, Satchell	
Moon, Dale	Yorkshire, Bart	Dusick, Brandon	
Nelms, Bobby		McGill, Andre	
Oien, Joshua		Miller, Don	
Rider, Matthew		Pettitway, Jeffery	
Rockwell, Margaret	LIFE STAR	Wainwright, Leroy	
Schlosser, Ariel	Alfaro, Walter		
Wunschel, Reina	Dunnavant, Delany		
Wunschel, Scott			
		CEHNC	
	ACCUPERMIT	Shott, Ken	
	Williams, Angelo		
	Schmidt, James	CENAB	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Finished cutting retaining wall then brought in Komatsu 228 (largest excavator) and pulled down the scored section of wall. Began digging the area that was behind the retaining wall.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT ()
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

R

87 11-28-18

0630 SAFETY BRIEF

0700 RADIO CHECKS.

0715 MINICAMS UP.

0809 DAMPS PUMPS RUNNING

0825 SOIL DRUMS 1844-1852 LOADED FOR
FEDERAL PROPERTY.0904 TEAM DOWN RANGE 100'0" TO CUT
RETAINING WALL W/ROCK SAW.

1129 STARTING MIDDAY CHALLENGE.

1220 MIDDAY COMPLETE.

1312 TEAM 3 DOWN RANGE LEVEL 'B' REMOVE
RETAINING WALL W/LARGE EXCAVATOR.

1345 TEAM 3 CLEARED POS

1435 SCR DRUMS 1844-1852 LOAD
FOR FEDERAL PROPERTY.1500 STARTING END OF DAY CHECKS
1700 SECURED

R. J. [Signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062
 Delivery Order: TO 0006
 Date: 29 November 2018
 Site Location: 4825 Glenbrook Road

Weather: _____
 33/42 winds 5-15 mph

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Breyman, Mark	Askew, Thomas	
Castell, Lorna	Heffelfinger, Gerald	Baker, Dawn	
Courtney, Kenneth	Prate, Warren	Bartash, Ian	
	Rutana, Steve	Brown, Matthew	
Matter, Phillip	Wright, David	Doyle, Satchell	
Moon, Dale	Yorkshire, Bart	Dusick, Brandon	
Nelms, Bobby		McGill, Andre	
Oien, Joshua		Miller, Don	
Rider, Matthew		Pettitway, Jeffery	
Rockwell, Margaret	LIFE STAR	Wainwright, Leroy	
Schlosser, Ariel	Alfaro, Walter		
Wunschel, Reina	Dunnavant, Delany		
Wunschel, Scott			
		CEHNC	
	ACCUPERMIT	Shott, Ken	
	Schmidt, James		
	Williams, Angelo	CENAB	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Remove large portion of sprinkler system that is in our work area. American University electrician removed the main power feed to sprinkler system. Filled 18 drums with soil from behind retaining wall.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT ()
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

[illegible]

P6

98

11-29-18

0630 SAFETY BRIEF

0700 RADIO CHECKS

0710 PDS UP

0714 MINICAMS UP

0740 PUMPED APPROX 250 GAL FROM
AREA EXCAVATION.

0750 DAMS PUMPS RUNNING

0835 MEDICAL IN PLACE, ALL MONITORS IN
PLACE AND RUNNING.0855 TEAM 1 DOWN RANGE LOVEL "8" OVEN SCHWARTZ
WRIGHT. INTENSIVE IN AREA 1.

0932 VOC COLLECTED. PPE CHECKS.

0954 PPE CHECKS.

1024 PPE CHECKS.

1040 STOPPED INTENSIVE OPERATIONS WHILE AA
CHECKS THE SPRINKLER SYSTEM.

1055 TEAM 1 CLEARED PDS. SOIL DRUMS 1853-1857 FILLED.

1140 STARTING MIDDAY CHALLENGE.

1215 MIDDAY COMPLETE.

1253 TEAM 2 DOWN RANGE LOVEL "8" RIDGE CRILL
HEFFELINGER. INTENSIVE AREA 2. FILLING
BARRELS.

1324 PPE CHECKS.

1419 SOIL DRUMS 1858-1862 FILLED. PPE CHECKS.

1453 PPE CHECKS.

1530 SOIL DRUMS 1863-1870 FILLED.

1544 COMPOSITE COLLECTED

1544 TEAM 2 CLEARED PDS.

1545 START/END OF DAY CHECKS.

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062
 Delivery Order: TO 0006
 Date: 30 November 2018
 Site Location: 4825 Glenbrook Road

Weather: _____
 36/45 p. cloudy, rain winds 5-10 mph

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Breyman, Mark	Askew, Thomas	
Castell, Lorna	Heffelfinger, Gerald	Baker, Dawn	
Courtney, Kenneth	Prate, Warren	Bartash, Ian	
Marion, Jediah	Rutana, Steve	Brown, Matthew	
Matter, Phillip	Wright, David	Doyle, Satchell	
Moon, Dale	Yorkshire, Bart	Dusick, Brandon	
Nelms, Bobby		McGill, Andre	
Oien, Joshua		Miller, Don	
Rider, Matthew	LIFE STAR	Pettitway, Jeffery	
Rockwell, Margaret	Alfaro, Walter	Wainwright, Leroy	
	Dunnavant, Delany		
Wunschel, Reina			
Wunschel, Scott		CEHNC	
	ACCUPERMIT	Shott, Ken	
	Schmidt, James		
	Williams, Angelo	CENAB	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Digging behind reaining wall area 25 drums filled. Setting up schedule to test IHF lightning protection system.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT ()
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

[illegible]

Pg

90

11/30-18

0630 SAFETY BRIEF

0700 RADIO CHECKS.

0815 SOIL DRUMS 1853-1867, PPE DRUMS 432-433
LOADED FOR TRANSPORT TO FEDERAL PROPERTY.0847 TEAM 3 DOWN RANGE LEVEL "B" MOUNTAIN WINDSHEET,
HEFFELFINGER.

0900 VOC COLLECTED.

0944 PPE CHECKS.

1009 PPE CHECKS.

1039 PPE CHECKS.

1108 SOIL DRUMS 1871-1885 FILLED

1125 TEAM 3 CLEARED PDS.

1135 STARTING MID DAY

1150 MID DAY COMPLETE.

1314 SOIL DRUMS 1868-1882 LOADED FOR FEDERAL
PROPERTY. SCR 565

1328 TEAM 1 DOWN RANGE LEVEL "B".


1352 PPE CHECKS.

1410 PPE CHECKS.

1501 COMPOSITE COLLECTED SOIL DRUMS
1886-1895 FILLED.

1506 TEAM 1 CLEARED PDS.

1530 END OF DAY MOUNTAIN WINDSHEET



SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062
 Delivery Order: TO 0006
 Date: 03 December 2018
 Site Location: 4825 Glenbrook Road

Weather:
 46/56 winds 5-15 mph

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Breyman, Mark	Baker, Dawn	
Castell, Lorna	Heffelfinger, Gerald		
Courtney, Kenneth	Prate, Warren	Bartash, Ian	
Marion, Jediah	Rutana, Steve	Brown, Matthew	
Matter, Phillip		Doyle, Satchell	
Moon, Dale	Yorkshire, Bart	McGill, Andre	
Nelms, Bobby		Miller, Don	
Oien, Joshua		Nguyen Phong	
Rider, Matthew	LIFE STAR	Pettitway, Jeffery	
Rockwell, Margaret	Alfaro, Walter	Wainwright, Leroy	
Schlosser, Ariel	Robinson, Omar		
Wunschel, Reina			
Wunschel, Scott		CEHNC	
	ACCUPERMIT	Shott, Ken	
	Schmidt, James		
	Williams, Angelo	CENAB	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Pumped 350 gallons of rain water from excavation area. 2 tanker trucks removed approximately 12,000 gallons of water from Baker tank to waste facility. 30 drums filled with soil from excavation in area 1.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
	Berkel ()
	DAVEY ()
	ACCUPERMIT ()
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

[illegible]

Pk

91 12-3-18

0630 SAFETY BRIEF

0700 RADIO CHECKS.

0740 PUMPING WATER FROM AREA 2
EXCAVATION.

0732 MUDICAMS UP

0800 DAMS PUMPS RUNNING.

0840 REMOVED APPROX 350 GAL WATER.

0917 SOIL DRUMS 1883-1895 LOADED FOR
FEDERAL PROPERTY.

0932 TEAM 2 DOWN RANGE LEVEL "B" RIDGE
COURTNEY, RAYMOND.

0942 VOC COLLECTED.

1007 PPE CHECKS.

1031 PPE CHECKS.

1132 SOIL DRUMS 1896-1910 FILLED.

1143 TEAM 2 CLEARED PDS. STARTING MID DAY.

1210 SOIL DRUMS 1896-1910 LOADED FOR
FEDERAL PROPERTY.

1215 MIDDAY COMPLETE

1334 TEAM 3 DOWN RANGE LEVEL "B" MOON.
MORIAN, BRYAN.

1354 PPE CHECKS.

1415 PPE CHECKS.

1438 PPE CHECKS.

1507 SOIL DRUMS 1911-1925 FILLED.

1517 COMPOSITE COLLECTED.

1522 TEAM 3 CLEARED PDS

1549 SOIL DRUMS 1911-1925 LOADED
FOR FEDERAL PROPERTY.

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062
 Delivery Order: TO 0006
 Date: 04 December 2018
 Site Location: 4825 Glenbrook Road

Weather: _____
 28/43 winds 5-15 mph

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Breyman, Mark	Askew, Thomas	
Castell, Lorna	Heffelfinger, Gerald	Baker, Dawn	
Courtney, Kenneth	Prate, Warren	Bartash, Ian	
Marion, Jediaiah	Rutana, Steve	Brown, Matthew	
Matter, Phillip	Wright, David	Nguyen, Phuong	
Moon, Dale	Yorkshire, Bart	Manthei, Michael	
Nelms, Bobby		McGill, Andre	
Oien, Joshua		Miller, Don	
Rider, Matthew		Pettitway, Jeffery	
Rockwell, Margaret	LIFE STAR	Wainwright, Leroy	
Schlosser, Ariel	Alfaro, Walter		
Wunschel, Reina	Anderson, Monique		
Wunschel, Scott			
		CEHNC	
	ACCUPERMIT	Shott, Ken	
	Schmidt, James		
	Williams, Angelo	CENAB	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive ops in area 1, removed 30 soil drums. 6,000 gallons of water removed from Baker tank and 90 drums transported to waste facility.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
	Berkel ()
	DAVEY ()
	ACCUPERMIT ()
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Had to reroute 4835 downspout on SE corner of house to 4835 driveway, informed CENAB Steelman of the the reroute.

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

93 12.4.15

0630 SAFETY BRIEF.

0700 RADIO CHECKS.

0732 MINICAMS UP

0748 ADAMS PUMPS RUNNING

0806 ALL MONITORS IN PLACE AND RUNNING
TEAM 1 DOWN RANGE LEVEL "B".

0834 PPE CHECKS.

0848 VOC COLLECTED.

0900 PPE CHECKS.

0922 PPE CHECKS.

0946 PPE CHECKS.

1019 SOIL DRUMS 1926-1940 FILLED.

1053 TEAM 1 CLEARED PDS.

1129 STARTING MIDDAY CHALLENGE.

1137 SOIL DRUMS 1926-1940, SCR DRUMS 566 & 567
AG 661 AND PPE 434 LOADED FOR FEDERAL
PROPERTY.

1156 MIDDAY COMPLETE.

1307 TEAM 2 DOWN RANGE LEVEL "B" RIDGE
CASTLE HILL FINGER

1338 PPE CHECKS.

1404 PPE CHECKS.

1433 PPE CHECKS.

1513 SOIL DRUMS 1941-1955 FILLED.

1515 COMPOSITE SAMPLE COLLECTED.

1525 TEAM 2 CLEARED PDS

1549 SOIL DRUMS 1941-1955, SCR 566 & 567 LOADED
FOR FEDERAL PROPERTY.

1600 Day Complete

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062
 Delivery Order: TO 0006
 Date: 06 December 2018
 Site Location: 4825 Glenbrook Road

Weather: _____
 partly cloudy 30/42, little wind

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Breyman, Mark	Askew, Thomas	
Castell, Lorna	Heffelfinger, Gerald	Baker, Dawn	
Courtney, Kenneth	Prate, Warren	Bartash, Ian	
Marion, Jediah	Rutana, Steve	Brown, Matthew	
Matter, Phillip	Wright, David	Nguyen, Phuong	
Moon, Dale	Yorkshire, Bart		
Nelms, Bobby		McGill, Andre	
Oien, Joshua			
Rider, Matthew	LIFE STAR	Pettitway, Jeffery	
Rockwell, Margaret	Alfaro, Walter	Wainwright, Leroy	
	Dunnavant, Delany		
Wunschel, Reina			
Wunschel, Scott		CEHNC	
	ACCUPERMIT	Shott, Ken	
	Schmidt, James		
	Williams, Angelo	CENAB	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30
 Continued digging in area 1, filled 30 drums.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
	Berkel ()
	DAVEY ()
	ACCUPERMIT ()
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

[illegible]

PG 94 12-6-18

- 0630 Morning Safety Brief
- 0710 Radio Checks
- 0715 Site Set up
- 0739 Minicams up
- 0758 DAAMS pumps on and monitors Running
- 0830 Site is Set up, Tm 3 Dressing out.
- 0840 Team 3 Down Range level B.
- 0848 VOC Sample Collected.
- 0921 PPE & Monitors Checked, all Good.
- 0950 PPE & Monitors Checked, all OK.
- 1020 Drums 1956 - 1970 Filled, Sending operator out.
- 1030 Tm 3 Processed out of PDS.
- 1105 Drums loaded & Heading for the Fed Site.
- 1115 lunch
- 1145 Tm 1 Dressing OUT.
- 1220 Tm 1 Going Down Range to fill Drums
- 1300 PPE & Monitors Checked, all OK.
- 1335 PPE & Monitors All OK.
- 1410 PPE & Monitor check, all OK.
- 1420 Minicams Reports 25.1 CF, AT Drum Fill area.
- 1424 Second C-pte clear, Team inspected Drums, Nothing Seen.
- 1427 Resumed excavating & Filling Drums.
- 1435 Drums 1971 to 1985 are filled, team will Dig a small Sump to collect water.
- 1452 Sump is complete, team Prepping to take the Composite Sample.
- 1500 Composite Sample Complete, Team Processing out.
- 1508 Tm 1 Clear of PDS. Tm 2 Prepping to load Soil Drums.

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062
 Delivery Order: TO 0006
 Date: 07 December 2018
 Site Location: 4825 Glenbrook Road

Weather:
 37/41 winds 5-15 mph

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Breyman, Mark	Askew, Thomas	
Castell, Lorna		Baker, Dawn	
	Prate, Warren	Bartash, Ian	
Marion, Jedidiah	Rutana, Steve	Brown, Matthew	
		Nguyen, Phuong	
Moon, Dale	Yorkshire, Bart	Manthei, Michael	
Nelms, Bobby		McGill, Andre	
Oien, Joshua		Miller, Don	
Rider, Matthew	LIFE STAR	Pettitway, Jeffery	
Rockwell, Margaret	Alfaro, Walter	Wainwright, Leroy	
	Bailey, Brooke		
Wunschel, Reina			
Wunschel, Scott		CEHNC	
	ACCUPERMIT	Shott, Ken	
	Pulisaroth, Andrew		
	Williams, Angelo	CENAB	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive ops in area 1, 10 drums filled with soil. Relocate 4825/36 boundary fence, relocate downspouting, secure extension cords. Pumped 200 gallons of rainwater from excavation area.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT ()
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

[illegible]

Pg

96 12-7-18

0630 SAFETY BRIEF

0700 RADIO CHECKS.

0748 MINICAMS UP PUMP IN/L

WATER FROM EXCAVATION AREA 1/B

0800 MAMS UP

0815 200 GALS PUMPED FROM AREA 1/B.

0846 TEAM 2 DOWN RANGE LEVEL "B". RIDER

CASTER, ~~RAHNA~~ - BREYMAN

0855 VOC COLLECTED.

0905 MINICAMS REPORTS ALARM FOR

CG 26.3 DRUM FILLING.

0909 2ND CYCLE @ 26.3 FORCE @ DRUM FILLING.

THE TEAM HAS COVERED DRUMS
STARTING TO PROCESS TAPR PDS.

0913 3RD CYCLE 27.6 CG @ DRUM FILLING.

0930 TEAM 2 PROCESSED TAPR PDS.

MINICAMS IS EXCHANGING EQUIPMENT.
FOR DRUM FILLING AREA.

1030 MIDDAY CHALLENGE.

1030 MIDDAY CHALLENGE COMPLETE.

1118 TEAM 1 DOWN RANGE LEVEL "B" ON

BUSCH, RIDERMAN.

1145 PPE CHECKS.

1209 PPE CHECKS.

1234 SOIL DRUMS 1986-1995 FILLED.

1240 COMPOSITE COLLECTED.

1251 TEAM 1 CLEARED PDS.

1412 SOIL DRUMS 1986-1995, PPE 435

LOADED FOR FEDERAL PRIORITY.

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062
 Delivery Order: TO 0006
 Date: 10 December 2018
 Site Location: 4825 Glenbrook Road

Weather: _____
 30/41 overcast, winds 5-15 mph

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Breyman, Mark	Askew, Thomas	
Castell, Lorna	Heffelfinger, Gerald	Bartash, Ian	
Courtney, Kenneth	Prate, Warren	Brown, Matthew	
Marion, Jediah	Rutana, Steve	Framarini, Trevor	
Matter, Phillip	Wright, David	Manthei, Michael	
Moon, Dale	Yorkshire, Bart	McGill, Andre	
Nelms, Bobby		Miller, Don	
Oien, Joshua		Nguyen, Phuong	
Rider, Matthew	LIFE STAR	Pettway, Jeffery	
Rockwell, Margaret	Alfaro, Walter	Wainwright, Leroy	
Schlosser, Ariel	Anderson, Monique		
Wunschel, Scott		CEHNC	
	ACCUPERMIT	Shott, Ken	
	Schmidt, James		
	Williams, Angelo	CENAB	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive ops in area 1, 35 drums filled. Started digging out the north-south retaining wall.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT ()
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

98 12-10-18

0630 SAFETY BRIEF

0700 RADIO CHECKS

0745 PDS UP

0746 MINICAMS UP.

0751 DAMS PUMPS RUNNING.

0818 TEAM 3 DOWN RANGE LEVEL "B" MOON
MARION WRIGHT.

0826 VOC COLLECTED.

0836 PPE CHECKS.

0900 PPE CHECKS.

0918 PPE CHECKS.

0938 PPE CHECKS.

1011 PPE CHECKS

1039 SOIL DRUMS 1996-2015 FILLED.

1048 TEAM 3 CLEARED PDS.

SOIL DRUMS 1996-2010 LOADED FOR
FEDERAL PROPERTY.

1140 MID DAY CHALLENGE.

1153 MID DAY COMPLETE.

1304 TEAM 1 DOWN RANGE LEVEL "B"
OLEN SCHLOSSER, GERT FINGER.

1322 PPE CHECKS.

1345 PPE CHECKS

1403 PPE CHECKS.

1420 PPE CHECKS

1443 PPE CHECKS.

1509 PPE CHECKS.

1519 SOIL DRUMS 2016-2030 FILLED.

1529 COMPOSITE COLLECTED

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062
 Delivery Order: TO 0006
 Date: 11 December 2018
 Site Location: 4825 Glenbrook Road

Weather: _____
 30/41 overcast, 5-10 mph winds

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Breyman, Mark	Askew, Thomas	
Castell, Lorna	Heffelfinger, Gerald	Bartash, Ian	
Courtney, Kenneth	Prate, Warren	Brown, Matthew	
Marion, Jediah	Rutana, Steve	Framarini, Trevor	
Matter, Phillip	Wright, David	Manthei, Michael	
Moon, Dale	Yorkshire, Bart	McGill, Andre	
Nelms, Bobby		Miller, Don	
Oien, Joshua		Nguyen, Phuong	
Rider, Matthew		Pettway, Jeffery	
Rockwell, Margaret	LIFE STAR	Wainwright, Leroy	
Schlosser, Ariel	Alfaro, Walter		
Wunschel, Scott	Dunnavant, Delany		
		CEHNC	
		Shott, Ken	
	ACCUPERMIT		
	Schmidt, James		
	Williams, Angelo	CENAB	
	Martinez, Vincente		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive in area 1 along north-south retaining wall. Located what appears to be Livens projector. EOD called.

End of Day: 1700

SAMPLES COLLECTED: No samples taken today as ordnance item was found, very early in shift.

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
	Berkel ()
	DAVEY ()
	ACCUPERMIT ()
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

At approximately 1050 team 2 locates what is suspected Levins projector on east side of north-south retaining wall. Everybody notified, EOD called. 1640 EOD on site. 1805 EOD departs, no liquid line, no fuzing per X-ray

Instructions given by government personnel:**Activities anticipated for tomorrow:**

PDT call about above mentioned ordnance item.

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg 100 12-11-18
 0630 SAFETY BRIEF
 0700 RADIO CHECKS
 0732 MINICAMS UP PDS UP CASCADE UP
 0800 SOIL DRUMS - 2011-2025, PPE 434 AQ 662
 LOADED FOR FEDERAL PROPERTY.
 0806 DAMPS PUMPS RUNNING.
 0917 SOIL DRUM 2026-2030 LOADED FOR
 FEDERAL PROPERTY, MINICAMS
 RECHARGE.
 0928 RECHARGE COMPLETE.
 0955 TEAM 2 DOWN RANGE LEVEL "B" RIVER
 COUNTRY BREYMAN.
 1002 VOC COLLECTED
 1013 PPE CHECKS.
 1040 PPE CHECKS.
 1150 THE TEAM REPORTS FINDING A
 CYLINDER TYPE OBJECT AT THE FOOTER.
 1110 PICTURES WERE TAKEN THE ITEM
 MITIGATED AND NOTIFICATIONS
 ARE BEING MADE. ALL INSTRUMENTS
 WERE CLEAR.
 1119 TEAM 2 CLEARED PDS.
 1305 RECHARGE DRUM FILLING MINICAMS.
 1319 DRAM FILLING RECHARGE COMPLETE.
 1640 EOB ON SITE.
 1800 THE CYLINDER WAS DETERMINED TO BE
 EMPTY, IT WAS GENTLY RAISED AND
 LEFT ON SITE.
 NEXT GC BOOK.

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062
 Delivery Order: TO 0006
 Date: 12 December 2018
 Site Location: 4825 Glenbrook Road

Weather: _____
 33/42, winds 5-10 mph

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Breyman, Mark	Askew, Thomas	
Castell, Lorna	Heffelfinger, Gerald	Bartash, Ian	
Courtney, Kenneth	Prate, Warren	Brown, Matthew	
Marion, Jediah	Wright, David	Framarini, Trevor	
Matter, Phillip	Yorkshire, Bart	Manthei, Michael	
Moon, Dale		McGill, Andre	
Nelms, Bobby		Miller, Don	
Oien, Joshua		Nguyen, Phuong	
Rider, Matthew		Pettway, Jeffery	
Rockwell, Margaret	LIFE STAR	Wainwright, Leroy	
Schlosser, Ariel	Gumbs Vines, Doreen		
Wunschel, Reina	Dunnivant, Delany		
Wunschel, Scott			
		CEHNC	
	ACCUPERMIT	Shott, Ken	
	Schmidt, James		
	Williams, Angelo	CENAB	
	Martinez, Vicente		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

PDT call reference Livens projector found yesterday, cleared for return to intrusive at 1019 AM. 1031 AM resumed intrusive operations in area 1 at the north-south retaining wall. 18 drums of soil filled. Weighed 100 drums for upcoming HAZ waste shipment.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT ()
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

R

2

12-12-18

0630 SAFETY BRIEF.

0700 RADIO CHECKS.

0807 SCR 569 "LOVINS" TO FCB PROPERTY
FOR HEAD SPACE.

0943 MINICHAMIS UP

0952 DDAMS PUMPS RUNNING.

1000 PDT CALL

1015 PDT GAVE GO AHEAD TO CONTINUE WORK.

1031 TEAM 3 DOWN RANGE LEVEL "B"

MOON, MARION, WRIGHT.

1038 VOC COLLECTED

1052 PPE CHECKS.

1111 PPE CHECKS.

1132 PPE CHECKS.

1155 PPE CHECKS

1219 PPE CHECKS.

1259 TEAM 3 CLEARED PDS

1300 MID DAY CHALLENGE.

1325 MID DAY COMPLETE.

1400 SOIL DRUMS 2031-2045 LOADED

FOR FEDERAL PROPERTY. SCR DRUMS 570571

1420 TEAM 1 DOWN RANGE LEVEL "B"

OJEN, RASCH, HOFFMANN JR.

1445 PPE CHECKS

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062
Delivery Order: TO 0006
Date: 13 December 2018
Site Location: 4825 Glenbrook Road

Weather:
 37/46, winds 5-10 mph

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Breyman, Mark	Askew, Thomas	
Castell, Lorna	Heffelfinger, Gerald	Nguyen, Phuong	
Courtney, Kenneth	Prate, Warren	Bartash, Ian	
Marion, Jedidiah	Rutana, Steve	Brown, Matthew	
Matter, Phillip		Framarini, Trevor	
Moon, Dale	Yorkshire, Bart	Manthei, Michael	
Nelms, Bobby		McGill, Andre	
Oien, Joshua		Miller, Don	
Rider, Matthew	LIFE STAR	Pettitway, Jeffery	
Rockwell, Margaret	Gumbs Vines, Doreen	Wainwright, Leroy	
Schlosser, Ariel	Dunnavant, Delany		
Wunschel, Reina			
Wunschel, Scott		CEHNC	
	ACCUPERMIT	Shott, Ken	
	Martinez, Vicente		
	Williams, Angelo	CENAB	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations in Area 1 along north-south retaining wall, 25 drums filled with soil.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors
 Berkel ()
 DAVEY ()
 ACCUPERMIT ()
 ACI (0)
 CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	<i>To be included if investigation is using CSS protocols</i>
Dig Sheet	Y/N	<i>To be included at least once every week during intrusive investigation</i>
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	<i>To be included weekly during field activities</i>
Property Management Summary	Y/N	<i>Include complete property inventory once every month</i>
Photographs	Y/N	

[illegible]

Pg

4

12-13-18

- 0630 SAFETY BRIEF.
- 0700 RADIO CHECKS.
- 0741 MINICAMS UP.
- 0749 DAAMS PUMPS RUNNING.
- 0811 TEAM 2 DOWN RANGE LEVEL "B"
RIDER, CASTELL, BRUMMAN.
- 0821 VOC COLLECTED.
- 0833 PPE CHECKS.
- 0856 PPE CHECKS.
- 0950 SOIL DRUMS 2049-2055 FILLED.
- 1020 PPE CHECKS.
- 1052 SOIL DRUMS 2056-2060 FILLED.
- 1058 TEAM 2 CLEARED PDS.
- 1100 CONFERENCE CALL.
- 1131 SOIL DRUMS 2045-2060, SER DRUM 572
PPE DRUM 437 LOADED FOR FLOOR
PROPERTY.
- 1132 STARTING MID DAY CHALLENGE.
- 1159 MIDDAY COMPLETE.
- 1245 TEAM 3 DOWN RANGE LEVEL "B"
MOON, WUNSCHER, HEFFELINER.
- 1317 PPE CHECKS.
- 1341 PPE CHECKS.
- 1409 PPE CHECKS.

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062
 Delivery Order: TO 0006
 Date: 14 December 2018
 Site Location: 4825 Glenbrook Road

Weather: _____
 43/47 overcast, drizzle, 5-10 mph winds

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Breyman, Mark	Askew, Thomas	
Castell, Lorna	Heffelfinger, Gerald	Bartash, Ian	
Courtney, Kenneth	Prate, Warren	Brown, Matthew	
Marion, Jediah	Yorkshire, Bart	Framarini, Trevor	
Matter, Phillip		Manthei, Michael	
Moon, Dale		McGill, Andre	
Nelms, Bobby		Miller, Don	
Oien, Joshua		Nguyen, Phuong	
Rider, Matthew		Pettway, Jeffery	
Rockwell, Margaret	LIFE STAR	Wainwright, Leroy	
Schlosser, Ariel	Alfaro, Walter		
Wunschel, Reina	Brooke, Bailey		
Wunschel, Scott			
		CEHNC	
	ACCUPERMIT	Shott, Ken	
	Vargas, Bustaro		
	Williams, Angelo	CENAB	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations clearing soil from front and back sides of north-south retaining wall. Pulled down north-south retaining wall and broke into very large pieces so we could move it.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT ()
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

[illegible]

D
6

12-14-18

0630 SAFETY BRIEF.

0700 RADIO CHECKS.

0741 MINI CAMS UP

0753 DAAMS PUMPS RUNNING.

0807 SOIL DRUMS 2061-2073 LOADED

0824 TM1 enter in level B, drum filling, 2074-2088

0913 PPE & Monitor check, all ok

0950 PPE & Monitor Check Complete.

1029 PPE & Monitor check Complete.

1053 Soil Drums are complete team prepping to take
Sample & Secure Drum lids.

1104 Composite Sample Complete.

1112 Team 1 clear of the PDS.

1120 loading Soil drums onto truck for transport.

1145 Lunch.

1215 Tees setting up to try and Break wall

1258 TM 2 in, level B to try & Break wall.

1400 The wall has been torn down, team heading to
the PDS.1405 TM 2 clear of PDS, Teams are performing
end of week clean up & maint.

1700 Day Complete.

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062
 Delivery Order: TO 0006
 Date: 17 December 2018
 Site Location: 4825 Glenbrook Road

Weather: _____
 43/47 5-10mph winds

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Breyman, Mark	Ashew, Tom	
Castell, Lorna	Heffelfinger, Gerald	Bartash, Ian	
Courtney, Kenneth	Prate, Warren	Brown, Matthew	
Marion, Jedidiah	Yorkshire, Bart	Framarini, Trevor	
Matter, Phillip	Rutana, Steve	Miller, Don	
Moon, Dale		Nguyen, Phuong	
Nelms, Bobby		Pettway, Jeffery	
Oien, Joshua		Tucker, Robin	
Rider, Matthew	LIFE STAR	Wainwright, Leroy	
Rockwell, Margaret	Alfaro, Walter	Satchell, Doyle	
Schlosser, Ariel	Gumbs Vines, Doreen	Smith, Ethan	
Wunschel, Reina			
Wunschel, Scott		CEHNC	
	ACCUPERMIT	Shott, Ken	
	Overton, Robert		
	Williams, Angelo	CENAB	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Pumped 2150 gallons of water, begin jackhammering concrete wall and loading it out in rolloffs.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT ()
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

7

12-17-18

0630 SAFETY BRIEF

0700 RADIO CHECKS

0800 PUMPING WATER FROM AREA 1/5
EXCAVATION.

1117 BREAKING CONCRETE RETAINING
WALL W/ HYDRAULIC HAMMER

1700 SECURED

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062
Delivery Order: TO 0006
Date: 18 December 2018
Site Location: 4825 Glenbrook Road

Weather:
 30/44 light winds

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Breyman, Mark	Askew, Thomas	
Castell, Lorna	Heffelfinger, Gerald	Bartash, Ian	
Courtney, Kenneth	Prate, Warren	Brown, Matthew	
Marion, Jedidiah	Yorkshire, Bart	Framarini, Trevor	
Matter, Phillip	Rutana, Steve	Satchell, Doyle	
Moon, Dale	Wright, David	Tucker, Robin	
Nelms, Bobby		Miller, Don	
Oien, Joshua		Nguyen, Phuong	
Rider, Matthew	LIFE STAR	Pettitway, Jeffery	
Rockwell, Margaret	Alfaro, Walter	Wainwright, Leroy	
Schlosser, Ariel	Gumbs Vines, Doreen		
Wunschel, Reina		CEHNC	
Wunschel, Scott		Shott, Ken	
	ACCUPERMIT		
	Overton, Robert		
	Williams, Angelo	CENAB	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive operations, instead breaking up concrete, cutting rebar and loading up in a rolloff.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
	Berkel ()
	DAVEY ()
	ACCUPERMIT ()
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

1. Pg 8

12-18-18

0630 SAFETY BRIEF

0700 RADIO CHECKS

0800 BUSTING CONCRETE/CUTTING REBAR

1700 SECURED

[Handwritten signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062
 Delivery Order: TO 0006
 Date: 19 December 2018
 Site Location: 4825 Glenbrook Road

Weather: _____
 36/48 southern winds 5-10 mph

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Breyman, Mark	Askew, Thomas	
Castell, Lorna	Heffelfinger, Gerald	Bartash, Ian	
Courtney, Kenneth	Prate, Warren	Brown, Matthew	
Marion, Jediaiah	Yorkshire, Bart	Doyle, Satchell	
Matter, Phillip	Wright, David	Framarini, Trevor	
Moon, Dale	Rutana, Steve	Miller, Don	
Nelms, Bobby		Pettway, Jeffery	
Oien, Joshua		Smith, Eathen	
Rider, Matthew	LIFE STAR	Tucker, Robin	
Rockwell, Margaret	Gumbs Vines, Doreen	Wainwright, Leroy	
Schlosser, Ariel	Robinson, Omar		
Wunschel, Reina			
Wunschel, Scott		CEHNC	
	ACCUPERMIT	Shott, Ken	
	Martinez, Vicinte		
	Williams, Angelo	CENAB	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive operations today. Continued loading out concrete, 1 rolloff removed. 211 drums weighed for upcoming HAZMAT shipment.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT ()
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg
9

12-19-18

0630 SAFETY BRIEF

0700 RADIO CHECKS

1700 END OF DAY

[Signature]

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062
 Delivery Order: TO 0006
 Date: 20 December 2018
 Site Location: 4825 Glenbrook Road

Weather: _____
 36/45 eastern winds @ 5-10 mph

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Breyman, Mark	Askew, Thomas	
Castell, Lorna	Heffelfinger, Gerald	Bartash, Ian	
Courtney, Kenneth	Prate, Warren	Doyle, Satchell	
Marion, Jediaiah	Yorkshire, Bart	Framarini, Trevor	
Matter, Phillip	Rutana, Steve	Manthei, Michael	
Moon, Dale	Wright, David	Miller, Don	
Nelms, Bobby		Pettway, Jeffery	
Oien, Joshua		Tucker, Robin	
Rider, Matthew		Wainwright, Leroy	
Rockwell, Margaret	LIFE STAR		
Schlosser, Ariel			
Wunschel, Reina			
Wunschel, Scott			
		CEHNC	
	ACCUPERMIT	Shott, Ken	
	Martinez, Vicente		
	Williams, Angelo	CENAB	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive operations today. Weighed last of HAZMAT drums, 79 of them. Set-up silt fence and hay bales along the truck gate. Police call around Federal Property and securing all property for the holidays.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors

Contractors

Berkel ()
DAVEY ()
ACCUPERMIT ()
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

10

12-20-18

0630 SAFETY BRIEF. NEW HORN BRIDGE

0710 RAPID CHECKS

1200 SECURED

Very
L.

SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062
 Delivery Order: TO 0006
 Date: 21 December 2018
 Site Location: 4825 Glenbrook Road

Weather: _____
 45/64 winds 5-20 mph

Personnel on Site

PARSONS	ZES	ECBC	
Busch, Matthew	Breyman, Mark		
Castell, Lorna	Heffelfinger, Gerald		
Courtney, Kenneth	Prate, Warren		
Marion, Jedidiah	Yorkshire, Bart		
Matter, Phillip	Rutana, Steve		
Moon, Dale	Wright, David		
Oien, Joshua			
Rider, Matthew	LIFE STAR		
Rockwell, Margaret			
Schlosser, Ariel			
Wunschel, Reina			
Wunschel, Scott		CEHNC	
	ACCUPERMIT		
		CENAB	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Police call around 4825, ensure all heat trace lines are energized and all hoses drained. Begin holiday break.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
_____	Berkel ()
_____	DAVEY ()
_____	ACCUPERMIT ()
_____	ACI (0)
_____	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	
