

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 04 January 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_

**Personnel on Site**

PARSONS	ZES	ECBC	
Busch, Matthew	Breyman, Mark		
Castell, Lorna	Heffelfinger, Gerald		
Courtney, Kenneth	Prate, Warren		
Marion, Jedidiah	Yorkshire, Bart		
Matter, Phillip	Rutana, Steve		
Moon, Dale	Wright, David		
Nelms, Bobby			
Oien, Joshua			
Rider, Matthew			
Rockwell, Margaret	<b>LIFE STAR</b>		
Schlosser, Ariel			
Wunschel, Reina			
Wunschel, Scott			
		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>		
	Overton, Robert		
	Williams, Angelo	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information  
 \_\_\_\_\_  
 \_\_\_\_\_

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
_____	Berkel ( )
_____	DAVEY ( )
_____	ACCUPERMIT ( )
_____	ACI (0)
_____	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	





2  
12

1-7-19

0630 SAFETY BRIEF

0700 RADIO CHECKS

0738 DAMS PUMPS IN PLACE & RUNNING.

0822 MINICAMS UP.

0828 TEAM 1 DOWN RANGE. REMOVING CONCRETE WALL.

0901 PPE CHECKS.

1031 TEAM 1 CHARGED PDS

1215 STARTING MIDDAY

1246 MIDDAY COMPLETE

1310 BREAKING CONCRETE WALL

WITH HYDRAULIC HAMMER.

1700 SECURED

BTJ  
Sh



[illegible]

P  
13

1-8-19

0630 SAFETY BRIEF

0700 RADIO CHECKS

0715 PDS UP

0730 SETUP TORM IN. MEDICAL IN DRIVE.

0705 MINICAMS UP.

0839 PUMPED 850 GALS FROM AREA 1.

0902 TEAM 3 DOWN RANGE LEVEL "B"

MOON, WUNSCHER, WRIGHT.

1025 VOC COLLECTED. DIGGING AREA 1/B.

1055 PPE CHECKS COMPLETE.

1117 PPE CHECKS.

1142 SOIL BORINGS 2089-2093 FILLED.

1155 TEAM 3 CLEARED PDS.

1157 STARTING MIDDAY CLEANING

1206 MINICAMS BACK UP

1320 TEAM 1 DOWN RANGE LEVEL "B"

1350 PPE CHECKS.

1424 PPE CHECKS.

1500 SOIL BORINGS 2094-2107 FILLED.

1519 COMPOSITE SAMPLE COLLECTED.

1530 TEAM 1 CLEARED PDS.

1546 STARTING END OF DAY CHECKS.

1700 SECURED

BUTLER

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 9 January 2019  
 Site Location: 4825 Glenbrook Road

Weather:  
 44/42 winds 5-20

**Personnel on Site**

PARSONS	ZES	ECBC	
Castell, Lorna	Breyman, Mark	Askew, Tom	
Christensen, James	Heffelfinger, Gerald	Caldwell, Jeff	
Courtney, Kenneth	Prate, Warren	Doyle Jr, Satchell	
Marion, Jedidiah	Yorkshire, Bart	Manthei, Micheal	
Matter, Phillip	Rutana, Steve	McClellan, Dale	
Moon, Dale	Wright, David	Miller, Don	
Nelms, Bobby		Perkins, Stephan	
Rockwell, Margaret		Shavers, Dedrick	
Schlosser, Ariel	<b>LIFE STAR</b>	Tucker, Willie	
Wunschel, Reina	Alfaro, Walter	Wainwright, LeRoy	
	Gumbs Vines, Doreen		
		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Overton, Robert		
	Williams, Angelo	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Moved excavation operation to slope area to remove last of retaining wall. 10 soil drums filled.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

[illegible]



Pg

14 1-9-19

0630 SAFETY BRIEF

0700 RADIO CHECKS

0748 MINICAMS UP

0813 SOIL DRUMS 2089-2103 LOADED  
FOR FEDERAL PROPERTY.0905 SOIL DRUMS 2104-2107, SCR DRUMS 576-578  
LOADED FOR FEDERAL PROPERTY.1000 PUMPING WATER FROM AREA 1/E  
EXCAVATION

1105 STARTING MID DAY CHALLENGE

1135 MID DAY COMPLETE

1220 MOON, MARIAH WRIGHT COVER "B"

1252 VOC COLLECTED

1316 PPE CHECKS

1355 PPE CHECKS

1417 SOIL DRUMS 2108-2117 FILLED

1421 COMPOSITE SAMPLE COLLECTED

1430 MOON, MARIAH, WRIGHT COVERED PDS

1524 SOIL DRUMS 2108-2117, PPE DRUMS 440/441  
LOADED FOR FEDERAL PROPERTY.

1700 SECURED

# SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 10 January 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 27/39 winds 5-25 cloudy

## Personnel on Site

PARSONS	ZES	ECBC	
Castell, Lorna	Breyman, Mark	Askew, Tom	
Christensen, James	Heffelfinger, Gerald	Caldwell, Jeff	
Courtney, Kenneth	Prate, Warren	Doyle Jr, Satchell	
Marion, Jedidiah	Yorkshire, Bart	Manthei, Micheal	
Matter, Phillip	Rutana, Steve	McClellan, Dale	
Moon, Dale	Wright, David	Miller, Don	
Nelms, Bobby		Perkins, Stephan	
Oien, Joshua		Shavers, Dedrick	
Rider, Matthew	<b>LIFE STAR</b>	Tucker, Willie	
Rockwell, Margaret	Gumbs Vines, Doreen	Wainwright, LeRoy	
Schlosser, Ariel	Haupt, Calvin		
Wunschel, Reina			
		<b>CEHNC</b>	
		Boles, Judson	
	<b>ACCUPERMIT</b>		
	Overton, Robert		
	Williams, Angelo	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30  
 Digging out last section of retaining wall, 38 drums filled.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information  
 \_\_\_\_\_  
 \_\_\_\_\_

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



[illegible]

Pg

15 1-10-19

0630 SAFETY BRIEF

0700 RADIO CHECKS

0747 MINICAMS UP

0700 DAMS PUMPS RUNNING.

0833 TEAM 2 DOWN RANGE LEVEL B RIDER,  
CASTLE, BOYMAN.

0846 VOC COLLECTED.

0911 PPE CHECKS.

1029 PPE CHECKS.

1100 SOIL DRUMS 2118-2137 FILLED.

CONFERENCE CALL

1110 TEAM 2 CLEARED PD3.

STARTING MID DAY CHALLENGE

1142 MID DAY COMPLETE.

1158 SOIL DRUMS 2118-2132 LOADED FOR  
FEDERAL PROPERTY.1246 TEAM 1 DOWN RANGE LEVEL B -  
BIGW, DURNING, HOFFER, FINLER.

1317 PPE CHECKS.

1400 PPE CHECKS.

1425 SOIL DRUMS 2138-2147 FILLED.

SOIL DRUMS 2138-2147 LOADED FOR  
FEDERAL PROPERTY.

1419 SOIL DRUMS 2148-2155 FILLED

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 11 January 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 25/39 5-15 overcast

**Personnel on Site**

PARSONS	ZES	ECBC	
Castell, Lorna	Breyman, Mark	Askew, Tom	
Christensen, James	Heffelfinger, Gerald	Caldwell, Jeff	
Courtney, Kenneth	Prate, Warren	Doyle Jr, Satchell	
Marion, Jedidiah	Yorkshire, Bart	Manthei, Micheal	
Matter, Phillip	Rutana, Steve	McClellan, Dale	
Moon, Dale	Wright, David	Miller, Don	
Nelms, Bobby		Perkins, Stephan	
Oien, Joshua		Tucker, Willie	
Rider, Matthew		Wainwright, LeRoy	
Rockwell, Margaret	<b>LIFE STAR</b>		
Schlosser, Ariel	Brooke, Bailey		
Wunschel, Reina	Dunnavant, Delany		
		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Martinez, Vicente		
	Williams, Angelo	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

30 soil drums filled today.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



Pg

17 1-11-19

0630 SAFETY BRIEF

0700 RADIO CHECKS

0734 MINICAMS UP.

0802 DAPMS PUMPS RUNNING.

0810 SOIL DRUMS 2148-2155 LOADED FOR  
FEDERAL PROPERTY.

0837 TEAM 2 DOWN RANGE LEVEL "B".

RIDER, CASTER, BRAYMAN.

0850 VOC COLLECTED.

0911 PPE CHECKS.

1000 SOIL DRUMS 2156-2165 FILLED.

1018 SOIL DRUMS 2156-2165 LOADED FOR  
FEDERAL PROPERTY.

1019 PPE CHECKS.

1102 SOIL DRUMS 2166-2175 FILLED.

1108 TEAM 2 HEARD PDS.

SOIL DRUMS 2166-2175 LOADED FOR  
FEDERAL PROPERTY.

1133 STARTING MIDDAY CHARGE.

1143 MIDDAY COMPLETE

1239 TEAM 3 DOWN RANGE LEVEL "B".

MATT WUNSCHER, WRIGHT.

1321 PPE CHECKS.

1405 SOIL DRUMS 2176-2185 FILLED

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 15 January 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 21/38 overcast

**Personnel on Site**

PARSONS	ZES	ECBC	
Castell, Lorna	Breyman, Mark	Askew, Tom	
Christensen, James	Heffelfinger, Gerald	Caldwell, Jeff	
Courtney, Kenneth	Prate, Warren	Doyle Jr, Satchell	
Marion, Jediaiah	Yorkshire, Bart	Manthei, Micheal	
Matter, Phillip	Rutana, Steve	McClellan, Dale	
Moon, Dale	Wright, David	Miller, Don	
Nelms, Bobby		Shavers, Dedrick	
Oien, Joshua		Tucker, Robin	
Rider, Matthew		Tucker, Willie	
Rockwell, Margaret	<b>LIFE STAR</b>	Wainwright, LeRoy	
Schlosser, Ariel	Brooke, Bailey		
Wunschel, Reina	Alfaro, Walter		
Wunschel, Scott			
		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Gustauo, Vargas		
	Schmidt, James	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 8:30

NON INTRUSIVE 2 hour delayed per OPM. Pumped 2100 gallons of water. Shoveled snow all over site.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information  
 \_\_\_\_\_  
 \_\_\_\_\_

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
_____	Berkel ( )
_____	DAVEY ( )
_____	ACCUPERMIT ( )
_____	ACI (0)
_____	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



72

19 1-15-19

0830 SAFETY BRIEF - 2 Hr Delay OPM.

1-14-19 OPM CLOSED.

0900 REMOVING SNOW

0952 MINICAMS UP

1051 SOIL DRUMS 2176-2185 LOADED  
FOR FEDERAL PROPERTY.

1115 STOPPING MID DAY CHALLENGE

1143 MID DAY COMPLETE

1241 PUMPING WATER FROM AREA

~~WB~~

1700 SECURED

*[Handwritten signature/initials]*







Pg  
20

1-16-19

0630 SAFETY BRIEF

0700 RADIO CHECKS. TRAFFIC  
SIGNS IN PLACE.

0750 MINICAMS UP & DRAMS PUMPS  
RUNNING.

0828 TEAM 2 DOWN RANGE LEVEL "B"  
RIBOX, CACIZU PROGRAM.

0840 VOC COLLECTED.

0858 PPE CHECKS.

0937 SOIL DRAMS 2186-2195 FILLED.

1013 SOIL DRAMS 2186-2195 LOADED  
FOR FEDERAL PROPERTY.

1053 SOIL DRAMS 2196-2205 FILLED

1115 SOIL DRAMS 2196-2205 LOADED  
FOR FEDERAL PROPERTY.

1133 STARTING MIDDAY CHALLENGE

1154 MIDDAY CHALLENGE COMPLETE.

1238 MON MARRION HAFELFINGER DOWN  
RANGE LEVEL "B".

1319 PPE CHECKS

1402 SOIL DRAMS 2206-2215 FILLED & LOADED  
FOR FEDERAL PROPERTY.

1434 SOIL DRAMS 2216-2221 FILLED

1443 PPE CHECKS



[illegible]

2-27-79

0630 SAFETY BRIEF.

0700 RADIO CHECKS.

0749 MINICAMS UP

0800 DAMS PUMPS RUNNING.

0808 MONITORS IN PLACE

0830 TEAM 1 DOWN RANGE LEVEL "B" 210M

SCHLOSSER HEFFELINGER

0840 VOC COLLECTED

0918 PPE CHECKS

0950 SOIL DRUMS 2228-2233 FILLED

1024 SOIL DRUMS 2234-2239 FILLED.

1030 PPE CHECKS

1105 SOIL DRUMS 2240-2245 FILLED.

1107 SOIL DRUMS 2228-2239, H<sub>2</sub>O DRUM 664

AND PPE DRUM 443 LOADED FOR

FEDERAL PROPERTY.

1133 STARTING MIDDAY CHALLENGE.

1148 MIDDAY COMPLETE

1313 TEAM 2 DOWN RANGE LEVEL "B"

RIDER, CASTLE, BREYMAN.

1355 SOIL DRUMS 2240-2251 FILLED.

1425 SOIL DRUMS 2240-2251 LOADED

FOR FEDERAL PROPERTY.

1439 SOIL DRUMS 2252-2257 FILLED

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 18 January 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 32/46 winds 5-10 mph

**Personnel on Site**

PARSONS	ZES	ECBC	
Castell, Lorna	Breyman, Mark	Askew, Tom	
Christensen, James	Heffelfinger, Gerald	Caldwell, Jeff	
Courtney, Kenneth	Prate, Warren	Doyle Jr, Satchell	
Marion, Jedidiah	Yorkshire, Bart	Manthei, Micheal	
Matter, Phillip	Rutana, Steve	McClellan, Dale	
	Wright, David	Miller, Don	
Nelms, Bobby		Shavers, Dedrick	
Oien, Joshua		Tucker, Robin	
Rider, Matthew	<b>LIFE STAR</b>	Tucker, Willie	
Rockwell, Margaret	Brooke, Bailey	Wainwright, LeRoy	
Schlosser, Ariel	Dunnavant, Delany		
Wunschel, Reina			
Wunschel, Scott		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Martinez, Vicente		
	Schmidt, James	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Hand dug 2 large anomollies that were underneath retaining wall, rebar found. Pumped 2150 gallons of water. Began breaking concrete after wall was moved, magged underneath and anomollies hand dug.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

**Problems encountered/resolutions:**

**Instructions given by government personnel:**

Told that we must break concrete and cut rebar in LEVEL B per Huntsville ACOE, relayed by Sean Buckley

**Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 22 January 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 16/32, south winds 5-10 mph

**Personnel on Site**

PARSONS	ZES	ECBC	
Castell, Lorna	Breyman, Mark	Askew, Tom	
	Heffelfinger, Gerald	Caldwell, Jeff	
Courtney, Kenneth	Prate, Warren	Edwards, Charles	
Marion, Jediah	Yorkshire, Bart	Mantei, Michael	
Matter, Phillip	Rutana, Steve	McClellan, Dale	
Moon, Dale	Wright, David	Miller, Don	
Nelms, Bobby		Shavers, Dedrick	
Oien, Joshua		Tucker, Robin	
Rider, Matthew	<b>LIFE STAR</b>	Tucker, Willie	
Rockwell, Margaret	Alfaro, Walter	Wainwright, LeRoy	
Schlosser, Ariel	Jackson, Mark		
Wunschel, Reina			
Wunschel, Scott		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Schmidt, James		
	Williams, Angelo	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Non-intrusive. Breaking up concrete and cutting rebar in LEVEL B. HAZMAT shipment of over 200 drums and over 15000 gallons of water.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

**Problems encountered/resolutions:**

Excavators frozen to the ground, cleaned tracks and parked on blocks for following day. Diesel engines were also difficult to start, no cure when working in low temperatures.

**Instructions given by government personnel:**

Told we must break concrete and cut rebar in level B by Huntsville ACOE, relayed by Sean Buckley.

**Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

25 1-22-19

0630 SAFETY BRIEF

0700 RADIO CHECKS.

0800 MINICAMS UP

0830 JARVIS PUMPS RUNNING

0854 LEVEL "B" DOWN RANGE TEAM 1

RIDER, CASTLE, HOFFERFINGER

BREAKING CONCRETE WALL WITH BRANCH  
HAMMER.

0910 HOFFERFINGER CLEARED PDS. THE

EXCAVATOR IS FROZEN TO THE GROUND.

THE TEAM IS HAND CUTTING REBAR.

0936 RIDER AND CASTLE CLEARED PDS

1115 STARTING MIDDAY CHALLENGE.

1133 MIDDAY CHALLENGE COMPLETE

1203 TEAM 3 DOWN RANGE LEVEL "B"

MOON, WUNSCHER, WRIGHT.

1247 PPE CHECKS


1324 PPE CHECKS

1400 CLEARED PDS. "WRIGHT"

1449 PPE CHECKS.

1505 TEAM 3 CLEARED PDS.

1700 SECURED





## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 23 January 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 57/48 partly cloudy, rain late in PM.

**Personnel on Site**

PARSONS	ZES	ECBC	
Castell, Lorna	Breyman, Mark	Askew, Tom	
Christensen, James	Heffelfinger, Gerald	Caldwell, Jeff	
Courtney, Kenneth	Prate, Warren	Edwards, Charles	
Marion, Jedidiah	Yorkshire, Bart	Mantei, Michael	
Matter, Phillip	Rutana, Steve	McClellan, Dale	
Moon, Dale	Wright, David	Miller, Don	
Nelms, Bobby		Shavers, Dedrick	
Oien, Joshua		Tucker, Robin	
Rider, Matthew	<b>LIFE STAR</b>	Tucker, Willie	
Rockwell, Margaret	Alfaro, Walter	Wainwright, LeRoy	
Schlosser, Ariel	Gumbs Vines, Doreen		
Wunschel, Reina			
Wunschel, Scott		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Schmidt, James		
	Williams, Angelo	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Non-intrusive, loading out concrete into rolloff. Pumped 2050 gallons of water.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

P  
26

1-23-19

0630 SAFETY BRIEF

0700 RADIO CHECKS

0730 MINICAMS UP

0746 PUMPING WATER

0930 DAMS PUMPS RUNNING

1129 STARTING MIDDAY CHALLENGE

1142 MIDDAY COMPLETE

1247 TEAM 1 DOWN ROWLE LOVER "B"

DIEN, SCHLOSSER, HOFFEELINGER

LOADING CONCRETE INTO ROWLEFF.


1418 HOFFEELINGER CLEARED PDS.

ROLL 27994 IS FULL

1430 TEAM 1 CLEARED PDS.

1500 ROWLEFF 27994 OFF SITE

1700 SECURED

A handwritten signature in dark ink, possibly reading "R. J. [unclear]", is written across the lower half of the page. A long, thin diagonal line is drawn from the bottom left towards the center of the page, passing over the signature.

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 24 January 2019  
 Site Location: 4825 Glenbrook Road

Weather:  
 34/58 rain

**Personnel on Site**

PARSONS	ZES	ECBC	
Castell, Lorna	Breyman, Mark	Askew, Tom	
Christensen, James	Heffelfinger, Gerald	Caldwell, Jeff	
Courtney, Kenneth	Prate, Warren	Edwards, Charles	
Marion, Jedidiah	Yorkshire, Bart	Mantei, Michael	
Matter, Phillip	Rutana, Steve	McClellan, Dale	
Moon, Dale	Wright, David	Miller, Don	
Nelms, Bobby		Shavers, Dedrick	
Oien, Joshua		Tucker, Robin	
Rider, Matthew	<b>LIFE STAR</b>	Tucker, Willie	
Rockwell, Margaret	Gumbs Vines, Doreen	Wainwright, LeRoy	
Schlosser, Ariel	Haupt, Calvin		
Wunschel, Reina			
Wunschel, Scott		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Williams, Angelo		
	Schmidt, James	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Non-intrusive. One team leader OSHA physical. Moved construction fence and restaked new fence line, removed electrical junction box from 4825/35 property line fence and relocated it farther uphill. Removed the ramp in front of PDS and bladed away the gravel that has built up there. Set up new EZ with monitors in place and then rain picked up significantly causing early dismissal at 11AM.

End of Day: 1100

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

27

1-24-19

0630 SAFETY BRIEF

0700 RADIO CHECKS.

0743 MINICAMS UP.

1100 SITE SUSPENDED OPERATIONS DUE  
TO HEAVY RAIN. WEEKLY CONFERENCE  
CALL

1130 POT CALL TO DISCUSS PPE SIGN GRADE.

1300 DAY COMPLETE

*[Handwritten signature]*

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 25 January 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 22/37 cold and breezy, 5-20 mph winds

**Personnel on Site**

PARSONS	ZES	ECBC	
Castell, Lorna	Breyman, Mark	Askew, Tom	
Christensen, James	Heffelfinger, Gerald	Caldwell, Jeff	
Courtney, Kenneth	Prate, Warren	Edwards, Charles	
Marion, Jediah	Yorkshire, Bart	Mantei, Michael	
Matter, Phillip	Rutana, Steve	McClellan, Dale	
Moon, Dale	Wright, David	Miller, Don	
		Shavers, Dedrick	
Oien, Joshua		Tucker, Robin	
Rider, Matthew		Tucker, Willie	
Rockwell, Margaret	<b>LIFE STAR</b>	Wainwright, LeRoy	
Schlosser, Ariel	Brooke, Bailey		
Wunschel, Reina	Dunnavant, Delany		
Wunschel, Scott			
		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Overton, Robert		
	Schmidt, James	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive. Surveyor on site marking boundaries and upcoming dig areas. Pumped 5500 gallons of water out of lower excavation. Filled 15 drums with soil from area A/B where retaining wall stood.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

**Problems encountered/resolutions:**

Problem finding area for team leader to observe the excavation. Solution: dug steps into the soil so we can walk to upper area of area A to observe excavations.

**Instructions given by government personnel:****Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	





PG 28

1-25-19

0630 Morning Safety Briefing.

0700 Radio Checks

0800 Surveyor on site to lay in area 1, 3, 4 &amp; 5.

0845 Site Personnel pumping water. <sup>Project</sup> Site Manager is on site working w/ site manager on a path forward in area 1 & 6.

1040 Begin Midday Challenge / lunch Break.

1130 Team setting up ~~up~~ for Intrusive operations.

1217 Tm 2 Down range to excavate Soil.

1235 Team Beginning to excavate. Moving Gravel &amp; Grass.

1253 Collecting VOC Sample.

1307 PPE &amp; Monitors checked &amp; OK.

1355 PPE &amp; Monitors checked &amp; OK.

1432 Drums 2258- 2272 complete, operator moving to PDS.

1437 Composite Sample Complete.

1450 Team going to PDS.

1454 Team clear of PDS, Personnel Pulling Monitors.

1500 End of week clean up.

1700 Day Complete.

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 28 January 2019  
 Site Location: 4825 Glenbrook Road

Weather:  
 32/39, 5-10 winds

**Personnel on Site**

PARSONS	ZES	ECBC	
Castell, Lorna	Breyman, Mark	Askew, Tom	
Christensen, James	Heffelfinger, Gerald	Crawford, Stephen	
Courtney, Kenneth	Prate, Warren	Edwards, Charles	
Marion, Jedidiah	Yorkshire, Bart	Mantei, Michael	
Matter, Phillip	Rutana, Steve	McClellan, Dale	
Moon, Dale	Wright, David	Miller, Don	
Nelms, Bobby		Phuong, Nguyen	
Oien, Joshua		Shavers, Dedrick	
Rider, Matthew		Tucker, Willie	
Rockwell, Margaret	<b>LIFE STAR</b>	Wainwright, LeRoy	
Schlosser, Ariel	Alfaro, Walter		
Wunschel, Reina	Robinson, Omar		
Wunschel, Scott			
		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Williams, Angelo		
	Schmidt, James	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive ops in Northeast corner of Area A. 42 drums of soil filled today. Repaired downspout on 4835 which had fallen off.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	





P  
29

1-28-19

0630 SAFETY BRIEF

0700 RADIO CHECKS

0753 MINI CAMS UP

0803 DAPMS PUMPS RUNNING

0841 SOIL DRUMS 2258-2272, SCR DRUM 579

PPE DRUMS 443-444 LOADED FOR  
FEDERAL PROPERTY.

0905 TEAM 3 DOWN RANGE LEVEL "B" MICH  
MARTIN WRIGHT.

0913 VOC COLLECTED

0936 PPE CHECKS.

1006 PPE CHECKS

1055 TEAM 3 CLEARED PDS. SOIL DRUMS 2275-2287

1150 STARTING MID DAY CHANGING

1210. MID DAY COMPLETE.

1231 TEAM 1 DOWN OILN. SCHLOSSER. EVERY MAN  
LEVEL "B"

1316 PPE CHECKS.

1343 PPE CHECKS

1431 SOIL DRUMS 2288-2307 FILLED.

1515 SOIL DRUMS 2308-2314 FILLED

1529 COMPOSITE SAMPLE COMPLETED

1535 TEAM 1 CLEARED PDS

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 29 January 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 20/40 Rain, winds 5-10

**Personnel on Site**

PARSONS	ZES	ECBC	
Castell, Lorna	Breyman, Mark	Askew, Tom	
Christensen, James	Heffelfinger, Gerald	Crawford, Stephen	
Courtney, Kenneth	Prate, Warren	Edwards, Charles	
Marion, Jediah	Yorkshire, Bart	Mantei, Michael	
Matter, Phillip	Rutana, Steve	McClellan, Dale	
Moon, Dale	Wright, David	Miller, Don	
Nelms, Bobby		Nguyen, Phuong	
Oien, Joshua		Shavers, Dedrick	
Rider, Matthew		Tucker, Willie	
Rockwell, Margaret	<b>LIFE STAR</b>	Wainwright, LeRoy	
Schlosser, Ariel	Alfaro, Walter		
Wunschel, Reina	Jackson, Mark		
Wunschel, Scott			
		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Williams, Angelo		
	Schmidt, James	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive in NE corner of Area A. 28 drums filled, snow came into area early sent teams home at 1400 as the roads were getting hazardous to drive on. 2550 gallons of water pumped out of excavation.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information  
 \_\_\_\_\_  
 \_\_\_\_\_

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
_____	Berkel ( )
_____	DAVEY ( )
_____	ACCUPERMIT ( )
_____	ACI (0)
_____	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



Pg

31 1-29-19

- 0630 SAFETY BRIEF.
- 0700 RADIO CHECKS, TRAFFIC IN PLACE
- 0739 MINICAMS UP
- 0819 DADMS PUMP
- 0831 SOIL DRUMS 2288-2302 LOADED FOR FEDERAL PROPERTY.
- 0853 TEAM 2 DOWN RANGE LEVEL "B" RIDER, ~~SCHEISSER~~ BROYMAN. CASTELL
- 0845 VOC COLLECTED.
- 0910 PPE CHECKS.
- 0923 SOIL DRUMS 2303-2314 AND AQ DRUM 665 LOADED FOR FEDERAL PROPERTY.
- 1017 PUMPING WATER FROM ARE ~~66~~
- 1032 SOIL DRUMS 2315-2329 FILLED PPE CHECKS.
- 1102 SOIL DRUMS 2330-2334 FILLED.
- 1125 STARTING MID DAY CATCHOVCA
- 1146 MID DAY COMPLETE.
- 1229 TEAM 3 DOWN RANGE LEVEL "B" MORN WUNSCHER, WILGAT.
- 1301 SOIL DRUMS 2315-2329 1020 FOR FED PROPERTY
- 1328 COMPOSITE SAMPLE COLLECTED.
- 1329 SOIL DRUMS 2335-2342 - FILLED.
- 1532 TEAM 3 CLEARED PDS.



## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 30 January 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 24/34 breezy, increasingly gusty winds.

**Personnel on Site**

PARSONS	ZES	ECBC	
Castell, Lorna	Breyman, Mark	Askew, Tom	
Christensen, James	Heffelfinger, Gerald	Crawford, Stephen	
Courtney, Kenneth	Prate, Warren	Edwards, Charles	
Marion, Jedidiah	Yorkshire, Bart	Mantei, Michael	
Matter, Phillip	Rutana, Steve	McClellan, Dale	
Moon, Dale	Wright, David	Miller, Don	
Nelms, Bobby		Nguyen, Phuong	
Oien, Joshua		Shavers, Dedrick	
Rider, Matthew		Tucker, Willie	
Rockwell, Margaret	<b>LIFE STAR</b>	Wainwright, LeRoy	
Schlosser, Ariel	Alfaro, Walter		
Wunschel, Scott	Gumbs Vines, Doreen		
Wunschel, Reina		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Vargas, Brian		
	Vargas, Gustavo	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

3 hour delay per OPM due to snowy, icy roads from storms yesterday/last night. Shoveled and swept walking areas clear before resuming work. 15 drums filled.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	





Pg

33

1-30-19

0930 SAFETY BRIEF 3hr Delay INW OPM.

0958 RADIO CHECKS.

1008 MINICAMS UP

1122 SOIL DRUMS 2330-2342 LOADED

FOR FEDERAL PROPERTY.

1140 STARTING MIDDAY CHALLENGE.

1148 MIDDAY CHALLENGE COMPLETE

1250 TEAM 1 DOWN RANGE LEVEL 'B' SIGN

JOURNEY, BRYMAN.

1245 VOC COLLECTED

1306 PPE CHECKS.

1335 PPE CHECKS.

1418 SOIL DRUMS 2343-2357 FILLED.

1427 COMPOSITE SAMPLE COLLECTED

1435 TEAM 1 CLEARED POS.

1458 SOIL DRUMS 2343-2357 LOADED

FOR FEDERAL PROPERTY.

1700 SECURED

Pg  
18/19



Pg

34 1-31-19

0630 SAFETY BRIEF

0700 RADIO CHECKS

0830 NO INTRUSIVE OPERATIONS DUE  
TO THE EXTREME COLD.

THE TEAMS WILL BE WORK TO EXPAND  
TEMP FORCE ON Runway 4825/4835

1700 SECURED

*[Handwritten signature]*

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 2 February 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 22/28 snow 1"+

**Personnel on Site**

PARSONS	ZES	ECBC	
Castell, Lorna	Breyman, Mark	Askew, Tom	
Courtney, Kenneth	Heffelfinger, Gerald	Crawford, Stephen	
Marion, Jedidiah	Prate, Warren	Edwards, Charles	
Matter, Phillip	Yorkshire, Bart	Mantei, Michael	
Moon, Dale	Rutana, Steve	McClellan, Dale	
Nelms, Bobby	Wright, David	Miller, Don	
Oien, Joshua		Phuong, Nguyen	
Rider, Matthew		Shavers, Dedrick	
Rockwell, Margaret	<b>LIFE STAR</b>	Tucker, Willie	
Schlosser, Ariel	Brooke, Bailey	Wainwright, LeRoy	
Wunschel, Scott	Dunnavant, Delany		
		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Williams, Angelo		
	Schmidt, James	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Not intrusive today. Snow started at about 7AM and continued into the afternoon. Ground conditions were extremely slippery considering level B teams wearing booties. No level B entries were made due today. Sent crews home at 1200.

End of Day: 1200

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



D<sub>4</sub>

35

2-1-19

0630 SAFETY BRIEF

0700 RADIO CHECKS

0740 MINICAMS UP

0812 DAMS PUMPS

0930 INTRUSIVE OPERATIONS SUSPENDED

DUE TO SNOW & TEMPERATURE.

1230 SITE SECURED

*[Handwritten signature]*



[illegible]

Rg

30 2-4-19

0630 SAFETY BRIEF

0700 RADIO CHECKS

0730 MINICAMS UP

0830 DRAWS PUMPS RUNNING

0850 TEAM 2 DOWN RANGE LEVEL "B"

RIDER CASTELL BREYMAN

0906 VOC COLLECTED

0928 PPE CHECKS

1033 PPE CHECKS

1117 SOIL DRUMS 2358-2382 FILLED

1127 TEAM 2 CLEARED POS.

1148 STARTING MIDDAY CHALLENGE

1142 MIDDAY CHALLENGE COMPLETE

1320 SOIL DRUMS 2358-2372 LOADED

FOR FED PROPERTY

1324 TEAM 1 DOWN RANGE 015N, ~~HEATER~~ CARTON

SOIL DRUMS 2383-2382 PPE DRUMS

445-446 LOADED FOR FEDERAL PROPERTY

1520 SOIL DRUMS 2383-2402 FILLED

1530 COMPOSITE SAMPLE COLLECTED

TEAM 1 CLEARED POS.

1700 SECURED

Rg

# SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 5 February 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 39/65 overcast

## Personnel on Site

PARSONS	ZES	ECBC	
Black, Jon	Breyman, Mark	Baker, Dawn	
Castell, Lorna	Heffelfinger, Gerald	Copeland, Eric	
Courtney, Kenneth	Prate, Warren	Druyor, Dana	
Marion, Jedidiah	Yorkshire, Bart	Dusick, Brandon	
Matter, Phillip	Rutana, Steve	Edwards, Charles	
Nelms, Bobby	Wright, David	Foor, Adam	
Oien, Joshua		King, Bernard	
Rider, Matthew		McGill, Andre	
Schlosser, Ariel	<b>LIFE STAR</b>	Ponce, Juan	
Southall, Daniel	Alfaro, Walter	Shavers, Dedrick	
Wunschel, Scott	Jacksn, Mark	Smith, Ethen	
		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Williams, Angelo		
	Schmidt, James	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations, 30 drums filled. HAZMAT shipment: 74 drums and approx. 5000 gallons of water shipped. Mask fit 2 new personnel.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

### Visitors


### Contractors

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	





Pg

37 2-5-19

0630 SAFETY BRIEF

0700 RADIO CHECKS

0730 WALTER NIAFO HET6 MUSTARD FOR  
TRAINING FOR CASEY SOUTHAEL AND  
JON BLACK0754 SOIL DRUMS 2383-2397 LOADED  
FOR FEDERAL PROPERTY.

0805 DAMPS PUMPS RUNNING.

0853 TEAM 2 DOWN RANGE LEVEL "B"  
RIDER CASTLE, WRIGHT.

0903 VOC COLLECTED

0934 PPE CHECKS

1010 PPE CHECKS

1052 SOIL DRUMS 2403-2417 FILLED

1057 TEAM 2 CLEARED PDS

1133 SOIL DRUMS 2398-2412 LOADED FOR  
FEDERAL PROPERTY.

1145 STARTING MID DAY CHANNEL 6.

1152 MID DAY COMPLETE.

1306 TEAM 2 DOWN RANGE LEVEL "B"  
BION, CURTAIN HINTERLAND

1333 PPE CHECKS

1405 PPE CHECKS

1437 COMPOSITE COLLECTED

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 6 February 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 48/49, winds 5-10 mph

**Personnel on Site**

PARSONS	ZES	ECBC	
Black, Jon	Breyman, Mark	Baker, Dawn	
Castell, Lorna	Heffelfinger, Gerald	Copeland, Eric	
Courtney, Kenneth	Prate, Warren	Druyor, Dana	
Marion, Jedidiah	Yorkshire, Bart	Dusick, Brandon	
Matter, Phillip	Rutana, Steve	Edwards, Charles	
Nelms, Bobby	Wright, David	Foor, Adam	
Oien, Joshua		King, Bernard	
Rider, Matthew		McGill, Andre	
Schlosser, Ariel	<b>LIFE STAR</b>	Ponce, Juan	
Southall, Daniel	Alfaro, Walter	Smith, Eathen	
Wunschel, Scott	Gumbs Vines, Doreen		
		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Williams, Angelo		
	Schmidt, James	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations 25 drums filled. 2000 gallons of water pumped from excavation area. New bullet proof glass panel installed in guard shack

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information  
 \_\_\_\_\_  
 \_\_\_\_\_

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
_____	Berkel ( )
_____	DAVEY ( )
_____	ACCUPERMIT ( )
_____	ACI (0)
_____	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



B

39 2-6-19

0630 SAFETY BRIEF

0700 RADIO CHECKS

0711 SOIL DRUMS 2428-2432, SEE DOWN 570  
LOADED FOR FEDERAL PROPERTY.

0830 DAMS PUMPS RUNNING

0 MINICAMS ARE HAVING EQUIPMENT  
PROBLEMS. PUMPING WATER AREA 1/A

1000 MINICAMS UP

1026 TEAM 2 DOWN RANGE LEVEL "B".

RIDER, MARIAN, WRIGHT.

1034 VOC COLLECTED.

1100 PPE CHECKS

1132 PPE CHECKS

1200 SOIL DRUMS 2433-2447 FILLED

1206 TEAM 2 CLEARED DDS.

STARTING MIDDAY CHALLENGE.

1327 SOIL DRUMS 2433-2447 LOADED  
FOR FEDERAL PROPERTY.

1330 MINICAMS UP.

1353 TEAM 1 DOWN RANGE LEVEL "A".

GLEN SCHLOSSER, HERFEL FINGER.

1437 PPE CHECKS

1452 MINICAMS REPORT .98 PERCENT

AT EXAMINATION POINT



## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 7 February 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 52/57 mostly clear

**Personnel on Site**

PARSONS	ZES	ECBC	
Black, Jon	Breyman, Mark	Baker, Dawn	
Castell, Lorna	Heffelfinger, Gerald	Copeland, Eric	
Courtney, Kenneth	Prate, Warren	Druyor, Dana	
Marion, Jedidiah	Yorkshire, Bart	Dusick, Brandon	
Matter, Phillip	Rutana, Steve	Edwards, Charles	
Nelms, Bobby	Wright, David	Foor, Adam	
Oien, Joshua		King, Bernard	
Rider, Matthew		McGill, Andre	
Rockwell, Margaret		Ponce, Juan	
Schlosser, Ariel	<b>LIFE STAR</b>	Smith, Eathen	
Southall, Daniel	Gumbs Vines, Doreen		
Wunschel, Scott	Haupt, Calvin		
		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Williams, Angelo		
	Schmidt, James	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations filled 55 drums in NE corner of area A. Sampled water in 1 Baker tank for disposal.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information  
 \_\_\_\_\_  
 \_\_\_\_\_

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
_____	Berkel ( )
_____	DAVEY ( )
_____	ACCUPERMIT ( )
_____	ACI (0)
_____	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



2/7/19

2-7-19

0630 SAFETY BRIEF

0700 RADIO CHECKS

0800 SOIL DRUMS 2448-2457 PPE

DRUM 447 LOADED FOR FEDERAL PROPERTY

0751 MINICAMS & DARRS UP

0833 TEAM 2 DOWN RANGE LEVEL "B" RIDER  
CARTER, BROYMAN

0841 VCC COLLECTED

0904 PPE CHECKS

0941 SOIL DRUMS 2458-2472 FILLED

1034 SOIL DRUMS 2458-2472 LOADED  
FOR FEDERAL PROPERTY

1103 SOIL DRUMS 2473-2487 FILLED

1115 TEAM 2 CIGARETTS

1200 STARTING MIDDAY CHALLENGE

1218 MIDDAY COMPLETE

1258 TEAM 1 DOWN RANGE LEVEL "B"  
OJEN, COURTNEY WRIGHT

1331 PPE CHECKS

1357 SOIL DRUMS 2473-2487 LOADED

FOR FEDERAL PROPERTY

1415 SOIL DRUMS 2488-2502 FILLED

1428 PPE CHECK

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 8 February 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 26/61 partly cloudy, 5-25 mph winds

**Personnel on Site**

PARSONS	ZES	ECBC	
Black, Jon	Breyman, Mark	Baker, Dawn	
Castell, Lorna	Heffelfinger, Gerald	Copeland, Eric	
Courtney, Kenneth	Prate, Warren	Druyor, Dana	
Marion, Jedidiah	Yorkshire, Bart	Dusick, Brandon	
Matter, Phillip	Rutana, Steve	Edwards, Charles	
Oien, Joshua	Wright, David	Foor, Adam	
Rider, Matthew		King, Bernard	
Rockwell, Margaret		McGill, Andre	
Schlosser, Ariel	<b>LIFE STAR</b>	Ponce, Juan	
Southall, Daniel	Alfaro, Walter	Smith, Eathen	
Wunschel, Scott	Dunnavant, Delany		
		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Schmidt, James		
	Williams, Angelo	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations in NE corner of Area A, 45 drums filled. 1 HAZMAT tanker with approx. 5000 gallons of water shipped off. 2350 gallons of water pumped.

End of Day: 1700

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

[illegible]



Pg

43

2-8-19

0630 Morning Safety Brief.

0645 Site Set up

0715 Radio checks.

0810 Loading Full drums to transport Fed Site.

0821 Tm 2 In to excavate, level B

0829 VOC complete.

1020 Drums 2513-2527 out &amp; on the way to Fed Site.

1107 Drums 2528-2542 Complete, Team Prepping to exit.

1116 Tm Tm 2 Clear of PDS.

1135 lunch

1210 Teams Prepping for Second level B entry

1252 Tm 1 entering level B to fill drums.

1400 Tm 1 Clear of PDS


1405 Loading Drums 2528-2542 For transport.

1458 Loading Drums 2543-2557 For Transport.

1509 Last load of Drums exiting.

1510 End of week clean up &amp; Maint.

1700 Day Complete

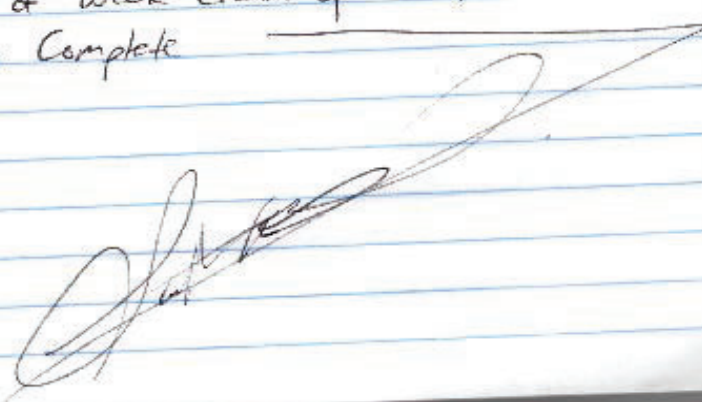



[illegible]

16

44 2-11-19

0830 SAFETY BRIEF 2HT DELAY OPM

0852 RADIO CHECKS. TRAFFIC SIGNS UP

MINICAMS DOING MAINTENANCE

PUMPING WATER FROM EXCAVATION.

1155 MINICAMS AND DARRMS UP

1307 TEAM 1 DOWN RANGE LEVEL "B"

DIEN, SCHLOSSER, WRIGHT.

1313 VOC COLLECTED

1330 PPE CHECKS


1358 PPE CHECKS.

1500 SOIL DRUMS 2558-2577 FILLED.

1511 COMPOSITE COLLECTED.

1517 TEAM 1 CLEARED PDS.

1700 SECURED

A large, stylized handwritten signature in black ink, slanted diagonally across the lower half of the page. The signature appears to be 'Jody' followed by a large, sweeping flourish.

**SPRING VALLEY, WASHINGTON DC**

**Contract No:** W912DY-09-D-0062  
**Delivery Order:** TO 0006  
**Date:** 12 February 2019  
**Site Location:** 4825 Glenbrook Road

**Weather:**  
 34/43 5-10 winds

**Personnel on Site**

PARSONS	ZES	ECBC	
Black, Jon	Breyman, Mark	Baker, Dawn	
Castell, Lorna	Heffelfinger, Gerald	Bartosh, Ian	
Courtney, Kenneth	Prate, Warren	Burrell, Dianne	
Marion, Jediaiah	Yorkshire, Bart	Copeland, Eric	
Matter, Phillip	Rutana, Steve	Crawford, Stephen	
Nelms, Bobby	Wright, David	Edwards, Charles	
Oien, Joshua		King, Bernard	
Rider, Matthew		McGill, Andre	
Rockwell, Margaret		Ponce, Juan	
Schlosser, Ariel	<b>LIFE STAR</b>	Shavers, Dietrick	
Southall, Daniel	Alfaro, Walter		
Wunschel, Scott	Jackson, Mark		
		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Vargas, Brian		
	Vargas, Gustavo	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive operations today, heavy rains. Removed 20 drums of soil that were filled yesterday. Day called at 10:30 constant rains getting stronger and forecast shows no end during work hours.

End of day: 10:30

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**

**Contractors**  
 Berkel ( )  
 DAVEY ( )  
 ACCUPERMIT ( )  
 ACI (0)  
 CPJ (0)

**Problems encountered/resolutions:**

**Instructions given by government personnel:**

**Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



Pg

45

2-12-19

0630 SAFETY BRIEF

0735 MINICAMS UP


0811 SOIL DRUMS 2558-2572 LOADED

FOR FEDERAL PROPERTY.

0908 SOIL DRUMS 2573-2577 LOADED

FOR FEDERAL PROPERTY.

1030 SITE SECURED DUE TO WEATHER

A large, stylized handwritten signature, likely "R. J. Smith", is written across the lower half of the page. The signature is written in dark ink and is positioned diagonally, crossing over the bottom of the log entries.

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 13 February 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 34/43 degrees, winds 5-20

**Personnel on Site**

PARSONS	ZES	ECBC	
Black, Jon	Breyman, Mark	Baker, Dawn	
Castell, Lorna		Bartosh, Ian	
Courtney, Kenneth	Prate, Warren	Burrell, Dianne	
Marion, Jedidiah	Yorkshire, Bart	Copeland, Eric	
Matter, Phillip	Rutana, Steve	Crawford, Stephen	
Nelms, Bobby	Wright, David	Edwards, Charles	
Oien, Joshua		King, Bernard	
Rider, Matthew		McGill, Andre	
Rockwell, Margaret		Ponce, Juan	
Schlosser, Ariel	<b>LIFE STAR</b>	Shavers, Dietrick	
Southall, Daniel	Alfaro, Walter		
Wunschel, Scott	Gumbs Vines, Doreen		
		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Vargas, Brian		
	Vargas, Gustavo	<b>CENAB</b>	
	Overton, Robert		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations, 40 drums of soil filled. Pumped 3400 gallons of water.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



Pg

46

2-13-19

0630 SAFETY BRIEF

0730 RADIO CHECKS MINICAMS UP

0745 DAAMS PUMPS RUNNING.

0845 TEAM 1 DOWN RANGE LEVEL "B" RIDER

CASTELL, BRYMAN.

0852 MINICAMS 148 FOR LEUISITE AT

EXCAVATION.

0901 2nd cycle 102 LEUISITE.

0911 3rd cycle clear.

0931 VOC COLLECTED. PUMP IN

WATER FROM EXCAVATION AREA 'A

1007 PPE CHECKS

1028 PPE CHECKS.

1050 SOIL DRUMS 2578-2592 FILLED.

1116 SOIL DRUMS 2593-2597 FILLED

1123 TEAM 2 CLEARED PDS.

1130 STARTING MIDDAY CHALLENGE.

1157 MIDDAY COMPLETE

1300 SOIL DRUMS 2578-2592 - LOADED FOR

FEDERAL PROPERTY.

1301 TEAM 1 DOWN RANGE LEVEL "B" SIGN

COMING BY WATER.

1322 PPE CHECK

1342 SOIL DRUMS 2593-2597 LOADED

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 14 February 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 45/53 winds 5-10

**Personnel on Site**

PARSONS	ZES	ECBC	
Black, Jon	Breyman, Mark	Baker, Dawn	
Castell, Lorna		Bartosh, Ian	
Courtney, Kenneth	Prate, Warren	Burrell, Dianne	
Marion, Jedidiah	Yorkshire, Bart	Copeland, Eric	
Matter, Phillip		Crawford, Stephen	
Nelms, Bobby	Wright, David	Edwards, Charles	
Oien, Joshua		King, Bernard	
Rider, Matthew		McGill, Andre	
Rockwell, Margaret	LIFE STAR	Ponce, Juan	
Schlosser, Ariel	Haupt, Calvin	Shavers, Dietrick	
Southall, Daniel	Gumbs Vines, Doreen		
Wunschel, Scott			
		CEHNC	
	ACCUPERMIT	Boles, Judson	
	Schmidt, James		
	Williams, Angelo	CENAB	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations in Area 1, 13 drums filled. Pumped 1700 gallons of water.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	





Pg  
48

2-14-19

0630 SAFETY BRIEF

0710 RADIO CHECKS.

0740 MINICAMS UP

0752 DAAMS PUMPS RUNNING

0802 SOIL DRUMS 2598-2612 LOADED  
FOR FEDERAL PROPERTY.0823 TEAM 1 DOWN RANGE LEVEL 2<sup>nd</sup> B  
OIGN SCHLOSSER BRBY MNN.0837 SOIL DRUMS 2613-2617 LOADED  
FOR FEDERAL PROPERTY.

0840 VOC COLLECTED.

0854 PPE CHECKS.

0924 PPE CHECKS. PUMPING WATER  
FROM ELIMINATION AREA 1/A

1007 COMPOSITE SAMPLE COLLECTED.

1018 TEAM 1 CLEARING PDS.

1020 NOTE: SOIL DRUMS 2618-2630 FILLED  
AT 1000.1127 SOIL DRUMS 2618-2630 LOADED FOR  
FEDERAL PROPERTY.

1150 CONFERENCE CALL.

1440 STARTING END OF DAY CHECKS.  
W/MONITORING. TRANSITIONING  
TO LEVEL D OPS

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 15 February 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 33/63, winds 5-10

**Personnel on Site**

PARSONS	ZES	ECBC	
Black, Jon	Breyman, Mark	Baker, Dawn	
Castell, Lorna		Bartosh, Ian	
Courtney, Kenneth	Prate, Warren	Burrell, Dianne	
Marion, Jedidiah	Yorkshire, Bart	Copeland, Eric	
Matter, Phillip		Crawford, Stephen	
Nelms, Bobby	Wright, David	Edwards, Charles	
Oien, Joshua		King, Bernard	
Rider, Matthew		McGill, Andre	
Rockwell, Margaret	LIFE STAR	Ponce, Juan	
Schlosser, Ariel	Brooke, Bailey	Shavers, Dietrick	
Southall, Daniel	Gumbs Vines, Doreen		
Wunschel, Scott			
		CEHNC	
	ACCUPERMIT	Boles, Judson	
	Schmidt, James		
	Williams, Angelo	CENAB	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No monitored intrusive operations today. Dug out an area for the rolloff to be put in nearer the excavator in north east corner of Area 1. Had the vehicle gate at Fed Prop fixed by DC Gate Experts.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



Ry

50 2-15-19

0630 SAFETY BRIEF

0700 RADIO CHECKS

0745 MINICAMS UP

0810 DAMS PUMPS RUNNING.  
PRODING AREA D'1140 STARTING END OF DAY CHECKS  
FOR MONITORING

1348 PUMPING WATER FROM EXCAVATION.

1400 END OF WORK MAINTENANCE.

Ry



## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 21 February 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 35/54 winds 5-10 mph

**Personnel on Site**

PARSONS	ZES	ECBC	
Black, Jon	Breyman, Mark	Baker, Dawn	
Castell, Lorna	Heffelfinger, Gerald	Bartosh, Ian	
Courtney, Kenneth	Prate, Warren	Burrell, Dianne	
Marion, Jediaiah	Rutana, Steve	Copeland, Eric	
Matter, Phillip	Wright, David	Crawford, Stephen	
Nelms, Bobby	Yorkshire, Bart	Doyle, Satchell	
Oien, Joshua		King, Bernard	
Rider, Matthew		McGill, Andre	
Rockwell, Margaret	<b>LIFE STAR</b>	Ponce, Juan	
Schlosser, Ariel	Haupt, Calvin	Shavers, Dietrick	
Southall, Daniel	Gumbs Vines, Doreen	Miller, Don	
Wunschel, Scott			
		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Vargas, Brian		
	Vargas, Gustavo	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations in northeast corner of Area 1, 2 rolloffs filled. 2550 gallons of water pumped.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information  
 \_\_\_\_\_  
 \_\_\_\_\_

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

53

2-21-19

0630 SAFETY BRIEF

0700 RADIO CHECKS, DOWNING

ICE &amp; SNOW FROM EQUIPMENT PADS

PREP'ING SITE FOR INTRUSION OPERATIONS

0800 DAMS PUMPS RUNNING

NOTE: MINICAMS UP @ 07:30

0922 ROLL OFF 291440 ON SITE.

0941 TEAM 2 DOWN RANK 16V02 "B"  
RIGID CASTON WRIGHT.

0950 VOC COLLECTED

1008 PPE CHECKS. PUMPING WATER

1039 PPE CHECKS

1118 TEAM 2 CLEARED PDS.

1120 STARTING MIDDAY CHALLENGE

1145 MIDDAY CHALLENGE COMPLETE.

1239 TEAM 2 DOWN RANK 16V02 "B"

DOWN, SCHLOSSER, HOFFER FINISH.

1500 PPE CHECKS

1310 ROLL OFF 291440 IS FULL

1320 ROLL OFF 291440 OFF SITE

1345 ROLL OFF 291432 ON SITE

1350 VOC COLLECTED

1417 PPE CHECKS

1434 PPE CHECKS

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 21 February 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 35/54 winds 5-10 mph

**Personnel on Site**

PARSONS	ZES	ECBC	
Black, Jon	Breyman, Mark	Baker, Dawn	
Castell, Lorna	Heffelfinger, Gerald	Bartosh, Ian	
Courtney, Kenneth	Prate, Warren	Burrell, Dianne	
Marion, Jedidiah	Rutana, Steve	Copeland, Eric	
Matter, Phillip	Wright, David	Crawford, Stephen	
Nelms, Bobby	Yorkshire, Bart	Doyle, Satchell	
Oien, Joshua		King, Bernard	
Rider, Matthew		McGill, Andre	
Rockwell, Margaret		Ponce, Juan	
Schlosser, Ariel	<b>LIFE STAR</b>	Shavers, Dietrick	
Southall, Daniel	Haupt, Calvin	Miller, Don	
Wunschel, Scott	Gumbs Vines, Doreen		
		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Vargas, Brian		
	Vargas, Gustavo	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations in northeast corner of Area 1, 2 rolloffs filled. 2550 gallons of water pumped.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information  
 \_\_\_\_\_  
 \_\_\_\_\_

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
_____	Berkel ( )
_____	DAVEY ( )
_____	ACCUPERMIT ( )
_____	ACI (0)
_____	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



Pg

53

2-21-19

0630 SAFETY BRIEF

0700 RADIO CHECKS, DOWNING

ICE &amp; SNOW FROM EQUIPMENT PADS

PREP'ING SITE FOR INTRUSIVE OPERATIONS

0800 DAMS PUMPS RUNNING

NOTE: MINICAMS UP @ 07:30

0922 ROLL OFF 291440 ON SITE.

0941 TEAM 2 DOWN RANK 16V02 "B"  
RIGOR CASTON WRITING.

0950 VOC COLLECTED

1008 PPE CHECKS. PUMPING WATER

1039 PPE CHECKS

1118 TEAM 2 CLEARED PDS.

1120 STARTING MIDDAY CHALLENGE

1145 MIDDAY CHALLENGE COMPLETE.

1239 TEAM 2 DOWN RANK 16V02 "B"

DOWN, SCHLOSSER, HOFFER FINISH.

1500 PPE CHECKS

1310 ROLL OFF 291440 IS FULL

1320 ROLL OFF 291440 OFF SITE

1345 ROLL OFF 291432 ON SITE

1350 VOC COLLECTED

1417 PPE CHECKS

1434 PPE CHECKS



## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 22 February 2019  
 Site Location: 4825 Glenbrook Road

Weather:  
 38/ 43, winds 5-10

**Personnel on Site**

PARSONS	ZES	ECBC	
Castell, Lorna		Baker, Dawn	
Courtney, Kenneth	Heffelfinger, Gerald	Bartosh, Ian	
Marion, Jedidiah	Prate, Warren	Burrell, Dianne	
Matter, Phillip	Rutana, Steve	Copeland, Eric	
Nelms, Bobby	Wright, David	Crawford, Stephen	
Oien, Joshua	Yorkshire, Bart	Doyle, Satchell	
Rider, Matthew		King, Bernard	
Rockwell, Margaret		McGill, Andre	
Schlosser, Ariel	<b>LIFE STAR</b>	Ponce, Juan	
Wunschel, Scott	Brooke, Bailey	Shavers, Dietrick	
	Dunnavant, Delaney		
		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Vargas, Brian		
	Vargas, Gustavo	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations 1 rolloff filled, minicams issue after midday ran out of time for digging by the time issue was resolved.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



Pg

55 2-22-19

0630 SAFETY BRIEF.

0700 RADIO CHECKS

0740 MINICAMS OP

0800 DRAINS PUMPS RUNNING

ROLL OFF 291441 ON SITE

PUMPING WATER FROM EXCAVATION.

0901 TEAM 2 DOWN RANLE LEVEL "B"

RIDER, MARION WRIGHT.

0910 COLLECTED VOC

0920 PPE CHECKS

0950 PPE CHECKS

1045 ROLL OFF 291441 IS FULL

1100 TEAM 2 CLEARED PDS

1140 ROLL OFF 291441

1150 STARTING MIDDAY CHALLENGE.

1200 ROLL OFF 290976 ON SITE.

1211 MIDDAY CHALLENGE COMPLETE.

1600 SECURED

A large, stylized handwritten signature, possibly reading "B. S. R.", is written across the bottom of the page. A diagonal line is drawn through the signature.

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 25 February 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 41/46, winds 5-20 mph

**Personnel on Site**

PARSONS	ZES	ECBC	
Banks, Janelle		Dusick, Brandon	
Blevins, Robert	Heffelfinger, Gerald	Bartosh, Ian	
Castell, Lorna	Prate, Warren	Miller, Don	
Courtney, Kenneth	Rutana, Steve	Copeland, Eric	
Jackson, Matthew	Wright, David	Kirby, Anna	
Luckanavage, Kyle	Yorkshire, Bart	Doyle, Satchell	
Marion, Jedidiah		King, Bernard	
Matter, Phillip		McGill, Andre	
Nelms, Bobby	<b>LIFE STAR</b>	Ponce, Juan	
Oien, Joshua	Alfaro, Walter	Shavers, Dietrick	
Rider, Matthew	Robinson, Omar		
Schlosser, Ariel			
Wunschel, Scott		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Williams, Angelo		
	Artaez, Carlos	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations in northeast corner of Area 1, 1 rolloff filled. Baltimore Geologist arrived at site and confirmed we are at competent saprolite. Set up confirmation sample grids for sampling tomorrow.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



Pg

56 2-25-19

0630 SAFETY BRIEF

0740 MINI CAMS UP.

0844 DAMS PUMPS RUNNING

0912 TEAM 2 DOWN RANK 1000' R

RIDER CASTELL, WRIGHT.

0920 COMPOSITE SAMPLE 206 COLLECTED.

0928 VOC COLLECTED.

0949 PPE CHECKS.

1038 PPE CHECKS.

1105 COLLECTED COMPOSITE

1119 TEAM 2 CLEARED PDS.


1130 STARTING MIDDAY

1200 MIDDAY COMPLETE BALTIMORE

GEOLOGIST CONFIRMS AREA 'A' &  
SAPROLITE.

1230 PUMPING WATER.

1700 SECURED

A handwritten signature in black ink, appearing to be 'R. J. Smith', is written across the bottom of the page. The signature is stylized and slanted.

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 26 February 2019  
 Site Location: 4825 Glenbrook Road

Weather:  
 30/48 degrees, winds 5-10

**Personnel on Site**

PARSONS	ZES	ECBC	
Banks, Janelle		Bartosh, Ian	
Blevins, Robert	Heffelfinger, Gerald	Copeland, Eric	
Castell, Lorna	Prate, Warren	Doyle, Satchell	
Courtney, Kenneth	Rutana, Steve	Dusick, Brandon	
Holloway, April	Wright, David	King, Bernard	
Jackson, Matthew	Yorkshire, Bart	Kirby, Anna	
Luckanavage, Kyle		McGill, Andre	
Marion, Jedidiah		Miller, Don	
Matter, Phillip		Ponce, Juan	
Nelms, Bobby	<b>LIFE STAR</b>	Shavers, Dietrick	
Oien, Joshua	Alfaro, Walter		
Rider, Matthew	Jackson, Mark		
Schlosser, Ariel			
Wunschel, Scott		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Overton, Robert		
	Williams, Angelo	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Confirmation samples in the following Area 1/Area A grids: 90 -70, 90 -90, 70 -90, 70 -70 and a field duplicate 15 samples in total. Pumped 3400 gallons of water.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	





P  
19

57 2-26-19

0630 SAFETY BRIEF

0710 RADIO CHECKS

1002 LEVEL "B" DOWN RANK 6 FOR

SAMPLING RIDER, 0100, 0100, 0100

1021 90-70 TOP COMPLETED

1033 90-70 MID COMPLETED

1044 90-70 BOTTOM COMPLETED

1107 90-90 EAST WALL TOP COMPLETED

1114 90-90 EAST WALL MID COMPLETED

1123 90-90 EAST WALL BOTTOM COMPLETED

1137 90-90 NORTH TOP COMPLETE

1146 90-90 NORTH MID COMPLETED

1154 90-90 NORTH BOTTOM COMPLETED

1202 70-90 TOP COMPLETED

1209 70-90 MID COMPLETED

1216 70-90 BOTTOM COMPLETED

1222 70-90 FLOOR COMPLETED

1234 70-70 FLOOR COMPLETED?

DUPLICATE

1240 TEAM SAMPLE CLEARED PDS.

1300 PUMPING WATER.

1700 SECURED

Bryce

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 27 February 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 37/ 47 degrees

**Personnel on Site**

PARSONS	ZES	ECBC	
Banks, Janelle	Breyman, Mark	Bartosh, Ian	
Blevins, Robert	Heffelfinger, Gerald	Copeland, Eric	
Castell, Lorna	Prate, Warren	Doyle, Satchell	
Courtney, Kenneth	Rutana, Steve	Dusick, Brandon	
Holloway, April		King, Bernard	
Jackson, Matthew	Yorkshire, Bart	Kirby, Anna	
Luckanavage, Kyle		McGill, Andre	
Marion, Jedidiah		Miller, Don	
Matter, Phillip	LIFE STAR	Ponce, Juan	
Nelms, Bobby	Alfaro, Walter	Shavers, Dietrick	
Oien, Joshua	Gumbs Vines, Doreen		
Rider, Matthew			
Schlosser, Ariel		CEHNC	
Wunschel, Scott	ACCUPERMIT	Boles, Judson	
	Overton, Robert		
	Williams, Angelo	CENAB	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations in Area 2 on 4835 property. 21 drums filled, glass-ware was found but no intact containers or CACM. There will be a lot of hand digging in this area due to A/C lines and above ground water line.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



Pg.

58 2-27-19

0630 SAFETY BRIEF

0700 RADIO CHECKS

0730 MINICAMP UP.

0916 SETUP COMPLETE TEAM 2 DOWN RANGE  
LEVEL "B" RIDGE, MARIAN, BRYAN.

0931 VOC COLLECTED AREA "2"

0954 PPE CHECKS

1044 PPE CHECKS.

1119 SOIL DRUMS 2631-2645 FILLED

1125 TEAM 2 CLEARED POS.

1135 STARTING MID DAY CHALLENGE

1150 MIDDAY CHALLENGE COMPLETE

1205 SOIL DRUMS 2631-2645 OFF TO  
FEDERAL PROPERTY.1325 TEAM 1 DOWN RANGE LEVEL "B"  
DIBN, SCHLOSSER.

1343 PPE CHECKS

1412 PPE CHECKS.

1511 SOIL DRUMS 2646-2651 FILLED


1515 COMPOSITE COLLECTED

1525 TEAM 1 CLEARED POS

SOIL DRUMS 2646-2651 LOADED

FED PROPERTY

1700 SECURED



## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 28 February 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 33/45 degrees, breezy, overcast 5-20 mph winds

**Personnel on Site**

PARSONS	ZES	ECBC	
Banks, Janelle	Breyman, Mark	Bartosh, Ian	
Blevins, Robert	Heffelfinger, Gerald	Copeland, Eric	
	Prate, Warren	Doyle, Satchell	
Courtney, Kenneth	Rutana, Steve	Dusick, Brandon	
Holloway, April	Wright, David	King, Bernard	
Jackson, Matthew	Yorkshire, Bart	Kirby, Anna	
Luckanavage, Kyle		McGill, Andre	
Marion, Jedidiah		Miller, Don	
Matter, Phillip		Ponce, Juan	
Nelms, Bobby	<b>LIFE STAR</b>	Shavers, Dietrick	
Oien, Joshua	Haupt, Calvin		
Rider, Matthew	Gumbs Vines, Doreen		
Schlosser, Ariel		<b>CEHNC</b>	
Wunschel, Scott	<b>ACCUPERMIT</b>	Boles, Judson	
	Vargas, Brian		
	Vargas, Gustavo	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations in Area 2, mostly hand-digging due to Air-conditioner lines and above ground water line. Glassware found, no CACM or intact containers found.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	





P<sub>2</sub>

59 2-28-19

0630 SAFETY BRIEF

0700 RADIO CHECKS

0730 MINICAMS &amp; 6 ARMS UP

0830 TEAM 2 DOWN RANGE LEVEL "B"  
RIDER, MARIAN

0835 VOC COLLECTED

0852 PPE CHECKS

0917 PPE CHECKS

0940 TEAM 2 CLEARED POS. SIL DRUMS 2652-2654

1000 PUMPING WATER FROM EXCAVATION

1100 CONFERENCE CALL

1135 STARTING MIDDAY CHALLENGE

1200 MIDDAY CHALLENGE COMPLETE

1240 TEAM 1 DOWN RANGE LEVEL "B"  
OIGN, COURTNEY

1302 DRUM 2655 FILLED PPE CHECK

1323 DRUM 2656 FILLED PPE CHECK

1336 DRUM 2657 FILLED, PPE CHECK

1357 DRUM 2658 FILLED PPE CHECK

1414 DRUM 2659 FILLED PPE CHECK

1429 DRUM 2660 FILLED PPE CHECK

1442 DRUM 2661 FILLED

1447 COMPOSITE COLLECTED

1500 TEAM 1 CLEARED POS

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 1 March 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 32/36 very cold with a 5-10 mph breeze.

**Personnel on Site**

PARSONS	ZES	ECBC	
Banks, Janelle	Breyman, Mark	Bartosh, Ian	
Blevins, Robert	Heffelfinger, Gerald	Copeland, Eric	
	Prate, Warren	Doyle, Satchell	
Courtney, Kenneth	Rutana, Steve	Dusick, Brandon	
Holloway, April	Wright, David	King, Bernard	
Jackson, Matthew	Yorkshire, Bart	Kirby, Anna	
Luckanavage, Kyle		McGill, Andre	
Marion, Jedidiah		Miller, Don	
Matter, Phillip		Ponce, Juan	
Nelms, Bobby	<b>LIFE STAR</b>	Shavers, Dietrick	
Oien, Joshua	Brooke, Bailey		
Rider, Matthew	Jackson, Mark		
Schlosser, Ariel		<b>CEHNC</b>	
Wunschel, Scott	<b>ACCUPERMIT</b>	Boles, Judson	
	Vargas, Brian		
	Vargas, Gustavo	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations in Area 2, 8 drums of soil removed. No further excavations in Area 2 until a decision by PDT is made. 53 pieces and approximately 5 pounds of glass removed from Area 2. 2100 gallons of water pumped.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



Pg  
9

61 3-1-19

0630 SAFETY BRIEF

0712 RADIO CHECKS

0800 MINICAMS; DAMS UP

0838 TEAM 1 DOWN RANGE LEVEL "B"

OIGEN SCHWICKER

0845 VOC COLLECTED

0907 SOIL DRUM 2662 FILLED PPE CHECK

0925 PPE CHECK

0928 SOIL DRUM 2663 FILLED

0938 SOIL DRUM 2664 FILLED PPE CHECK

0950 SOIL DRUM 2665 FILLED PPE CHECK

1002 SOIL DRUM 2666 FILLED PPE CHECK

1019 SOIL DRUM 2667 FILLED PPE CHECK

1043 SOIL DRUM 2668 FILLED

1116 SOIL DRUM 2669 FILLED, COMPOSITE COLLECTED

1130 SCR 583 DOUBLE BAGGED "GLASS"

53 PIECES, APPROXIMATELY 5185

1151 TEAM 1 CLEARED PDS

1300 Teams loading drums &amp; pumping water

1700 SECURED



## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 4 March 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 34/38 degrees partly cloudy

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Breyman, Mark	Askew, Tom	
Castell, Lorna	Heffelfinger, Gerald	Bartosh, Ian	
Courtney, Kenneth	Prate, Warren	Caldwell, Jeff	
Holloway, April	Rutana, Steve	Dusick, Brandon	
Jackson, Matthew	Wright, David	Heard, Irvin	
Luckanavage, Kyle	Yorkshire, Bart	Jones, LaMarcus	
Marion, Jedidiah		Kirby, Anna	
Matter, Phillip		McClellan, Dale	
Nelms, Bobby	<b>LIFE STAR</b>	McGill, Andre	
Oien, Joshua	Alfaro, Walter	Wainwright, LeRoy	
Rider, Matthew	Robinson, Omar		
Wunschel, Scott		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Overton, Robert		
	Williams, Angelo	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Clean backfill removal in Area 3, no monitoring needed. Pumped 4600 gallons of water out of Area 1.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

**Problems encountered/resolutions:**

Parsons rental vehicle involved in traffic accident, no injuries.

**Instructions given by government personnel:****Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



Pg

62 3-4-19

0630 RADIO CHECK

0700 RADIO CHECK

0730 REMOVING CROWN BARK FILL FROM  
AREA 5 PUMPING WATER.

1120 MINICAMS UP

1700 SECURED



## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 5 March 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 24/ 36 overcast

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Breyman, Mark	Askew, Tom	
Castell, Lorna	Heffelfinger, Gerald	Bartosh, Ian	
Courtney, Kenneth	Prate, Warren	Caldwell, Jeff	
Holloway, April	Rutana, Steve	Dusick, Brandon	
Jackson, Matthew	Wright, David	Heard, Irvin	
Luckanavage, Kyle	Yorkshire, Bart	Jones, LaMarcus	
Marion, Jedidiah		Kirby, Anna	
Matter, Phillip		McClellan, Dale	
Nelms, Bobby	<b>LIFE STAR</b>	McGill, Andre	
Oien, Joshua	Alfaro, Walter	Wainwright, LeRoy	
Rider, Matthew	Brooke, Bailey		
Schlosser, Ariel			
Wunschel, Scott		<b>CEHNC</b>	
Banks, Janelle	<b>ACCUPERMIT</b>	Boles, Judson	
	Overton, Robert		
	Williams, Angelo	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations in Area 3, monitored. 34 drums of soil removed.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



R

63 3-5-19

0630 SAFETY BRIEF

0703 RADIO CHECKS

0806 MINICAMS UP DAMS UP.

0808 TEAM 2 DOWN RANGE LEVEL B-

0845 DIPPER, CASTELL, WRIGHT.

0853 VOC COLLECTED.

0933 PPE CHECK.

1002 PPE CHECK

1111 SOIL DRUMS 2670-2689 FILLED.

1122 TEAM 2 CLEARED PDS.

1207 SOIL DRUMS 2670-2684 LOADED FOR  
FEDERAL PROPERTY. STARTING MID DAY

1230 MIDDAY COMPLETE

1330 TEAM 1 DOWN RANGE LEVEL "B" DOWN

CHURNING, HATCHER.

1402 PPE CHECK.

1436 PPE CHECK

1510 SOIL DRUMS 2690-2703 FILLED.


1513 COMPOSITE COLLECTED

1521 TEAM 1 CLEARED PDS.

1600 SOIL DRUMS 2685-2699 LOADED FOR

FEDERAL PROPERTY.

1700 SECURED



## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 6 March 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 24/36 partly cloudy

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Breyman, Mark	Askew, Tom	
Castell, Lorna	Heffelfinger, Gerald	Bartosh, Ian	
Courtney, Kenneth	Prate, Warren	Caldwell, Jeff	
	Rutana, Steve	Dusick, Brandon	
Jackson, Matthew	Wright, David	Heard, Irvin	
Luckanavage, Kyle	Yorkshire, Bart	Jones, LaMarcus	
Marion, Jedidiah		Kirby, Anna	
Matter, Phillip		McClellan, Dale	
Nelms, Bobby	<b>LIFE STAR</b>	McGill, Andre	
Oien, Joshua	Alfaro, Walter	Wainwright, LeRoy	
Rider, Matthew	Gumbs Vines, Doreen		
Schlosser, Ariel			
Wunschel, Scott		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Overton, Robert		
	Williams, Angelo	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations in Area 3, 11 drums filled. Finished intrusive operations on Area 3, collected composite samples. Pumped 1700 gallons of water from Area 1.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



Pg

64

3-6-19

0630 SAFETY BRIEF

0700 RADIO CHECKS.

0747 MINICAMS UP

0815 DAMS PUMPS RUNNING

0843 TEAM 2 DOWN RANGE LEVEL B RIDGE  
MAYDAY BROG MAN.

0847 VOC COLLECTED

0920 PPE CHECKS

1015 COMPOSITE COLLECTED. SOIL DAMMS 2704-2714

1020 TEAM 2 CLEARED PDS.

SOIL DAMMS 2700-2714, PPE DAMMS  
453/454 OFF SITE.

1130 STARTING MIDDAY CHALLENGE

1150 MIDDAY COMPLETE

1235 TEAM 1 DOWN RANGE LEVEL B-  
OIL, CHURNING, SCOTSSER.1350 CONFIRMATION SAMPLES COLLECTED  
FROM -30-90 NORTH WALL.

1355 TEAM 1 CLEARED PDS.

1700 SECURED



## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 7 March 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 28/42 breezy and cool

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Breyman, Mark	Askew, Tom	
Castell, Lorna	Heffelfinger, Gerald	Bartosh, Ian	
Courtney, Kenneth	Prate, Warren	Caldwell, Jeff	
Holloway, April	Rutana, Steve	Dusick, Brandon	
Jackson, Matthew	Wright, David	Heard, Irvin	
Luckanavage, Kyle	Yorkshire, Bart	Jones, LaMarcus	
Marion, Jedidiah		Kirby, Anna	
Matter, Phillip		McClellan, Dale	
Nelms, Bobby	<b>LIFE STAR</b>	McGill, Andre	
Oien, Joshua	Gumbs Vines, Doreen	Wainwright, LeRoy	
Rider, Matthew	Haupt, Calvin		
Schlosser, Ariel		<b>CEHNC</b>	
Wunschel, Scott		Boles, Judson	
Banks, Janelle	<b>ACCUPERMIT</b>		
	Atreaga, Carlos		
	Williams, Angelo	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive activities today. Setting up site for excavation of Area 4, bring in loads of gravel, remove construction pads covering area 4, move medical monitoring tent.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

**Problems encountered/resolutions:**

**Instructions given by government personnel:**

**Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

65 3-7-19

1630 SAFETY BRIEF

0700 RADIO CHECK.

0730 PREPARE AREA 4 FOR INITIAL WFO OPS.

1100 CONFERENCE CALL.

1700 SECURED.

*[Handwritten signature]*

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 8 March 2019  
 Site Location: 4825 Glenbrook Road

Weather:  
 33/37 winds 5-10

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Breyman, Mark	Askew, Tom	
Castell, Lorna	Heffelfinger, Gerald	Bartosh, Ian	
Courtney, Kenneth	Prate, Warren	Caldwell, Jeff	
Holloway, April	Rutana, Steve	Dusick, Brandon	
Jackson, Matthew	Wright, David	Heard, Irvin	
Luckanavage, Kyle	Yorkshire, Bart	Jones, LaMarcus	
Marion, Jedidiah		Kirby, Anna	
Matter, Phillip		McClellan, Dale	
Nelms, Bobby	<b>LIFE STAR</b>	McGill, Andre	
Oien, Joshua	Jackson, Mark	Wainwright, LeRoy	
Rider, Matthew	Brooke, Bailey		
Schlosser, Ariel			
Wunschel, Scott		<b>CEHNC</b>	
Banks, Janelle	<b>ACCUPERMIT</b>	Boles, Judson	
	Overton, Robert		
	Williams, Angelo	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive activities today. Pumped 2925 gallons of water today. Lined 3 rolloffs. Issue with rolloff truck.

End of day: 11:30

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

**Problems encountered/resolutions:**

Rolloff truck has a serious hydraulic leak which will need to be repaired before further use.

**Instructions given by government personnel:****Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

66 3-8-19

0630 SAFETY BRIEF

0700 RADIO CHECKS

0730 PUMPING WATER

1750 SECURED

~~Handwritten signature~~

**SPRING VALLEY, WASHINGTON DC**

**Contract No:** W912DY-09-D-0062  
**Delivery Order:** TO 0006  
**Date:** 11 March 2019  
**Site Location:** 4825 Glenbrook Road

**Weather:**  
 49/60 partly sunny

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Breyman, Mark	Alvano, Lou	
Castell, Lorna	Heffelfinger, Gerald	Askew, Tom	
Courtney, Kenneth	Prate, Warren	Bartosh, Ian	
Holloway, April	Rutana, Steve	Caldwell, Jeff	
Jackson, Matthew	Wright, David	Heard, Irvin	
Luckanavage, Kyle	Yorkshire, Bart	Jones, LaMarcus	
Marion, Jedidiah		McClellan, Dale	
Matter, Phillip		McGill, Andre	
Nelms, Bobby	<b>LIFE STAR</b>	Wainwright, LeRoy	
Oien, Joshua	Alfaro, Walter	Wooten, Mike	
Rider, Matthew	Robinson, Omar		
Schlosser, Ariel			
Wunschel, Scott		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Overton, Robert		
	Williams, Angelo	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No monitored intrusive today, 2 rollofs of clean backfill removed. Pumped 4600 gallons of water out of Area 4.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

**Problems encountered/resolutions:**

**Instructions given by government personnel:**

**Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

07 3-11-19

0630 SAFETY BRIEF

0700 RADIO CHECKS

0750 PUMPING WATER

1354 REMOVING CLEAN BACKFILL  
FROM AREA 4.

1700 SECURED

*[Handwritten signature]*



## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 12 March 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 38/60 gentle winds

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Breyman, Mark	Alvano, Lou	
Castell, Lorna	Heffelfinger, Gerald	Askew, Tom	
Courtney, Kenneth	Prate, Warren	Bartosh, Ian	
Holloway, April	Rutana, Steve	Heard, Irvin	
Jackson, Matthew	Wright, David	Jones, LaMarcus	
Luckanavage, Kyle	Yorkshire, Bart	McClellan, Dale	
Marion, Jedidiah		McGill, Andre	
Matter, Phillip		Pushley, Ed	
Nelms, Bobby	<b>LIFE STAR</b>	Wainwright, LeRoy	
Oien, Joshua	Alfaro, Walter	Wooten, Mike	
Rider, Matthew	Jackson, Mark		
Schlosser, Ariel			
Wunschel, Scott		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Overton, Robert		
	Williams, Angelo	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No monitored intrusive operations, 2 rolloffs of clean backfill removed from Area 4. HAZMAT shipment 2 box trucks and 2 water tanker trucks.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

R

68 3-12-19

0630 SAFETY BRIEF

0700 RADIO CHECKS

0743 MINICAMS UP REMOVING CIGAR  
PACKS FROM 'AREA 4.

1140 STARTING MID DAY

1220 MIDDAY COMPLETE

1700 SECURED

R  
S

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 13 March 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 38/57, calm winds

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Breyman, Mark	Alvano, Lou	
Castell, Lorna	Heffelfinger, Gerald	Askew, Tom	
Courtney, Kenneth	Prate, Warren	Bartosh, Ian	
Holloway, April	Rutana, Steve	Caldwell, Jeff	
Jackson, Matthew	Wright, David	Heard, Irvin	
Luckanavage, Kyle	Yorkshire, Bart	Jones, LaMarcus	
Marion, Jedidiah		McClellan, Dale	
Matter, Phillip		McGill, Andre	
Nelms, Bobby	<b>LIFE STAR</b>	Wainwright, LeRoy	
Oien, Joshua	Alfaro, Walter	Wooten, Mike	
Rider, Matthew	Gumbs Vines, Doreen		
Schlosser, Ariel			
Wunschel, Scott		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Overton, Robert		
	Williams, Angelo	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No monitored intrusive today. Pumped 2550 gallons of water from Area 1. Surveyed the extent of excavation in Area 3 as head space and lo levels came back negative, then backfilled Area 3. Built a parking pad for the ambulance in the former area 3. 2 HAZ water trucks removed water from Fed Prop.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

69

3-13-19

0630 SAFETY BRIEF

0700 RADIO CHECKS

0737 PUMPING WATER FROM EXCAVATION.

0930 SEAN BUCKLEY ON SITE TO DISCUSS

ACTIONS TO BE TAKEN IN THE

PDS WORK/IF THERE ARE SMELLS

COMING FROM EXCAVATION 4.


NOTE: MINICAMS UP @ 08:18.

1130 MIDDAY CHALLENGE

1150 MIDDAY CHALLENGE COMPLETE

1230 BACK FILLING AREA 3.

1700 SECURED

A large, stylized handwritten signature, likely "Ryan", is written across the lower half of the page. A diagonal line is drawn from the bottom left corner of the page, passing through the signature.

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 14 March 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 48/69 clear, mostly sunny

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Breyman, Mark	Alvano, Lou	
Castell, Lorna	Heffelfinger, Gerald	Askew, Tom	
Courtney, Kenneth	Prate, Warren	Bartosh, Ian	
Holloway, April	Rutana, Steve	Caldwell, Jeff	
Jackson, Matthew	Wright, David	Heard, Irvin	
Luckanavage, Kyle	Yorkshire, Bart	Jones, LaMarcus	
Marion, Jedidiah		McClellan, Dale	
Matter, Phillip		McGill, Andre	
Nelms, Bobby	<b>LIFE STAR</b>	Wainwright, LeRoy	
Oien, Joshua	Gumbs Vines, Doreen	Wooten, Mike	
Rider, Matthew	Haupt, Calvin		
Schlosser, Ariel			
Wunschel, Scott		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Overton, Robert		
	Williams, Angelo	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No monitored intrusive operations. Dug a sump in former arsenic area of Area 1. Safety issue with stairs to lowest level, had to readjust and revamp stairs. Set up mitigation tarps for Area 4 and other mitigation items. Replaced torn sandbags on fence perimeter. Pumped 1700 gallons of water from Area 1.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**

DC Water : 2 people asking about water meters.

**Contractors**

Berkel ( )

DAVEY ( )

ACCUPERMIT ( )

ACI (0)

CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



R

70 3-14-19

0630 SAFETY BRIEF

0700 RADIO CHECKS

0750 PREP'ING AREA "A" DIGGING SUMP.

1029 COLLECTED VOC. TOLL OFF 291436

1205 VOC COLLECTED TOLL OFF 290959

1235 COMPOSITE COLLECTED

1327 PREP'ING TO GRAVEL SUMP.

1700 SECURED

~~R  
H~~



## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 15 March 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 63/70 over cast

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Breyman, Mark	Alvano, Lou	
Castell, Lorna	Heffelfinger, Gerald	Askew, Tom	
Courtney, Kenneth	Prate, Warren	Bartosh, Ian	
Holloway, April	Rutana, Steve	Caldwell, Jeff	
Jackson, Matthew	Wright, David	Heard, Irvin	
Luckanavage, Kyle	Yorkshire, Bart	Jones, LaMarcus	
Marion, Jedidiah		McClellan, Dale	
Matter, Phillip		McGill, Andre	
Nelms, Bobby	<b>LIFE STAR</b>	Wainwright, LeRoy	
Oien, Joshua	Brooke, Bailey	Wooten, Mike	
Rider, Matthew	Jackson, Mark		
Schlosser, Ariel			
Wunschel, Scott		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Overton, Robert		
	Williams, Angelo	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive operations today. Finished the sump in Area 1 and finished the stair repair.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information  
 \_\_\_\_\_  
 \_\_\_\_\_

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

R

71

3-15-19

0630 SAFETY BRIEF

0700 RADIO CHECKS

1700 SECURED

*[Handwritten signature]*

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 18 March 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 41/50 overcast

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Breyman, Mark	Askew, Tom	
Castell, Lorna		Bartosh, Ian	
Courtney, Kenneth	Prate, Warren	Caldwell, Jeff	
Holloway, April	Rutana, Steve	Doyle, Satchell	
Jackson, Matthew	Wright, David	Heard, Irvin	
Luckanavage, Kyle	Yorkshire, Bart	Jones, LaMarcus	
Marion, Jedidiah		McClellan, Dale	
Matter, Phillip		McGill, Andre	
Nelms, Bobby	<b>LIFE STAR</b>	Perkins, Stephen	
Oien, Joshua	Brooke, Bailey	Wainwright, LeRoy	
Rider, Matthew	Jackson, Mark	Wooten, Mike	
Schlosser, Ariel			
Wunschel, Scott		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Overton, Robert		
	Williams, Angelo	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive activities today. Weighed approximately 200 drums for HAZ shipment coming up. Pumped out approximately 150 gallons out of the new sump. Got dump truck in so we can remove clean backfill off of Area 4.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

72 3-18-19

0630 SAFETY PRIBT

0724 Radio checks Complete.

0755 Tm 1 excavating clean fill from area 4.

1700 Shutdown

*[Handwritten signature]*

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 19 March 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 34/53 sunny

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Breyman, Mark	Askew, Tom	
Castell, Lorna	Heffelfinger, Gerald	Bartosh, Ian	
Courtney, Kenneth		Caldwell, Jeff	
Holloway, April	Rutana, Steve	Doyle, Satchell	
Jackson, Matthew	Wright, David	Heard, Irvin	
Luckanavage, Kyle	Yorkshire, Bart	McClellan, Dale	
Marion, Jedidiah		McGill, Andre	
Matter, Phillip		Perkins, Stephen	
Nelms, Bobby	<b>LIFE STAR</b>	Wainwright, LeRoy	
Oien, Joshua	Gumbs Vines, Doreen	Wooten, Mike	
Rider, Matthew	Jackson, Mark		
Schlosser, Ariel			
Wunschel, Scott		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Overton, Robert		
	Williams, Angelo	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations in Area 4. Removed 1 dump truck of clean backfill from Area 4, then proceed to monitored intrusive operations. 39 drums of soil removed. Fed Property electrical issues repaired, guard shack lighting and cameras.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information  
 \_\_\_\_\_  
 \_\_\_\_\_

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
_____	Berkel ( )
_____	DAVEY ( )
_____	ACCUPERMIT ( )
_____	ACI (0)
_____	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	





P  
1

3-19-19

0630 SAFETY BRIEF

0724 RADIO CHECK

0748 MINICAMS OP

0755 EXCAVATING CISTERN BACK HILL AREA 4.

0950 TEAM 2 DOWN RANGE LEVEL "B"

2100 CISTERN HEFTED FINGER.

1029 VOC COLLECTED

1105 PPE CHECK

1105 SOIL DRUMS 2715-2729 FILLED.

TEAM 2 CLEARED PDS.

1149 SOIL DRUMS 2715-2729 LOADED FOR FEED

1200 STOPPING MID DAY

1219 MID DAY COMPLETE

1300 TEAM 1 DOWN RANGE LEVEL "B"

1327 PPE CHECKS

1457 SOIL DRUMS 2730-2753 FILLED.

1438 COMPOSITE COLLECTED

1446 TEAM 1 CLEARED PDS

1514 SOIL DRUMS 2730-2744 LOADED FOR FEED

1540 SOIL DRUMS 2745-2753 LOADED FOR FEED

1710 SECURED



## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 20 March 2019  
 Site Location: 4825 Glenbrook Road

Weather:  
 36/56 overcast

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Breyman, Mark	Askew, Tom	
Castell, Lorna	Heffelfinger, Gerald	Bartosh, Ian	
Courtney, Kenneth	Prate, Warren	Caldwell, Jeff	
Holloway, April	Rutana, Steve	Doyle, Satchell	
Jackson, Matthew	Wright, David	Heard, Irvin	
Luckanavage, Kyle	Yorkshire, Bart	McClellan, Dale	
Marion, Jedidiah		McGill, Andre	
Matter, Phillip		Perkins, Stephen	
Nelms, Bobby	<b>LIFE STAR</b>	Wainwright, LeRoy	
Oien, Joshua	Gumbs Vines, Doreen	Wooten, Mike	
Rider, Matthew	Richardson, Elliott		
Schlosser, Ariel			
Wunschel, Scott		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Overton, Robert		
	Williams, Angelo	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations in Area 4, 48 drums filled.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



P<sub>4</sub>

2

3-20-19

0630

SAFETY BRIEF

0700

RADIO CHECKS.

0747

MINICAMS AND DRAWS UP

0803

TEAM 2 DOWN RANGE LEVEL "B" RIDGE

CASTLE, BRYAN.

0816

VOC COLLECTED.

0834

PPE CHECKS.

0937

SOIL DRUMS 2754-2777 FILLED

0951

TEAM 2 CLEARED PDS

1015

SOIL DRUMS 2754-2768 LOADED FOR FED

SOIL DRUMS 2769-2777 &amp; PPE DRUM 455

LOADED FOR FED.

1100

STARTING MID DAY CHALLENGE

1110

BROOK BROTHER, DAVID KINE AND

JEFF NOTT ON SITE TO DISCUSS AREA "2".

1120

MID DAY COMPLETE

1213

TEAM 1 DOWN RANGE LEVEL "B" OVER

JACKSON HOFFERLAND.

1240

PPE CHECK

1327

PPE CHECK

1350

SOIL DRUMS 2778-2801 FILLED

1405

COMPOSITE COLLECTED.

1410

TEAM 1 CLEARED PDS

1437

SOIL DRUMS 2778-2792 LOADED FOR FED

# SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 21 March 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 36/53 Heavy rains

## Personnel on Site

PARSONS	ZES	ECBC	
Blevins, Robert	Breyman, Mark	Askew, Tom	
Castell, Lorna	Heffelfinger, Gerald	Bartosh, Ian	
Courtney, Kenneth	Prate, Warren	Caldwell, Jeff	
Holloway, April	Rutana, Steve	Doyle, Satchell	
Jackson, Matthew		Heard, Irvin	
Luckanavage, Kyle	Yorkshire, Bart	McClellan, Dale	
Marion, Jedidiah		McGill, Andre	
Matter, Phillip		Perkins, Stephen	
Nelms, Bobby	LIFE STAR	Wainwright, LeRoy	
Oien, Joshua	Gumbs Vines, Doreen	Wooten, Mike	
Rider, Matthew	Haupt, Calvin		
Schlosser, Ariel			
Wunschel, Scott		CEHNC	
	ACCUPERMIT	Boles, Judson	
	Overton, Robert		
	Williams, Angelo	CENAB	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Very heavy rains, no intrusive operations today. Unloaded 400 soil drums from Uline. Sent crews home at 1030, as heavy rains were not slowing down. Total rain received today 2.85"

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

### Visitors


### Contractors

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



Pg

4

3-21-19

0630 SAFETY BRIEF.

0700 RADIO CHECKS

0730 THE TEAM AT FED PROPERTY  
FOR NEW BARREL SHIPMENT

1100 CONFERENCE CALL.

1200 SITE SHUTDOWN DUE TO WEATHER  
"RAIN"

*[Handwritten signature]*





R

5 3-22-19

0630 SAFETY BRIEF

0700 RADIO CHECK

0740 MINICAMS UP

0750 PUMPING WATER

1600 STARTING END OF WEEK  
MAINTENANCE.

1700 SECURED

*[Handwritten signature]*

# SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 25 March 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 48/61 partly cloudy

## Personnel on Site

PARSONS	ZES	ECBC	
Blevins, Robert	Breyman, Mark	Askew, Tom	
Castell, Lorna	Heffelfinger, Gerald	Bartosh, Ian	
Courtney, Kenneth	Prate, Warren	Caldwell, Jeff	
Holloway, April		Doyle, Satchell	
Luckanavage, Kyle	Wright, David	Heard, Irvin	
Marian, Jedidiah	Yorkshire, Bart	McClellan, Dale	
Matter, Phillip		McGill, Andre	
Nelms, Bobby		Nguyen, Phuong	
Oien, Joshua	LIFE STAR	Wainwright, LeRoy	
Rider, Matthew	Brooke, Bailey	Wooten, Mike	
Schlosser, Ariel	Richardson, Elliott		
Wunschel, Scott			
		CEHNC	
		Boles, Judson	
	ACCUPERMIT		
	Overton, Robert		
	Williams, Angelo		
		CENAB	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations in Area 4, 41 drums filled. Medical ran a little late due to a broken down ambulance, which was replaced.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information  
 \_\_\_\_\_  
 \_\_\_\_\_

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

## **Problems encountered/resolutions:**

1030AM: miniCAMS hit for CG, determined to be bad miniCAMS which was replaced.

## **Instructions given by government personnel:**

## **Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



P  
19

b 3-25-19

0630 SAFETY BRIEF

0700 RADIO CHECKS

0750 MINICAMS UP.

0815 DAAMS PUMPS RUNNING.

0835 TEAM 2 DOWN RANGE LEVEL B

RIDER, CASTELL, PROYMAN.

0844 VOC COLLECTED

1000 SOIL DRUMS 2802-2821 FILLED

1002 CG REPORTED @ EXCAVATION 28.1

1020 CG REPORTED @ EXCAVATION 3RD CYCLE 27.8  
SUSPECTED ELECTRICAL ISSUE.

1023 THE EXCAVATION MITIGATED.

PROCESSING THE DOWN RANGE TEAM.

Notes 2nd cycle 27.1 CG

1034 TEAM 2 CLEARED PDS.

1040 REPLACING THE EXCAVATION MINICAMS.

1143 MINICAMS BACK UP

1213 SOIL DRUMS 2802-2816 LOADED FOR FED.

1256 SOIL DRUMS 2817-2821 LOADED FOR FED.

1302 TEAM 1 DOWN RANGE LEVEL B

DIEN, COURTNEY, WELCH.

1443 SOIL DRUMS 2822-2842 FILLED.

1449 COMPOSITE COLLECTED

1452 TEAM 1 CLEARED PDS.





[illegible]

Pg

8 3-26-19

- 0630 SAFETY BRIEF
- 0715 RADIO CHECK
- 0748 MINICAMS UP.
- 0825 SOIL DRUMS 2837-2842 & SCR  
DRUM 589 LOADED FOR FED.
- 0832 TEAM 2 DOWN RANGE LEVEL "B" RIDER  
BLOWING, HEFFELFINGER
- 0846 VOC COLLECTED
- 0928 MINICAMS REPORTS "L" @ DRUM  
FILLING .49
- 0938 2<sup>nd</sup> cycle .58 "L" DRUM FILLING  
THE TEAM STARTING MITIGATION  
OF DRUMS AND EXHAUSTION
- 0948 3<sup>rd</sup> cycle .43 "L" @ DRUM FILLING.
- 1007 THE TEAM CIRCLED PAS W/ DAMMS  
@ DRUM FILLING.
- 1008 4<sup>th</sup> cycle .20 "L"
- 1018 5<sup>th</sup> cycle .17 ALL PM'S HAVE  
BEEN NOTIFIED. ECBC ARE  
ANALYZING TUBES.
- 1111 USACE REPORTS THAT THE DAMMS  
TUBES WERE CLEAR FOR AGENT.
- 1130 STARTING MID DAY CHALLENGE
- 1143 MID DAY COMPLETE





P  
19

10 3-27-19

0630 SAFETY BRIEF

0700 RADIOS CHECKS.

0745 MINICAMS UP

0800 DAMS PUMPS RUNNING.

0845 TEAM 2 DOWN RANGE LEVEL "B"

RIDER, CASTLE, REEYMAN.

0855 GRAB SAMPLE FROM AREA 4

SOIL BARREL 2853 COMPLETE.

0900 COMPOSITE SAMPLE FOR BARRELS

2843-2853 COLLECTED.

0910 VOC COLLECTED

0930 PPE CHECK

1001 SOIL DRUMS 2854-2869 FILLED.

1009 TEAM 2 CLEARED PDS.

1034 SOIL DRUMS 2843-2857 LOADED  
FOR FED.1053 SOIL DRUMS 2858-2869 LOADED  
FOR FED.

1140 DCC WATER ON SITE

1145 STARTING MIDDAY

1157 MIDDAY COMPLETE

1222 TEAM 1 DOWN RANGE LEVEL "B"

1251 PPE CHECK

1358 PPE CHECK





[illegible]

Pg

12 3-28-19

0630 SAFETY BRIEF

0700 RADIO CHECK

0740 MINICAMS UP.

0750 BARRIS PUMPS RUNNING.

0814 TEAM 2 DOWN RANGE COVER "B".

RIDER, BLOVINS, WRIGHT.

0827 VOC COLLECTED.

0840 PPE CHECK.

0846 MINICAMS 1' L" .40 @ EXCAVATION "L".

.45 @ DRUM FILLING. VOC 2.3 EXCAVATION

VOC 1.5 DRUM FILLING. MITIGATED DRUMS.

0855 "L" .30 EXCAVATION. "L" .31 DRUM FILLING

2ND CYCLE. VOC 2.3 / 1.5 RESPECTIVELY

TEAM MITIGATING EXCAVATION.

0906 "L" .24 EXCAVATION "L" .23 DRUM FILLING.

0916 "L" .19 EXCAVATION "L" .16 DRUM FILLING.

0926 "L" .11 EXCAVATION "L" .11 DRUM FILLING.

0936 BARRIS PUMPS/TUBES @ EXCAVATION

AND DRUM FILLING STATIONS. WILL BE

ANALYZED. THE TEAM CIGARET PDS.

ALL DMS WERE NOTIFIED. TEMP 44°

1100 STARTING MIDDAY CHALLENGE

1135 MIDDAY CHALLENGE COMPLETE

1242 TEAM 1 DOWN RANGE COVER "B" GLEN, SCHWARTZ



Pg

14 3-29-19

0630 SAFETY BRIEF

1400 PDU CALL

1500 SEU PDB

0759 1st team down before 1st  
 0800 2nd team down before 1st  
 0801 3rd team down before 1st

0901 1st team down before 1st  
 0902 2nd team down before 1st

1000 3rd team down before 1st  
 1001 4th team down before 1st

1100 5th team down before 1st  
 1101 6th team down before 1st

1200 7th team down before 1st  
 1201 8th team down before 1st

1300 9th team down before 1st  
 1301 10th team down before 1st

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 1 April 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 38/54 partly cloudy

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Breyman, Mark	Bartosh, Ian	
Castell, Lorna	Prate, Warren	Burrell, Dianne	
Courtney, Kenneth	Wright, David	Duff, Todd	
Holloway, April	Yorkshire, Bart	Harris, Brian	
Luckanavage, Kyle		Jones, LaMarcus	
Marian, Jedidiah		King, Bernard	
Matter, Phillip		Privett, Arlita	
Nelms, Bobby		Skipper, Brandon	
Oien, Joshua	<b>LIFE STAR</b>	Smith, Ethan	
Rider, Matthew	Gumbs Vines, Doreen	Wooten, Mike	
Schlosser, Ariel	Richardson, Elliott		
Wunschel, Scott			
		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Overton, Robert		
	Williams, Angelo	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Inserted 1 DAAMS pump under Area 4 excavation mitigation tarp and ran for 1 hour then recovered pump and mitigation. Prepared Area 1 for intrusive operations, which started today and 24 drums were filled.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

**Problems encountered/resolutions:**

A natural spring in on eastern edge of Area 1 so we will direct flow to the sump.

**Instructions given by government personnel:**

Install 1 DAAMS pump under Area 1 excavation mitigation and run for 1 hour, then recover and fix mitigation.

**Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	





P<sub>4</sub>

15

4-1-19

0630 SAFETY RIDER

0700 RADIO CHECK

0750 DAMS PUMPS RUNNING

0759 TEAM 1 DOWN RANGE LEVEL "B"

DOWN COURNOY. PLACE DAMS  
IN AREA "4" MINI CAMS UP.0901 TEAM 1 RETRIEVED DAMS FROM  
AREA 4.

0905 TEAM 1 CLEARED PDS.

1000 SOIL DRUMS 2897-2903 &amp; PPE DRUMS

458/459 LOADED FOR TROOP PRIMARY

1140 STARTING MIDDAY CHALLENGE

1155 MIDDAY COMPLETE

1250 THE DAMS PERIMETER PUMPS

FROM AREA 4 WERE COLLECTED

AREA 1 DAMS &amp; MINI CAMS IN PLACE.

1326 TEAM 2 DOWN RANGE LEVEL "B"

RIDER, CASTLE, BRYAN. AREA 1.

1340 VOL COLLECTED

1525 Camp Sample Complete.

1536 Tm 2 clear of PDS.

1700 SECURED

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 2 April 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 38/53 partly cloudy, late rain

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Breyman, Mark	Bartosh, Ian	
Castell, Lorna	Prate, Warren	Burrell, Dianne	
Courtney, Kenneth	Wright, David	Duff, Todd	
Holloway, April	Yorkshire, Bart	Harris, Brian	
Luckanavage, Kyle		Jones, LaMarcus	
Marian, Jedidiah		King, Bernard	
Matter, Phillip		Privett, Arlita	
Nelms, Bobby		Skipper, Brandon	
Oien, Joshua	<b>LIFE STAR</b>	Smith, Ethan	
Rider, Matthew	Gumbs Vines, Doreen	Wooten, Mike	
Schlosser, Ariel	Brooke, Bailey		
Wunschel, Scott			
		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Vargas, Brian		
	Vargas, Gustavo	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations in Area 1, eastern edge. 37 drums filled, minor miniCAMS issue during midday only slight delay.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

[illegible]

Pg

16

42-19

0630 SAFETY BRIEF

0700 RADIO CHECK

0752 SOIL DRUMS 2904-2918 LOADED

FOR FEDERAL PROPERTY.

0754 MINICAMS UP.

0809 SOIL DRUMS 2919-2927 LOADED FOR FED.

0846 DAMS PUMPS UPS IN PLACE

0917 VOC COLLECTED.

0933 PPE CHECK

1028 PPE CHECK

1118 SOIL DRUMS 2928-2951 FILLED.

1126 TEAM 2 CLEARED PDS. STARTING MID DAY

1157 SOIL DRUMS 2928-2942 LOADED FOR FED

1219 SOIL DRUMS 2943-2951 LOADED FOR FED.

1212 MINICAMS UP @ 1302

1323 TEAM 1 DOWN RANGE LEVEL 2" OVER

COURTESY, BREYMAN.

1400 PPT CALL

1440 PPE CHECK

1505 PPT CALL COMPLETE

1517 SOIL DRUMS 2952-2964 FILLED

1530 COMPOSITE COLLECTED

1535 TEAM 1 CLEARED PDS.

1700 SECURED

RW







Pg

17 4-3-19

0630 SAFETY BRIEF

0700 RADIO CHECKS

0755 SOIL DRUMS 2952-2964 LOADED

PPE DRUM 460 LOADED.

0753 MINICAMS UP.

0833 DAPMS PUMPS RUNNING

0855 TEAM 2 DOWN RANKE LEVEL "K"  
TRIDER CASTELL, BROGMAN.

0902 V6 C COLLECTED

0930 PPE CHECK

1015 PPE CHECK

1047 PPE CHECK

1117 TEAM 2 CLEARED POS.

1127 STARTING MIDDAY CHANGE.

1142 SOIL DRUMS 2965-2979 LOADED FOR FEO.

1155 MIDDAY COMPLETE.

1210 SOIL DRUMS 2980-2987, SCR DRUMS 590/591  
LOADED FOR FEO.1342 TEAM 3 DOWN RANKE LEVEL "K" LUCKANAHOLE  
MINIHO WPHAT

1410 PPE &amp; Monitor Check Complete.

1440 PPE &amp; Monitor Check Complete.

1445 Team Found what they believe to be the Sewer  
line to 4835.

1510 Team Suspended excavating.

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 4 April 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 48/67 partly cloudy

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Breyman, Mark	Bartosh, Ian	
Castell, Lorna	Prate, Warren	Burrell, Dianne	
Courtney, Kenneth	Wright, David	Duff, Todd	
Holloway, April	Yorkshire, Bart	Harris, Brian	
Luckanavage, Kyle		Jones, LaMarcus	
Marian, Jedidiah		King, Bernard	
		Privett, Arlita	
Nelms, Bobby		Skipper, Brandon	
Oien, Joshua	<b>LIFE STAR</b>	Smith, Ethan	
Rider, Matthew	Gumbs Vines, Doreen	Wooten, Mike	
Schlosser, Ariel	Haupt, Calvin		
Wunschel, Scott			
		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Vargas, Brian		
	Vargas, Gustavo	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations in Area 1, 24 drums filled. Temperature above 75 degrees ended intrusive operations at 13:30.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

**Problems encountered/resolutions:**

Temperature above 75 degrees, intrusive ops stopped. DC Water had an employee walk onto our site unauthorized, he was talked to by Mr. Boles and Mr. Steelman.

**Instructions given by government personnel:****Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



R

19 4-4-19

0630 SAFETY BRIEF

0700 RADIO CHECK

0805 SOIL DRUMS 2988-3002 LOADED  
FOR FEB: PROPERTY.

0853 MINICAMS UP

0842 SOIL DRUMS 3003-3005 LOADED FOR FEB

0912 TEAM 2 DOWN RATTLE LEVEL "B" RIDER  
REVINS WRIGHT.

0933 PPE CHECK

0944 VOC COLLECTED

1024 PPE CHECK

1100 SOIL DRUMS 3006-3018 FILLED

1108 TEAM 2 CLEARED PDS.

1128 SOIL DRUMS 3006-3018 LOADED FOR FEB.

1130 STARTING MID DAY

1146 MID DAY LUNCH

1242 TEAM 1 DOWN RATTLE LEVEL "B" OVER  
CURRING PROGRAM.

1309 PPE CHECK

1337 SOIL DRUMS 3019-3030 FILLED.

1338 STOPPED INTENSIVE OPS DUE TO TEMP 77F

1345 COMPOSITE COLLECTED

1351 TEAM 1 CLEARED PDS

1700 SECURED

R. R. R.

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 5 April 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 48/53 rain

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Breyman, Mark	Bartosh, Ian	
Castell, Lorna	Prate, Warren	Burrell, Dianne	
Courtney, Kenneth	Wright, David	Duff, Todd	
Holloway, April	Yorkshire, Bart	Harris, Brian	
Luckanavage, Kyle		Jones, LaMarcus	
Marian, Jedidiah		King, Bernard	
		Privett, Arlita	
Nelms, Bobby		Skipper, Brandon	
Oien, Joshua	<b>LIFE STAR</b>	Smith, Ethan	
Rider, Matthew	Brooke, Bailey	Wooten, Mike	
Schlosser, Ariel	Jackson, Mark		
Wunschel, Scott			
		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Vargas, Brian		
	Vargas, Gustavo	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations in Area 1, 44 drums filled. No heat issues today.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information  
 \_\_\_\_\_  
 \_\_\_\_\_

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	





P<sub>7</sub>

20 4-5-09

0630 SAFETY BRIEF

0700 RADIO CHECK

0753 MINICAMS UP

0807 DAMS PUMPS UP.

0830 TEAM 2 DOWN RANGE LEVEL "B" RIDER  
CASTER, BREYMAN.

0839 VOC COLLECTED

0910 PPE CHECK

0937 PPE CHECK

1036 SOIL DRUMS 3031-3054 FILLED

1044 TEAM 2 CLEARED POS

SOIL DRUMS 3031-3045 LOADED FOR FED

1130 SOIL DRUMS 3046-3054, SCR 592

LOADED FOR FED PROPERTY, STARTING MIDDAY

1216 MIDDAY COMPLETE,

1304 TEAM 1 DOWN RANGE LEVEL "B"

OEN, CARRERA, WRIGHT.

1330 PPE CHECK

1400 PPE CHECK

1441 SOIL DRUMS 3055-3074 FILLED.

1450 COMPOSITE COLLECTED

1500 TEAM 1 CLEARED POS

1702 SECURED



## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 8 April 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 81 degrees and overcast, winds 5-10 mph

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Breyman, Mark	Bartosh, Ian	
Castell, Lorna	Prate, Warren	Burrell, Dianne	
Courtney, Kenneth	Wright, David	Duff, Todd	
Holloway, April	Yorkshire, Bart	Harris, Brian	
Luckanavage, Kyle		Jones, LaMarcus	
Marian, Jedidiah		King, Bernard	
Matter, Phillip		Privett, Arlita	
Nelms, Bobby		Skipper, Brandon	
Oien, Joshua	<b>LIFE STAR</b>	Smith, Ethan	
Rider, Matthew	Brooke, Bailey	Wooten, Mike	
Schlosser, Ariel	Jackson, Mark		
Wunschel, Scott			
		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Vargas, Brian		
	Vargas, Gustavo	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations in Area 1, 8 drums filled before the temperature exceeded 75 degrees at 0957. Set up 110 gallons of decon water for the PDS to use as the city water supply will be shut off tomorrow. Moved stairs to make room for access to Area 5 for future work. Yard hydrant is leaking called our plumbing subcontractor ACI to come and repair it.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



R<sub>7</sub>

21 4-8-19

0630 RADIO CHECKS &amp; SAFETY BRIEF

0747 SOIL DRUMS 3055-3069 LOADED  
FOR FED.0822 SOIL DRUMS 3070-3074 LOADED  
FOR FED.

0837 MINICAMS UP @ 0801, DRUMS @ 0830.

0857 TEAM 2 DOWN RANGE LEVEL 2.

RIGOR, BLOVINS, WRIGHT.

0907 VOC COLLECTED.

0920 PPE CHECK

0947 PPE CHECK

0958 SUSPENDED INTRUSING OPS DUE TO TEMP.

1002 SOIL DRUMS 3075-3082 FILLED, AND  
COMPOSITE COLLECTED.


1007 TEAM 2 CLEARED POS.

1040 SOIL DRUMS 3075-3082 LOADED FOR FED

PPE DRUM 461, AQ DRUM 668 LOADED

FOR FED PROPERTY

1700 SECURED



## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 9 April 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 61/80 hazy

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Breyman, Mark	Bartosh, Ian	
Castell, Lorna	Prate, Warren	Burrell, Dianne	
Courtney, Kenneth	Wright, David	Duff, Todd	
Holloway, April	Yorkshire, Bart	Harris, Brian	
Luckanavage, Kyle		King, Bernard	
Marian, Jedidiah		McGill, Andre	
Matter, Phillip		Miller, Dan	
Nelms, Bobby		Privett, Arlita	
Oien, Joshua	<b>LIFE STAR</b>	Skipper, Brandon	
Rider, Matthew	Alfaro, Walter	Smith, Ethan	
Schlosser, Ariel	Jackson, Mark	Threadgill, Marcus	
Wunschel, Scott			
		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Overton, Robert		
	Williams, Angelo	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations in Area 1, 27 drums filled. Pumped 350 gallons of water. Dug out yard hydrant in preparation for ACI to repair a leak. At 11:07 the temperature reached 75 degrees and level B operations were halted.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

**Problems encountered/resolutions:**

Water to our site was shut-off by DC water, we set up a temporary decon water supply and pump.

**Instructions given by government personnel:****Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

[illegible]



Pg

22 4-9-19

0630 SAFETY BRIEF

0700 RADIO CHECK

0723 DC WATER HAS SHUT OFF WATER.

0745 MINICAMS UP

0750 DAAMS PUMPS RUNNING.

0805 TEAM 1 DOWN RANGE LEVEL "B" OPEN

CINEMAX, BRYMAN.

0837 PPE CHECK VOC COLLECTED

0912 PPE CHECK

0947 PPE CHECK

1040 SOIL DRUMS 3083-3109 FILLED

1057 COMPOSITE COLLECTED

1100 TEAM 1 CLEARED PDS.

1210 PUMPING WATER FROM AREA 1

1347 SOIL DRUMS 3083-3107 LOADED FOR FEO.

1416 SOIL DRUMS 3098-3109 LOADED FOR FEO.

1700 SECURED.

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 10 April 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 53/76 winds 5-15mph

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Breyman, Mark	Bartosh, Ian	
Castell, Lorna	Prate, Warren	Burrell, Dianne	
Courtney, Kenneth	Wright, David	Duff, Todd	
Holloway, April	Yorkshire, Bart	King, Bernard	
Luckanavage, Kyle		McGill, Andre	
Marian, Jedidiah		Miller, Dan	
Matter, Phillip		Privett, Arlita	
Nelms, Bobby		Skipper, Brandon	
Oien, Joshua	<b>LIFE STAR</b>	Smith, Ethan	
Rider, Matthew	Alfaro, Walter	Threadgill, Marcus	
Schlosser, Ariel	Gumbs Vines, Doreen		
Wunschel, Scott			
		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Overton, Robert		
	Williams, Angelo	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive Area 1, 18 drums filled from area on 4835 side. At 1321 the temperatures exceeded 75 degrees and we ended intrusive operations.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



Pg

23 4-10-19

0630 SAFETY BRIEF

0700 RADIO CHECK

0745 MINICHMS UP.

0822 TEAM 2 DOWN RANGE LEVEL "B".

RIDER, CASPIL, URIGHT,

0845 PPE CHECK

0910 PPE CHECK

0939 PPE CHECK

0958 SOIL DRUMS 3110-3120 FILLED.

1003 TEAM 2 CLEARED POS.

1045 SOIL DRUMS - 3110-3120, SCL 593,  
PPE 462 LOADED FOR FED PROPERTY.

1120 STARTING MIDDAY

1135 MIDDAY COMPLETE

1230 TEAM 1 DOWN RANGE LEVEL "B" OPEN

COURTNEY, BRYAN

1239 VOL COLLECTED.

1300 PPE CHECK

1321 COMPOSITE COLLECTED, SOIL DRUMS

3121-3127 FILLED. INTENSIVE OPERATIONS  
SUSPENDED DUE TO TEMPERATURE.

1329 TEAM 1 CLEARED POS.

1340 SOIL DRUMS 3121-3127, SCL 594

LOADED FOR FED

# SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 11 April 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 53/66 partly cloudy

## **Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Breyman, Mark	Bartosh, Ian	
Castell, Lorna	Prate, Warren	Burrell, Dianne	
Courtney, Kenneth	Wright, David	Duff, Todd	
Holloway, April	Yorkshire, Bart	King, Bernard	
Luckanavage, Kyle		McGill, Andre	
Marian, Jedidiah		Miller, Dan	
Matter, Phillip		Privett, Arlita	
Nelms, Bobby		Skipper, Brandon	
Oien, Joshua	<b>LIFE STAR</b>	Smith, Ethan	
Rider, Matthew	Gumbs Vines, Doreen	Threadgill, Marcus	
Schlosser, Ariel	Haupt, Calvin		
Wunschel, Scott			
		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Vargas, Brian		
	Vargas, Gustavo	<b>CENAB</b>	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive Area 1/B, 41 drums filled. AUES (approximately 7 pieces) found near chimney. 2 lagging boards that were rotted were replaced on retaining wall of 4801 Glenbrook.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information  
 \_\_\_\_\_  
 \_\_\_\_\_

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	





Pg

25 4-11-19

0630 SAFETY BRIEF

0710 RADIO CHECKS

0745 MINICAMS UP

0750 DRAINS PUMPS UP &amp; RUNDOWN

0807 Team Two Down Range.

0814 VOC Sample Collected.

0934 Team Found Softball size Piece of CACM

1115 TM 2 Clear of PDS.

1120 TM 3 loading drums for transport

1135 Begin mid-day Challenge.

1212 Drums 3128-3151 Transported to Fod.

1355 MID DAY COMPLETE

1315 TEAM 1 DOWN RANGE, LEVER'S OPEN

SCHLOSSER, WEIGHT

1330 PPE CHECKS

1404 PPE CHECKS

1432 PPE CHECKS


1501 PPE CHECKS

1517 SOIL DRUMS 3152-3168 FILLED

1522 COMPOSITE COLLECTED

1530 TEAM 1 CLEARED PDS

1700 SECURED



## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 12 April 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 53/77

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert		Bartosh, Ian	
Castell, Lorna	Prate, Warren	Burrell, Dianne	
Courtney, Kenneth	Wright, David	Duff, Todd	
Holloway, April	Yorkshire, Bart	Harris, Brian	
Luckanavage, Kyle		King, Bernard	
Marian, Jedidiah		Wainwright, LeRoy	
Matter, Phillip		Jones, LaMarcus	
Nelms, Bobby		Privett, Arlita	
Oien, Joshua	LIFE STAR	Skipper, Brandon	
Rider, Matthew	Gumbs Vines, Doreen	Smith, Ethan	
Schlosser, Ariel	Jackson, Mark		
Wunschel, Scott			
		CEHNC	
		Boles, Judson	
	ACCUPERMIT		
	Vargas, Brian		
	Vargas, Gustavo	CENAB	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations in Area 1/B, 8 drums filled. Grab sample collected in grid 10-90 because we were approximately 3 feet below house foundation and large amounts of rain due in this afternoon and weekend. At 1150 temperatures went above 75 degrees and intrusive operations were stopped.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



Pg

24 4-12-19

0630 SAFETY BRIEF

0700 RADIO CHECKS

0751 SOIL DRUMS 3152-3166 LOADED FOR FED.

0744 MINICAMS UP.

0750 DAMS PUMPS RUNNING.

0831 SOIL DRUMS 3167/3168 PPE 463 LOADED FOR FED

0853 TEAM 2 DOWN RANGE, RIDER, CASTLE, GRAVE  
LOUOL "D", FED

0913 VOC COLLECTED.

0917 PPE CHECKS

0944 PPE CHECKS.

1010 SOIL DRUMS 3169-3176 FILLED.

1034 COMPOSITE COLLECTED

1057 GRAB SAMPLE 18 COLLECTED

1103 TEAM 2 CITED PAS.

1135 STARTING MIDDAY CHALLENGE.


1144 MIDDAY COMPLETE.

1205 INTRUSIVE OBS SUSPENDED DUE TO TEMPS.

1301 SOIL DRUMS 3169-3176 LOADED FOR

FED PROPERTY.

1710 SECURED









P<sub>9</sub>

27 4-15-19

0630 SAFETY BRIEF

0700 RADIO CHECKS. PUMPING WATER AREA A

0744 MINICAMS UP

0845 DAMS PUMPS RUNNING.

0915 TM 1 to the PDS.

0918 TEAM 1 DOWN RANGE B RIVER  
COURNOY PRATE.

0926 VOC COLLECTED.

0933 PPE CHECKS

0956 PPE CHECKS

1021 PPE CHECKS

1055 PPE CHECKS.

1124 SOIL DRUMS 3177-3194 FILLED.

1135 TEAM 1 CLEARED PDS

1144 STATISTICAL MIDDAY CHALLENGE

SOIL DRUMS 3177-3194 LOADED AND FED.

1154 MIDDAY COMPLETE

1324 SOIL DRUMS 3192-3194 LOADED FOR FED

~~1334~~ 1334 TEAM 2 DOWN RANGE B RIVER  
BLONIS PRATE

1357 PPE CHECKS

1418 PPE CHECKS

1449 PPE CHECKS

1525 SOIL DRUMS 3195-3212 FILLED.

# SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 16 April 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 44/68 partly cloudy

## **Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Breyman, Mark	Bartosh, Ian	
Castell, Lorna	Prate, Warren	Duff, Todd	
Courtney, Kenneth		Harris, Brian	
Holloway, April	Yorkshire, Bart	Jones, LaMarcus	
Luckanavage, Kyle		King, Bernard	
Marian, Jediaiah		Landers, Brian	
Matter, Phillip		Nguyen, Phuong	
Nelms, Bobby		Privett, Arlita	
Oien, Joshua	<b>LIFE STAR</b>	Skipper, Brandon	
Rider, Matthew	Alfaro, Walter	Smith, Ethan	
Schlosser, Ariel	Jackson, Mark	Wooten, Mike	
Wunschel, Scott			
		<b>CEHNC</b>	
		Boles, Judson	
	<b>ACCUPERMIT</b>		
	Overton, Robert		
	Williams, Angelo	<b>CENAB</b>	
		Whitten, Ricky	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations in Area B, 33 drums filled. Set up sump pump near underground springs on eastern edge of Area 1.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



P  
19

29 4-16-19

0630 SAFETY BRIEF.

0700 RADIO CHECKS

0744 MINICAMS UP.

0750 SOIL DRUMS 3195-3209 TRANSPORTED  
TO FED PROPERTY.

0800 DAMS UP.

0834 SOIL DRUMS 3210-3212, SCR 595 TRANSPORTED  
TO FED.0855 TEAM 2 DOWN RANGE "B" RIDER  
CASTELL PRATE.

0904 VOC COLLECTED.

0920 PPE CHECKS.

0944 PPE CHECKS.

1006 PPE CHECKS.

1039 PPE CHECKS.

1109 SOIL DRUMS 3213-3224 FILLED.

1116 TEAM 2 CLEARED POS.

1130 STARTING MIDDAY CHALLENGE.

1144 MIDDAY COMPLETE.

1304 TEAM 1 DOWN RANGE "B" OBT. COURTESY  
PROFMAN.

1328 PPE CHECKS.

1349 PPE CHECKS.

1419 PPE CHECKS.







B

31 4/17-19

0630 SAFETY BRIEF

0700 RADIO CHECKS

0730 SOIL DRUMS 3245-3245, AQ 669, PPE 464  
TRANSPORTED TO F

0743 MUNI CAMS UP.

0750 DAAMS UP.

0824 TEAM 2 "B" RIDER, BLONDS, APOY in air.

0834 VOC COLLECTED

0844 PPE CHECKS.

0911 PPE CHECKS.

0933 PPE CHECKS.

1013 PPE CHECKS.

1058 PPE CHECKS

1115 SOIL DRUMS 3246-3278 FULLED.

1123 TEAM CLEARED PDS

1124 MIDDAY CHALLENGE.

1148 SOIL DRUMS 3246-3261 TRANSPORTED TO FEO.

1143 MIDDAY COMPLETE

1300 TEAM 1 DOWN RANGE B" OVER, CUMULATIVE, UNPILLOTED.

1328 PPE CHECKS.

1354 PPE CHECKS

1410 SOIL DRUMS 3279-3291

1414 COMPOSITE COLLECTED.

1427 TEAM 1 CLEARED PDS.





P  
19

33 4-18-19

0630 SAFETY BRIEF

0700 RADIO CHECKS.

0743 MINICAMS UP

0745 PAAWS RUNNING.

0815 TEAM 2 DOWN RANGE "B" RIDER, CASTELL, WRIGHT.

0824 VOC COLLECTED

0832 PPE CHECKS.

0848 PPE CHECKS.

0903 PPE CHECKS.

0918 PPE CHECKS.

0937 PPE CHECKS

1010 BALTIMORE COG GEOLOGIST W/ SEAN

RUCKLEY PARSONS PM. CONFIRM THAT  
COMPTON SAR ROUTE IN GRIDS 10-90/10-70.

1033 SOIL DRUMS 3292-3318 FILLED.

1037 TEAM 2 CLEARED PDS.

1134 STARTING MID DAY CHALLENGE.

1136 SOIL DRUMS 3291-3305 TRANSPORTED  
TO FED. PROPERTY.

1143 MID DAY COMPLETE.

1233 TEAM 1 DOWN RANGE "B" OLEN COVERNOY. BRG m m.

1257 PPE CHECKS

1318 COMPOSITE COLLECTED, SOIL DRUMS 3314-3326 FILLED

1323 TEAM 1 CLEARED PDS

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 19 April 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 66/77 Partly cloudy then heavy rains after noon.

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Breyman, Mark	Bartosh, Ian	
Castell, Lorna	Prate, Warren	Duff, Todd	
Courtney, Kenneth	Wright, David	Harris, Brian	
Holloway, April	Yorkshire, Bart	Jones, LaMarcus	
Luckanavage, Kyle		King, Bernard	
Marian, Jedidiah		Nguyen, Phuong	
Matter, Phillip		Privett, Arlita	
Nelms, Bobby		Skipper, Brandon	
Oien, Joshua	<b>LIFE STAR</b>	Smith, Ethan	
Rider, Matthew	Brooke, Bailey	Wooten, Mike	
Schlosser, Ariel	Jackson, Mark		
Wunschel, Scott			
		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Williams, Angelo		
	Vargas, Gustavo	<b>CENAB</b>	
		Whitten, Ricky	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations in Area B, nearest Glenbrook Road, 22 drums filled. Weighed 83 drums for upcoming HAZMAT shipment. Heavy rains and thunderstorms rolled in around 12:30.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

**Problems encountered/resolutions:**

Lightning hold at 8:37, rain began at noon.

**Instructions given by government personnel:****Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	





P<sub>4</sub>

35 4-19-19

0630 SAFETY BRIEF

0700 RADIO CHECKS.

0742 MUNICAMS UP

0753 DAAMS RUNNING

0814 TEAM 2 DOWN RANGE B° RIDER, RIVINS PROGRAM.

0819 VOC COLLECTED.

0832 PPE CHECKS.

0851 LIGHTNING HOLD.

0841 COMPOSITE COLLECTED. CLEARED PDS

0907 OFF LIGHTNING HOLD.

0934 TEAM 2 DOWN RANGE B° RIDER, RIVINS PROGRAM.

1000 PPE CHECKS.

1022 PPE CHECKS.

1045 SOIL DRUMS 3327-3348 FILLED


1049 COMPOSITE COLLECTED. INTRUSIVE  
OPS SUSPENDED DUE TO TEMPERATURE.

1056 TEAM 2 CLEARED PDS.

1117 SOIL DRUMS 3327-3341 TRANSPORTED TO FED.

SOIL DRUMS 3342-3348 TRANSPORTED TO FED.

1200 SECURED



## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 22 April 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 55/71 mostly sunny

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Breyman, Mark	Babcock, Kendall	
Castell, Lorna	Prate, Warren	Bartosh, Ian	
Courtney, Kenneth	Wright, David	Duff, Todd	
Holloway, April	Yorkshire, Bart	Harris, Brian	
Luckanavage, Kyle		Jones, LaMarcus	
Marian, Jedidiah		King, Bernard	
Matter, Phillip		Privett, Arlita	
Nelms, Bobby		Skipper, Brandon	
Oien, Joshua	<b>LIFE STAR</b>	Smith, Ethan	
Rider, Matthew	Alfaro, Walter	Wooten, Mike	
Schlosser, Ariel	Robinson, Omar		
Wunschel, Scott			
		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Overton, Robert		
	Williams, Angelo	<b>CENAB</b>	
		Whitten, Ricky	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations in Area B parallel with Glenbrook, 47 drums filled. HAZMAT shipment 226 drums shipped and approximately 20,000 gallons of water removed to treatment/disposal facility. At 14:17 temperatures went above 75 degrees and intrusive operations were halted for the day. Pumped 725 gallons of water out of excavation area.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

**Problems encountered/resolutions:**

**Instructions given by government personnel:**

**Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



R

36 422-19

0630 SAFETY BRIEF

0700 RADIO CHECKS.

0744 MIVICAMS UP

0750 DRAWS PUMPS RUNNING.

0818 TEAM 2 DOWN RANK 8- RIDGE, CHILL, WEIGHT.

0844 VOC COLLECTED, PPE CHECKS

0856 PPE CHECK

0917 PPE CHECKS.

0935 PPE CHECKS

0948 PPE CHECKS

1006 PPE CHECKS

1020 SOIL DRUMS 3349-3378

1027 TEAM 2 CLEARED PDS.

1124 SOIL DRUMS 3349-3343, PPE 465.

LOADED FOR FED.

1205 SOIL DRUMS 3364-3378 TRANSPORTED TO FED

1301 TEAM 1 DOWN RANK 8- OVEN, CHILLING, PPE 465

1321 PPE CHECKS

1341 PPE CHECKS.

1401 PPE CHECKS.

1417 SOIL DRUMS 3379-3395 FILLED

1424 COMPOSITE COLLECTED, SUSPENDED

INTENSIVE OPS DUE TO TEMPERATURE

1434 TEAM 1 CLEARED PDS.

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 23 April 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 52/ 84 clear, hot

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Breyman, Mark	Babcock, Kendall	
Castell, Lorna	Prate, Warren	Bartosh, Ian	
Courtney, Kenneth	Wright, David	Duff, Todd	
Holloway, April	Yorkshire, Bart	Harris, Brian	
Luckanavage, Kyle		Jenkins, Troy	
Marian, Jedidiah		Jones, LaMarcus	
Matter, Phillip		King, Bernard	
Nelms, Bobby		Landers, Brian	
Oien, Joshua	LIFE STAR	Privett, Arlita	
Rider, Matthew	Alfaro, Walter	Skipper, Brandon	
Schlosser, Ariel	Jackson, Mark	Wooten, Mike	
Wunschel, Scott			
		CEHNC	
		Boles, Judson	
	ACCUPERMIT		
	Overton, Robert		
	Williams, Angelo	CENAB	
		Whitten, Ricky	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations in Area B, 4 drums filled before heat exceeded 75. Pumped 375 gallons. Tested 1701 miniCAM column in Area 4. Sampled water in one Baker tank. 416 soil drums arrived.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	





P<sub>9</sub>

38

4-23-19

0630 SAFETY BRIEF

0705 RADIO CHECKS

0743 MINICAMS UP DAMS ZUNDENL

0835 SOIL DRUMS 3379-3393 TRANSPORTED TO FED.

0915 TEAM 2 DOWN RANGE B<sup>+</sup> RIDGE, BEOVINS, BPOYMAN.

0930 DAMS PUMPS AREA "4" RUNNING

0934 SOIL DRUMS 3396-3399 FILLED.

INTRUSIVE GPSS SUSPENDED DUE  
TO TEMPERATURE.

0935 COMPOSITE COLLECTED. VOC @ 09:20

0945 TEAM 2 CLEARED PDS.

1014 TEAM 2 DOWN RANGE B<sup>+</sup> RIDGE, BEOVINS  
PLACING MONITORS IN AREA "4".

1024 TEAM 2 CLEARED PDS.

1307 SOIL DRUMS 3394-3399, SER 596 TRANSPORTED  
TO FED.1423 TEAM 1 DOWN RANGE B<sup>+</sup> OBTN SCHLOSSER  
RECOVERING MONITORS FROM AREA "4"

1430 CLEARED PDS.

1700 SECURED

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 24 April 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 60/74 winds 5-15 mph

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Breyman, Mark	Babcock, Kendall	
Castell, Lorna	Prate, Warren	Bartosh, Ian	
Courtney, Kenneth	Wright, David	Duff, Todd	
Holloway, April	Yorkshire, Bart	Harris, Brian	
Luckanavage, Kyle		Jones, LaMarcus	
Marian, Jedidiah		King, Bernard	
Matter, Phillip		Landers, Brian	
Nelms, Bobby		Privett, Arlita	
Oien, Joshua	<b>LIFE STAR</b>	Skipper, Brandon	
Rider, Matthew	Alfaro, Walter	Wooten, Mike	
Schlosser, Ariel	Gumbs Vines, Doreen		
Wunschel, Scott			
		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Overton, Robert		
	Williams, Angelo	<b>CENAB</b>	
		Whitten, Ricky	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations in Area B, 34 drums filled before temps exceeded 75. Pumped 500 gallons of water, begin cleaning out 1 Baker tank for turn in.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



Pg

39

4-24-19

0630 SAFETY BRIEF

0700 RADII CHECKS

0743 MINICAMS UP

0757 PUMPING WATER 500 GAL AREA B

0809 TEAM 2 DOWN RANGE &amp; RIDGE, CASTLE, W/14 HT.

0812 VOC COLLECTED

0821 PPE CHECKS

0845 PPE CHECKS

0903 PPE CHECKS.

0921 PPE CHECKS.

0938 PPE CHECKS.

1000 SOIL DRUMS 3400-3433 FILLED.

1006 TEAM 2 CLEARED PDS.

1043 SOIL DRUMS 3400-3414 TRANSPORTED TO FED.

1128 SOIL DRUMS 3415-3429 TRANSPORTED TO FED.

1130 STARTING MIDDAY.

1143 MIDDAY COMPLETE.

1236 TEAM 1 DOWN RANGE B° OVER CHIMNEY

1240 COMPOSITE COLLECTED.

1245 TEAM CLEARED PDS. SUSPENDED INTRUSIVE OPS.

DUE TO TEMPERATURE.

1302 SOIL DRUMS 3430-3433, PPE 466

TRANSPORTED TO FED PROPERTY.

1700 SECURED

/ [Signature]

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 25 April 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 58/71 cloudy, some showers

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Breyman, Mark	Babcock, Kendall	
Castell, Lorna	Prate, Warren	Bartosh, Ian	
Courtney, Kenneth	Wright, David	Duff, Todd	
Holloway, April	Yorkshire, Bart	Harris, Brian	
Luckanavage, Kyle		Jones, LaMarcus	
Marian, Jedidiah		King, Bernard	
Matter, Phillip		Landers, Brian	
Nelms, Bobby		Privett, Arlita	
Oien, Joshua	<b>LIFE STAR</b>	Skipper, Brandon	
Rider, Matthew	Gumbs Vines, Doreen	Wooten, Mike	
Schlosser, Ariel	Haupt, Calvin		
Wunschel, Scott			
		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Overton, Robert		
	Williams, Angelo	<b>CENAB</b>	
		Whitten, Ricky	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations in Area B, turned corner from parallel with Glenbrook to digging parallel with 4835 foundation. Ernst electrical subcontractors performed megger test on lightning protection system in the IHF. At 13:52 the temps exceeded 75 and intrusive ops were halted. 48 drums filled.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	





Pg

40

4-25-19

0630 SAFETY BRIEF

0700 RADIO CHECKS

0743 MINICAMS UP/DAMS PUMPS RUNNING

0810 TEAM 2 DOWN RANKE &amp; B. RIDER CASTLE BRIDGE

0818 VOC COLLECTED

0829 PPE CHECKS

0849 PPE CHECKS

0911 PPE CHECKS

0930 PPE CHECKS

0950 PPE CHECKS

1010 SOIL DRUMS 3434-3467 FILLED.

1015 TEAM 2 CLEARED PDS.

1048 SOIL DRUMS 3434-3448 TRANSPORTED TO FED.

1117 SOIL DRUMS 3449-3463 TRANSPORTED TO FED.

1130 STATICAL MID DAY CONFERENCE CALL  
@ 11:00.

1143 MIDDAY COMPLETE.

1252 TEAM 1 DOWN RANKE &amp; B. RIDER CASTLE BRIDGE

1314 PPE CHECKS

1335 PPE CHECKS

1347 SOIL DRUMS 3468-3481 FILLED.

1355 COMPOSITE COLLECTED.

1400 TEAM 1 CLEARED PDS.

1432 SOIL DRUMS 3464-3478 TRANSPORTED TO FED.

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 26 April 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 62/72 showers

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Breyman, Mark	Babcock, Kendall	
Castell, Lorna	Prate, Warren	Bartosh, Ian	
Courtney, Kenneth	Wright, David	Duff, Todd	
Holloway, April	Yorkshire, Bart	Harris, Brian	
Luckanavage, Kyle		Jones, LaMarcus	
		King, Bernard	
Matter, Phillip		Privett, Arlita	
Nelms, Bobby		Skipper, Brandon	
Oien, Joshua	<b>LIFE STAR</b>	Landers, Brian	
Rider, Matthew	Brooke, Bailey	Wooten, Mike	
Schlosser, Ariel	Jackson, Mark		
Wunschel, Scott			
		<b>CEHNC</b>	
		Boles, Judson	
	<b>ACCUPERMIT</b>		
	Overton, Robert		
	Williams, Angelo	<b>CENAB</b>	
		Whitten, Ricky	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations in Area B, along the exit of PDS, 30 drums filled. Cut up 60 old unserviceable plastic drums at Fed Prop.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information  
 \_\_\_\_\_  
 \_\_\_\_\_

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
_____	Berkel ( )
_____	DAVEY ( )
_____	ACCUPERMIT ( )
_____	ACI (0)
_____	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



P  
19

42 4-26-19

0630 SAFETY BRIEF

0700 RADIO CHECKS.

0730 DAMMS PUMPS RUNNING

0742 MINICAMS UP.

0813 TEAM 2 DR B RIDER, BLEVINS, WRIGHT.

0820 VOC COLLECTED.

0836 PPE CHECKS.

0845 PPE CHECKS.

0903 PPE CHECKS.

0918 PPE CHECKS.

0948 PPE CHECKS.

1008 SOIL DRUMS 3482-3511 FILLED

1013 COMPOSITE COLLECTED.

1020 TEAM 2 CLEARED PDS.


1050 SOIL DRUMS - 3479-3493 TRANSPORTED TO FED

1139 SOIL DRUMS 3494-3508 TRANSPORTED TO FED.

1228 SOIL DRUMS 3509-3511 TRANSPORTED TO FED.

1317 TEAMS WORKING AT FED PROPERTY.

1702 SECURITY

A large, stylized handwritten signature or set of initials, possibly 'P' and 'H', written in dark ink. It is written over the bottom portion of the page, partially obscuring some of the text.

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 29 April 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 45/62 winds 5-10 mph

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Breyman, Mark	Askew, Thomas	
Castell, Lorna	Prate, Warren	Babcock, Kendall	
Courtney, Kenneth	Wright, David	Caldwell, Jeff	
Holloway, April	Yorkshire, Bart	Crawford, Stephen	
Luckanavage, Kyle		Duff, Todd	
Marien, Jedidiah		Harris, Brian	
Matter, Phillip		Landers, Brian	
Nelms, Bobby		Miller, Donald	
Oien, Joshua	LIFE STAR	Skipper, Brandon	
Rider, Matthew	Gumbs Vines, Doreen	Threadgill, Marcus	
Schlosser, Ariel	Robinson, Omar	Wagner, Darien	
Wunschel, Scott		Wainwright, LeRoy	
		CEHNC	
		Boles, Judson	
	ACCUPERMIT		
	Overton, Robert		
	Williams, Angelo	CENAB	
		Whitten, Ricky	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Collected 8 confirmation samples in Area 4. Intrusive operations in Area B, 22 drums filled. 416 soil drums arrived on site.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	





P  
16

43 4-29-19

0630 SAFETY BRIEF

0709 RADIO CHECK

0742 MINICAMS UP

0757 DARRIN'S RUNNING.

0834 TEAM DOWN RANGE 'B' RIDER, UEN, CUNNINGHAM.  
SAMPLING AREA '4'

0947 ALL SAMPLES COLLECTED TEAM CLEARED POS.

1043 TEAM 2 DOWN RANGE 'B' RIDER, CASTELL, BRAYMAN.  
WORKING AREA 'B'

1052 VOC COLLECTED.

1105 PPE CHECKS.

1144 SOIL DRUMS 3512-3522 FILLED.

1148 TEAM 2 CLEARED POS.

1150 STARTING MIDDAY CHALLENGE

1202 MIDDAY COMPLETE.

1235 TEAM 1 DOWN RANGE AREA '4' LOVER 'B'  
UEN, CUNNINGHAM.

1342 PPE CHECKS

1406 PPE CHECKS.

1423 SOIL DRUMS 3523-3533 FILLED.

1430 COMPOSITE COLLECTED

1435 TEAM 1 CLEARED POS.

15 SOIL DRUMS 3512-3524 TRANSPORTED TO FED.  
PROPERTY.

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 30 April 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 60/83 hot, mostly sunny

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Breyman, Mark	Askew, Thomas	
Castell, Lorna	Prate, Warren	Babcock, Kendall	
Courtney, Kenneth	Wright, David	Caldwell, Jeff	
Holloway, April	Yorkshire, Bart	Crawford, Stephen	
Luckanavage, Kyle		Duff, Todd	
Marien, Jedidiah		Harris, Brian	
Matter, Phillip		Landers, Brian	
Nelms, Bobby		Miller, Donald	
Oien, Joshua	LIFE STAR	Threadgill, Marcus	
Rider, Matthew	Alfaro, Walter	Wagner, Darien	
Schlosser, Ariel	Brooke, Bailey	Wainwright, LeRoy	
Wunschel, Scott			
		CEHNC	
		Boles, Judson	
	ACCUPERMIT		
	Overton, Robert		
	Williams, Angelo	CENAB	
		Whitten, Ricky	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations in Area B, 29 drums filled, at 10:41 temperatures exceeded 75 degrees and intrusive operations were halted. Repaired chainlink fence on 4825/4835 property line as it was damaged during high winds over the weekend. Cut up old unserviceable drums at Fed Prop.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

**Problems encountered/resolutions:**

**Instructions given by government personnel:**

Informed Ricky Whitten (Baltimore COE) of loud noise at 4835, possibly an attic fan malfunction.

**Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



Pg

45 4-30-19

0630 SAFETY BRIEF

0645 Ky 16 LUCKAWANLE REPORTS A  
SPRAIN/PAIN IN HIS RIGHT ~~ARM~~  
LATISSIMUS DORSI MUSCLE.

WORK CARD IS BEING NOTIFIED.

THE UPPER MANAGEMENT WILL BE  
INFORMED. NO MEDICAL TREATMENT  
WAS REQUIRED.

0709 RADIO CHECKS.

0742 MINICAMS/DAMS UP.

0815 TEAM 2 DOWN RANGE "B" RIDER ELEVINS, WRIGHT.

0826 VOC COLLECTED.

0836 PPE CHECKS.

0853 PPE CHECKS

0908 PPE CHECKS

0924 PPE CHECKS

0942 PPE CHECKS.

0958 PPE CHECKS.

1017 PPE CHECKS.

1035 COMPOSITE COLLECTED SOIL DRUMS 3534-5562  
FILLED

1040 TEAM 2 CLEARED PDS.

1047 INTENSIVE OPS SUSPENDED DUE TO TEMPERATURE.  
79.9°F

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 1 May 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 60/73 overcast and cooler

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Breyman, Mark	Askew, Thomas	
Castell, Lorna	Prate, Warren	Babcock, Kendall	
	Wright, David	Caldwell, Jeff	
Holloway, April	Yorkshire, Bart	Crawford, Stephen	
Luckanavage, Kyle		Duff, Todd	
Marien, Jedidiah		Harris, Brian	
Matter, Phillip		Landers, Brian	
Nelms, Bobby		Miller, Donald	
Oien, Joshua	LIFE STAR	Threadgill, Marcus	
Rider, Matthew	Alfaro, Walter	Wagner, Darien	
Schlosser, Ariel	Gumbs, Doreen	Wainwright, LeRoy	
Wunschel, Scott			
		CEHNC	
	ACCUPERMIT	Boles, Judson	
	Overton, Robert		
	Williams, Angelo	CENAB	
		Whitten, Ricky	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations in Area B, 63 drums filled, no heat stoppage today. Densel at Fed Prop repairing/servicing AC units.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

**Problems encountered/resolutions:**

AC unit at Federal Property was reported to not be cooling in the office area, Densel called.

**Instructions given by government personnel:****Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	





1 PL

47 5-1-19

0630 SAFETY BRIEF

0700 RADIO CHECKS.

0748 MINICAMS UP.

0745 DAAMS RUNNING.

0815 TEAM 2 DOWN RANGE B\* RIDER, CASTLE, FREYMAN.

0825 VOL COLLECTED

0840 PPE CHECKS.

0855 PPE CHECKS.

0913 PPE CHECKS

0947 PPE CHECKS

1008 PPE CHECKS

1043 SOIL DRUMS 3563-3597 FILLED.

1055 TEAM 2 CLEARED POS. STARTING MIDDAY

1125 SOIL DRUMS 3563-3577 TRANSPORTED TO RED PROP.

1200 SOIL DRUMS 3578-3592 TRANSPORTED TO RED PROP.

1150 DAY COMPLETE.

1230 TEAM 1 DOWN RANGE B OIEN, <sup>MARIAN</sup> ~~BEYMAN~~ WRIGHT.

1245 PPE CHECKS.

1300 PPE CHECKS

1315 PPE CHECKS

1330 PPE CHECKS

1345 PPE CHECKS

1400 PPE CHECKS

1415 PPE CHECKS

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 2 May 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 68/88 sunny, hot

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Breyman, Mark	Askew, Thomas	
Castell, Lorna	Prate, Warren	Babcock, Kendall	
Courtney, Kenneth	Wright, David	Caldwell, Jeff	
Holloway, April	Yorkshire, Bart	Crawford, Stephen	
Luckanavage, Kyle		Duff, Todd	
Marien, Jedidiah		Harris, Brian	
Matter, Phillip		Landers, Brian	
Nelms, Bobby		Miller, Donald	
Oien, Joshua	<b>LIFE STAR</b>	Threadgill, Marcus	
	Gumbs Vines, Doreen	Wagner, Darien	
Schlosser, Ariel	Haupt, Calvin	Wainwright, LeRoy	
		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Vargas, Brandon		
	Williams, Angelo	<b>CENAB</b>	
		Whitten, Ricky	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations in Area B, 16 drums filled before temperature rose above 75 degrees at 0936 AM.  
 Densel repairing/servicing AC units at Fed Prop. Pumped 425 gallons of water.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



P<sub>2</sub>

49 5-2-19

0630 SAFETY BRIEF

0700 RADIO CHECKS.

0748 MINICAMS/DAMS UP

0800 TEAM 1 DOWN RANGE B DIEN, CHERNOBYL, WRIGHT

0808 VOC COLLECTED.

0825 PPE CHECKS.

0840 PPE CHECKS. 3623-3631 FILLED.

0900 PPE CHECKS. STOPPED PPE TO TEMP.

0918 PPE CHECKS. COLLECTED.

0934 PPE CHECKS. TO PDS

0938 SOIL DRUMS 3626-3642 FILLED. INTENSIVE  
OPS SUSPENDED DUE TO TEMP.

0949 COMPOSITE COLLECTED.

0952 TEAM 1 CLEARED PDS.


1038 SOIL DRUMS 3623-3637 TRANSPORTED TO FED

1120 SOIL DRUMS 3638-3642, PPE DRUM 468

TRANSPORTED TO FED PROPERTY.

CONFERENCE CALL @ 11:00.

1700 SECURED



## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 3 May 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 67/82 overcast

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Breyman, Mark	Askew, Thomas	
Castell, Lorna	Prate, Warren	Babcock, Kendall	
Courtney, Kenneth	Wright, David	Caldwell, Jeff	
Holloway, April	Yorkshire, Bart	Crawford, Stephen	
Luckanavage, Kyle		Duff, Todd	
Marien, Jedidiah		Harris, Brian	
Matter, Phillip		Landers, Brian	
Nelms, Bobby		Miller, Donald	
Oien, Joshua	<b>LIFE STAR</b>	Threadgill, Marcus	
	Brooke, Bailey	Wagner, Darien	
Schlosser, Ariel	Jackson, Mark		
Wunschel, Scott		Wainwright, LeRoy	
		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Overton, Robert		
	Williams, Angelo	<b>CENAB</b>	
		Whitten, Ricky	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations in Area B, 9 drums filled before temperatures exceeded 75 degrees at 0945 AM.  
 Pumped 1770 gallons of water.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information  
 \_\_\_\_\_  
 \_\_\_\_\_

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
_____	Berkel ( )
_____	DAVEY ( )
_____	ACCUPERMIT ( )
_____	ACI (0)
_____	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	





Pg

50 5-3-19

0630 SAFETY, NOLET

0700 RADIO CHECKS

0738 MINICAMS/DNAMS UP

0850 TEAM 1 DOWN RANCE'S, OWN COUNTRY, ARROYO &amp; AL.

0900 VOC COLLECTED

0911 PPE CHECKS

0937 SOIL DRUMS 3643-3651 FILLED.

0942 INTRUSIVE SUSPENDED DUE TO TEMP.

0943 COMPOSITE COLLECTED.

0940 TEAM 1 CLEARED PDS.

1100 SOIL DRUMS 3643-3651 TRANSPORTED

1010 TO FEB.

1700 SECURED





Pa

51 5-6-19

0630 SAFETY BRIEF

0736 MINIDRUMS / DRUMS UP.

0705 TEAM 1 DOWN RANGE, DOWN, CONTINUING, WEIGHT

0801 VOC COLLECTED

0823 PPE CHECKS.

0838 PPE CHECKS.

0855 PPE CHECKS.

0921 PPE CHECKS.

0942 PPE CHECKS.

1007 PPE CHECKS.

1012 SOIL DRUMS 3652-3678 FILLED.

1018 TEAM 1 CLEARED POS.

1113 SOIL DRUMS 3664-3678 TRANSPORTED

1136 STARTING MIDDAY CHALLENGE.

1159 MIDDAY COMPLETE.

1204 SOIL DRUMS 3652-3663, 3664-3678  
TRANSPORTED.


1224 TEAM 3 DOWN RANGE &amp; DOWNHILL, SCHLOSSER

1228 COMPOSITE COLLECTED.

1233 TEAM 3 CLEARED POS.

1310 PUMPING WATER

1700 SECURED







[illegible]



R

52 5-7-19

0630 SAFETY BRIEF

0722 MINI DAMS / DAMS UP

0805 TEAM 2 IN 'B' RIDER, GIOVINI, BROYMAN.

0813 VDC COLLECTED. 2 PPE CHECKS.

0832 PPE CHECKS.

0847 PPE CHECKS.

0858 SOIL DAMS 3679-3689 FILLED. TEMP 75.2°F

0902 COMPOSITE COLLECTED

0907 TEAM 2 CLEARED PDS.

1700 SECURED

R  
X





24

53 5-8-19

0630 SAFETY BRIEF

0700 RADIO CHECKS

0752 MINICAMS UP

0815 TEAM 2 DOWN RANGE "B" RIBON, CASTELL, WRIGHT.

0853 VOC COLLECTED.

0855 PPE CHECKS.

0915 PPE CHECKS

0932 PPE CHECKS

0951 SOIL DRUMS - 3690 - 3719

0955 TEAM 2 CLEARED PDS.

1030 SOIL DRUMS 3690 - 3704 TRANSPORTED TO FED

1110 SOIL DRUMS 3705 - 3709 TRANSPORTED TO FED.

1114 STARTING MIDDAY CHALLENGE.

1140 MIDDAY COMPLETE

1220 TEAM 1 DOWN RANGE "B" OVER, COUNTRY, PROGRAM.

1230 PPE CHECKS

1250 PPE CHECKS.

1300 PPE CHECKS

1327 PPE CHECKS

1409 SOIL DRUMS 3710 - 3734 FILLED.

1413 COMPOSITE SAMPLE COLLECTED

1420 TEAM 1 CLEARED PDS.

1447 SOIL DRUMS 3710 - 3724 TRANSPORTED  
TO FED. PROP.







R

55 5-9-19

0630 SAFETY BRIEF

0742 MINICAMS / DAAMS VP

0820 TEAM 2 DOWN RANGE "B" RIDER, BLEVINS, BRYAN

0826 VOC COLLECTED.

0842 PPE CHECKS.

0905 PPE CHECKS.

0927 SOIL DRUMS 3735-3751 FILLED

0938 COMPOSITE COLLECTED.

0946 TEAM 2 CLEARED POS.

1017 SOIL DRUMS 3735-3749 TRANSPORTED TO FED.

1034 SOIL DRUMS 3750-3751 TRANSPORTED TO FED.

1100 CONFERENCE CALL

1130 MIDDAY CHALLENGE


1142 MIDDAY COMPLETE.

1205 TEAM 1 DOWN RANGE LEVEL "B" IN AREA "B"  
CONFIRMATION SAMPLES. DIET, CHAMPNEY.

1255 SAMPLING IN AREA "B" COMPLETE

1302 TEAM 1 CLEARED POS

1700 SECURED





R


56 5-10-19

0630 SAFETY BRIEF

0700 RADIO CHECKS.

0800 CUTTING THE APRON W/ TRACK SAW

1700 DAY COMPLETE

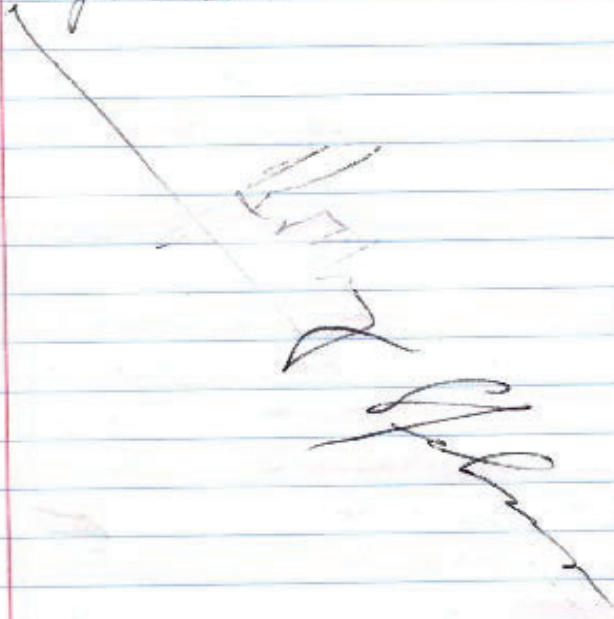

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 13 May 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 mid 50's, rain

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Prate, Warren	Askew, Thomas	
	Wright, David	King, Bernie	
Courtney, Kenneth	Yorkshire, Bart	Caldwell, Jeff	
Holloway, April		Crawford, Stephen	
Marien, Jedidiah		Druyor, Chris	
Matter, Phillip		Harris, Brian	
Nelms, Bobby		McClellan, Dale	
Oien, Joshua		Threadgill, Marcus	
Rider, Matthew	<b>LIFE STAR</b>	Wagner, Darien	
Schlosser, Ariel	Alfaro, Walter	Wainwright, LeRoy	
Wunschel, Scott	Gumbs Vines, Doreen	Nichols, Doug	
		<b>CEHNC</b>	
		Boles, Judson	
	<b>ACCUPERMIT</b>		
	Arteaga, Carlos		
	Williams, Angelo	<b>CENAB</b>	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive operations. Heavy rains on and off all day. Pumped 4150 gallons of water.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information  
 \_\_\_\_\_  
 \_\_\_\_\_

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
_____	Berkel ( )
_____	DAVEY ( )
_____	ACCUPERMIT ( )
_____	ACI (0)
_____	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

57 5-13-14

0630 SAFETY BRIEF

0700 RADIO CHECKS

0800 PUMPING WATER

1700 Day COMPLETE

*[Signature]*



## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 14 May 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 lo 50's, overcast

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Prate, Warren	Askew, Thomas	
Castell, Lorna	Wright, David	King, Bernie	
Courtney, Kenneth	Yorkshire, Bart	Caldwell, Jeff	
Holloway, April		Crawford, Stephen	
Marien, Jedidiah		Druyor, Chris	
Matter, Phillip		Harris, Brian	
Nelms, Bobby		McClellan, Dale	
Oien, Joshua		Threadgill, Marcus	
Rider, Matthew	<b>LIFE STAR</b>	Wagner, Darien	
Schlosser, Ariel	Jackson, Mark	Nichols, Doug	
Wunschel, Scott	Gumbs Vines, Doreen		
		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Arteaga, Carlos		
	Williams, Angelo	<b>CENAB</b>	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations on the Skirt in Area B, 18 drums filled. Baltimore geologist confirms saprolite in 30-70. Water samples of 2 Baker tanks. Approximately 2/3 of skirt removed today.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information  
 \_\_\_\_\_  
 \_\_\_\_\_

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
_____	Berkel ( )
_____	DAVEY ( )
_____	ACCUPERMIT ( )
_____	ACI (0)
_____	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	





Pg

58 5-14-19

0630 SAFETY BRIEF

0700 RADIO CHECKS

0736 MINICAMS UP

1115 STARTING MID DAY CATCHING

1125 MID DAY COMPLETE.

1141 VOL COLLECTED

1420 SOIL DRUMS 3752-3769 KILLED.

1424 COMPOSITE COLLECTED

1440 SOIL DRUMS 3752-3766 TRANSFERRED

TO FED PROPERTY.

1700 DAY COMPLETE

A handwritten signature, possibly "R. J. S.", is written in the lower half of the page. A long, straight diagonal line is drawn from the left margin, passing through the signature, and extending towards the bottom right corner of the page.

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 15 May 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 51/74 5-10 mph winds

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Prate, Warren	Askew, Thomas	
Castell, Lorna	Wright, David	Caldwell, Jeff	
Courtney, Kenneth	Yorkshire, Bart	Crawford, Stephen	
Holloway, April		Druyor, Chris	
Marien, Jedidiah		Harris, Brian	
Matter, Phillip		King, Bernie	
Nelms, Bobby		McClellan, Dale	
Oien, Joshua		Nichols, Doug	
Rider, Matthew	<b>LIFE STAR</b>	Threadgill, Marcus	
Schlosser, Ariel	Haupt, Calvin	Wagner, Darien	
Wunschel, Scott	Gumbs Vines, Doreen		
		<b>CEHNC</b>	
		Boles, Judson	
	<b>ACCUPERMIT</b>		
	Vargas, Brandon		
	Williams, Angelo	<b>CENAB</b>	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations in Area B on the apron, removed last of apron, dug to saprolite. Baltimore geologist confirms saprolite in grids -50-70 and -50-90. Confirmation samples of -50-70, -50-90 (all apron area) and 30-70 (outside PDS).

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information  
 \_\_\_\_\_  
 \_\_\_\_\_

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
_____	Berkel ( )
_____	DAVEY ( )
_____	ACCUPERMIT ( )
_____	ACI (0)
_____	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



Pg

59 5-15-19

0630 SAFETY BRIEF

0700 RADIO CHECKS

0742 MINICAMS UP

0825 CONFIRMATION SAMPLE FROM

GRID 30-70

1146 STARTING MIDDAY.

1155 MIDDAY COMPLETE.


1313 VOC COLLECTED FROM APRON.

1351 COMPOSITE COLLECTED

1513 CONFIRMATION SAMPLING FOR APRON COMPLETE

SOIL DRUM 3770-3776 FILLED.

1700 Day COMPLETE



## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 16 May 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 59/76 AM showers 5-10 mph

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Prate, Warren	Askew, Thomas	
Castell, Lorna	Wright, David	King, Bernie	
Courtney, Kenneth	Yorkshire, Bart	Caldwell, Jeff	
Holloway, April		Crawford, Stephen	
Marien, Jedidiah		Druyor, Chris	
Matter, Phillip		Harris, Brian	
Nelms, Bobby		McClellan, Dale	
Oien, Joshua		Threadgill, Marcus	
Rider, Matthew	<b>LIFE STAR</b>	Wagner, Darien	
Wunschel, Scott	Brooke, Bailey	Nichols, Doug	
	Haupt, Calvin		
		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Martinez, Vicente		
	Williams, Angelo	<b>CENAB</b>	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive operations today. Filled in apron/skirt area and removed all drums associated with previous operations. Pumped water off of Area 4 tarp so it can be backfilled.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



B

00 5-16-19

0630 SAFETY BRIEF

0700 RADIO CHECKS

0800 BACK FILLING APRON / PUMPING WATER

1100 CONFERENCE CALL

1700 DAY COMPLETE

*[Handwritten signature]*

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 17 May 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 64/83 light winds

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Prate, Warren	Askew, Thomas	
Castell, Lorna	Wright, David	King, Bernie	
Courtney, Kenneth	Yorkshire, Bart	Caldwell, Jeff	
Marien, Jedidiah		Crawford, Stephen	
Matter, Phillip		Druyor, Chris	
Nelms, Bobby		Harris, Brian	
Oien, Joshua		McClellan, Dale	
Wunschel, Scott		Threadgill, Marcus	
	LIFE STAR	Wagner, Darien	
	Brooke, Bailey	Nichols, Doug	
	Jackson, Mark		
		CEHNC	
	ACCUPERMIT	Boles, Judson	
	Martinez, Vicente		
	Williams, Angelo	CENAB	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive operations today. Removed rain tarp off of Area 4, lined area with geotextile fabric and began backfilling it. 7 loads of backfilled used.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information  
 \_\_\_\_\_  
 \_\_\_\_\_

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
_____	Berkel ( )
_____	DAVEY ( )
_____	ACCUPERMIT ( )
_____	ACI (0)
_____	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

P  
61

5-17-19

0630 SAFETY BRIEF

0700 RADIO CHECKS

0730 BACK FILLING AREA 4<sup>th</sup>

1700 DAY COMPLETE

A handwritten signature in dark ink, consisting of stylized, overlapping loops and strokes, positioned diagonally across the center of the page.

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 20 May 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 74/89 very hot and humid, overcast

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Prate, Warren	Askew, Thomas	
Castell, Lorna	Wright, David	Caldwell, Jeff	
Courtney, Kenneth	Yorkshire, Bart	Crawford, Stephen	
		Druyor, Chris	
		Harris, Brian	
		King, Bernie	
Matter, Phillip		McClellan, Dale	
Nelms, Bobby		Tucker, Robin	
Oien, Joshua		Wagner, Darien	
Rider, Matthew	<b>LIFE STAR</b>		
	Broke, Bailey		
Wunschel, Scott	Jackson, Mark		
		<b>CEHNC</b>	
		Boles, Judson	
	<b>ACCUPERMIT</b>		
	Overton, Robert		
	Williams, Angelo	<b>CENAB</b>	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive operations today. Pumped 400 gallons of water today. Removed silt and construction fences to prepare for Area 5 intrusive operations. Put stone in former Areas 1&2 then brought in 11 loads of backfill to begin making ramp for Area 5.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

P<sub>4</sub>

62 5-20-19

0630 SAFETY BRIEF

0730 RACK FILLING

1700 Day complete

~~SECRET~~

# SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 21 May 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 59/73 5-15 mph winds

## Personnel on Site

PARSONS	ZES	ECBC	
Blevins, Robert	Prate, Warren	Askew, Thomas	
Castell, Lorna	Wright, David	Caldwell, Jeff	
Courtney, Kenneth	Yorkshire, Bart	Crawford, Stephen	
Holloway, April		Druyor, Chris	
Marien, Jedidiah		Harris, Brian	
Matter, Phillip		King, Bernie	
Nelms, Bobby		McClellan, Dale	
Oien, Joshua		McGill, Andre	
Rider, Matthew	<b>LIFE STAR</b>	Tucker, Robin	
Wunschel, Scott	Jackson, Mark	Wagner, Darien	
	Gumbs Vines, Doreen		
		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Overton, Robert		
	Arteage, Carlos	<b>CENAB</b>	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive operations today. Put gravel in Area B adjacent to the 4835 foundation. Ramp to Area 5 completed moved Komatsu 35 and 228 up to second level. Set up drums for Area 5 excavation.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information  
 \_\_\_\_\_  
 \_\_\_\_\_

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



R

63 5-21-19

0630 SAFETY BRIEF

0730 BACK FILLING

1700 DAY COMPLETE

0830 [illegible] [illegible] [illegible]

1000 [illegible] [illegible] [illegible]

1130 [illegible]

1230 [illegible] [illegible] [illegible]

1300 [illegible]

1400 [illegible] [illegible] [illegible]

1500 [illegible] [illegible]

1600 [illegible] [illegible] [illegible]

1700 [illegible] [illegible] [illegible]

1800 [illegible] [illegible]

1900 [illegible]

2000 [illegible]

2100 [illegible]

2200 [illegible]

2300 [illegible]

2400 [illegible]

2500 [illegible]

2600 [illegible]

2700 [illegible]

2800 [illegible]

2900 [illegible]

3000 [illegible]

3100 [illegible]

3200 [illegible]

3300 [illegible]

3400 [illegible]

3500 [illegible]

3600 [illegible]

3700 [illegible]

3800 [illegible]

3900 [illegible]

4000 [illegible]

4100 [illegible]

4200 [illegible]

4300 [illegible]

# SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 22 May 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 59/76 mostly sunny, variable winds

## Personnel on Site

PARSONS	ZES	ECBC	
Blevins, Robert	Prate, Warren	Askew, Thomas	
Castell, Lorna	Wright, David	King, Bernie	
Courtney, Kenneth	Yorkshire, Bart	Caldwell, Jeff	
Holloway, April		Crawford, Stephen	
Marien, Jedidiah		Druyor, Chris	
Matter, Phillip		Harris, Brian	
Nelms, Bobby		McClellan, Dale	
Oien, Joshua		Tucker, Robin	
Rider, Matthew	<b>LIFE STAR</b>	Wagner, Darien	
Wunschel, Scott	Brooke, Bailey	McGill, Andre	
	Gumbs Vines, Doreen		
		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Overton, Robert		
	Williams, Angelo	<b>CENAB</b>	
	Arteage, Carlos	Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations in Area 5, 57 drums filled, Area 5 completed. No glass, CACAM or any evidence of AUES noted.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



P<sub>2</sub>

64 5-22-19

0630 SAFETY BRIEF

0700 RADIO CHECKS

0811 MINICAMS UP

0829 TEAM 2, RIDER, RICHARDS, WRIGHT

MID "D" DIGGING AREA 5".

0833 VOC COLLECTED

0937 MINICAMS NEEDS TO RECALIBRATE.

1000 MINICAM BACK UP.

1200 STARTING MIDDAY CHALKING.

1225 MIDDAY COMPLETE

1235 TEAM 1 DOWN, COURTESY WRIGHT.

1437 COMPOSITE COLLECTED, SOIL DRUMS

3777-3833 FILLED

1700 DAY COMPLETE



[illegible]



B

65 5-23-19

0630 SAFETY BRIEF.

0700 RADIO CHECKS.

1040 SOIL DRUMS 3777-3833 TRANSPORTED  
TO FEDERAL PROPERTY.

1100 CONFERENCE CALL

1130 PBT CALL

1700 Day COMPLETE

*[Handwritten signature]*



P<sub>9</sub>

66 5-24-19

0630 SAFETY BRIEF

0700 RADIO CHECKS

1700 DAY COMPLETE

1700 DAY COMPLETE

A handwritten signature in black ink, consisting of stylized, overlapping loops and strokes, positioned diagonally across the center of the page.

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 28 May 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Prate, Warren	Brown, Matt	
Castell, Lorna	Wright, David	Caldwell, Jeff	
Courtney, Kenneth	Yorkshire, Bart	Crawford, Stephen	
Holloway, April		Druyor, Chris	
		Harris, Brian	
Matter, Phillip		King, Bernie	
Nelms, Bobby		McClellan, Dale	
Oien, Joshua		McGill, Ande	
Rider, Matthew	<b>LIFE STAR</b>	Threadgill, Marcus	
Wunschel, Scott		Tucker, Robin	
		Tucker, Willie	
		<b>CEHNC</b>	
		Boles, Judson	
	<b>ACCUPERMIT</b>		
	Overton, Robert		
	Williams, Angelo	<b>CENAB</b>	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information  
 \_\_\_\_\_  
 \_\_\_\_\_

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
_____	Berkel ( )
_____	DAVEY ( )
_____	ACCUPERMIT ( )
_____	ACI (0)
_____	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

R<sub>1</sub>

67 5-28-19

0630 SAFETY BRIEF

0703 LIGHTNING HOLD.

0750 OTC LIGHTNING HOLD.

1700 DAY COMPLETE

*[Handwritten signature]*

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 29 May 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 74/93 hot, humid thunderstorms late.

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Prate, Warren	Brown, Matt	
Castell, Lorna	Wright, David	Caldwell, Jeff	
Courtney, Kenneth	Yorkshire, Bart	Crawford, Stephen	
Holloway, April		Druyor, Chris	
Matter, Phillip		Harris, Brian	
Nelms, Bobby		King, Bernie	
Oien, Joshua		McClellan, Dale	
Rider, Matthew		Threadgill, Marcus	
Wunschel, Scott	<b>LIFE STAR</b>	Tucker, Robin	
		Tucker, Willie	
		Wagner, Darien	
		<b>CEHNC</b>	
	<b>ACCUPERMIT</b>	Boles, Judson	
	Overton, Robert		
	Williams, Angelo	<b>CENAB</b>	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive operations today. C.P. Johnson surveyed in 3 arsenic grids today. Komatsu 228 serviced by factory mechanic, once service was done the entire 228 was cleaned. Set up Komatsu 35 for cleaning. Contacted Densel (HVAC contractor) to perform a service call in AC units at Fed Prop.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT (2)
ACI (0)
CPJ (1)

**Problems encountered/resolutions:**

A/C issue reported to me by USACE rep Brian Steelman about trailer A/C's at Fed Prop, HVAC contractor called.

**Instructions given by government personnel:****Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



Pg.

68 5-29-19

0630 SAFETY BRIEF.

0700 RADAR CHECKS CPI ON SITE.

0730 RISH MAINTENANCE ON SITE

1100 RISH MAINTENANCE OFF SITE.

1700 DAY COMPLETE

*[Handwritten signature]*

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 30 May 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 74/90 overcast, humid, thunderstorms in PM.

**Personnel on Site**

PARSONS	ZES	ECBC	
Blevins, Robert	Prate, Warren	Brown, Matt	
Castell, Lorna	Wright, David	Caldwell, Jeff	
Courtney, Kenneth	Yorkshire, Bart	Crawford, Stephen	
Holloway, April		Druyor, Chris	
Marien, Jedidiah		Harris, Brian	
Matter, Phillip	ACCUPERMIT	King, Bernie	
Nelms, Bobby	Arteage, Carlos	McClellan, Dale	
Oien, Joshua	Williams, Angelo	Threadgill, Marcus	
Rider, Matthew		Tucker, Robin	
Wunschel, Scott		Tucker, Willie	
		CEHNC	
		Boles, Judson	
		CENAB	
		Steelman, Todd	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive operations. Removed medical monitoring tent and the liner for the PDS, along with some floor tiles. Cleaned out the dress-out trailer. Sent out ADR-1500 dust monitor for calibration. Brushed/shoveled off Komatsu 35 and washed it down.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information  
 \_\_\_\_\_  
 \_\_\_\_\_

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
_____	Berkel ( )
_____	DAVEY ( )
_____	ACCUPERMIT (2)
_____	ACI (0)
_____	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

P  
19  
69

5-30-19

0630 Safety BRIEF

0700 RADIO CHECKS.

1100 CONFERENCE CALL

1700 Day COMPLETE

~~Handwritten signature/initials~~

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 31 May 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 70/85 light winds

**Personnel on Site**

PARSONS	ZES	ECBC	
Castell, Lorna	Prate, Warren	Caldwell, Jeff	
Courtney, Kenneth	Wright, David	Crawford, Stephen	
Marien, Jedidiah	Yorkshire, Bart	Druyor, Chris	
Matter, Phillip		King, Bernie	
Nelms, Bobby		McClellan, Dale	
Oien, Joshua	<b>ACCUPERMIT</b>	Threadgill, Marcus	
Rider, Matthew	Arteage, Carlos		
Wunschel, Scott	Williams, Angelo		
	<b>CENAB</b>		
	Steelman, Todd		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive operations. ECBC removed PDS tent and most floor mats. Weighed 85 drums for future HAZMAT shipment. Moved construction pads off of grid 30-50 in preparation for arsenic removal. Posted new public space permits after lamination.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information  
 \_\_\_\_\_  
 \_\_\_\_\_

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
_____	Berkel ( )
_____	DAVEY ( )
_____	ACCUPERMIT ( )
_____	ACI (0)
_____	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

70 5-31-19

0630 SAFETY BRIEF

0700 RADIO CHECKS.

0715 Teams preparing down range area for intensive operations  
Monday in gear 30-50. Castell & Courtney weighing  
drums & Fed Prep. EXBC removed PDS tent & some flooring.

1500 Vehicle inspections & maintenance. Traffic dismissed

~~1700~~ End of day, all secure. *[Signature]*

*nothing follows*

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 3 June 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 59/72 overcast, rain. Winds 5-15 mph

Personnel on Site

PARSONS	ZES		
Blevins, Robert	Prate, Warren		
Castell, Lorna	Wright, David		
Courtney, Kenneth	Yorkshire, Bart		
Holloway, April			
Marien, Jedidiah			
Matter, Phillip	ACCUPERMIT		
Nelms, Bobby	Vargas, Brian		
Oien, Joshua	Vargas, Gustavo		
Rider, Matthew			
Wunschel, Scott			
	CENAB		
	Steelman, Todd		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Begin removal of backfill over grid 30-50, no samples taken. CCDC removes cascade trailer, used 2WD truck and it could not pull trailer out of gravel, excavator used. Weighed 72 drums, dumped and lined 3 rollofs.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors


Contractors

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



P  
GT

7/ 6-3-19

0630 SAFETY BRIEF

0700 RADIO CHECKS

0715 PREPARE TO EXCAVATE GRID 30, -50

0900 EYE WASH IN PLACE W/ NEW SOLUTION.

1700 END OF DAY

*[Handwritten signature]*

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 4 June 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 59/78 overcast

**Personnel on Site**

PARSONS	ZES		
Blevins, Robert			
Castell, Lorna	Wright, David		
Courtney, Kenneth	Yorkshire, Bart		
Holloway, April			
Marien, Jedidiah			
Matter, Phillip	ACCUPERMIT		
Nelms, Bobby	Vargas, Brian		
Oien, Joshua	Vargas, Gustavo		
Rider, Matthew			
Wunschel, Scott			
	CENAB		
	Steelman, Todd		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Backfill removal in grid 30-50, then removed 2 feet of saprolite and resampled. 4 confirmation samples taken; Floor, North wall, East wall, West wall. Set up construction fence around grid once completed and set up -30-70.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



P<sub>9</sub>

72 6-4-19

0630 SAFETY BRIEF

0700 RADIO CHECKS

0815 EXCAVATING GRID 30-50

1003 VEC COLLECTED FOR ROLL OFF 290978.

1131 VEC COLLECTED FOR ROLL OFF 274987

1330 GRID 30-50 SAMPLING COMPLETE.

1700 DAY COMPLETE

*[Handwritten signature]*

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 5 June 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 65/83 partly cloudy

Personnel on Site

PARSONS	ZES		
Blevins, Robert	Prate, Warren		
Castell, Lorna	Wright, David		
Courtney, Kenneth	Yorkshire, Bart		
Holloway, April			
Marien, Jedidiah			
Matter, Phillip	ACCUPERMIT		
Nelms, Bobby	Vargas, Brian		
Oien, Joshua	Vargas, Gustavo		
Rider, Matthew			
Wunschel, Scott			
	CENAB		
	Steelman, Todd		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Begin intrusive operations in grid -30-70, only removing backfill today. Thunderstorms ended downrange operations at approximately 4PM, heavy storms moved in. 3 truckloads sent to subtitle D landfill.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information  
 \_\_\_\_\_  
 \_\_\_\_\_

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
_____	Berkel ( )
_____	DAVEY ( )
_____	ACCUPERMIT ( )
_____	ACI (0)
_____	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

73 6-5-19

0630 SAFETY BRIEF

0700 RADIO CHECKS.

0800 DICKING L210 -30, -70 "OVER BURDEN".

1700 END OF DAY

*[Handwritten signature]*



## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 6 June 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 70/85 partly cloudy

**Personnel on Site**

PARSONS	ZES		
Courtney, Kenneth	Prate, Warren		
Marien, Jedidiah	Wright, David		
Matter, Phillip	Yorkshire, Bart		
Nelms, Bobby			
Oien, Joshua			
Rider, Matthew			
Wunschel, Scott	<b>ACCUPERMIT</b>		
Holloway, April	Vargas, Brian		
	Vargas, Gustavo		
	<b>CENAB</b>		
	Steelman, Todd		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Intrusive operations in grid -30-70. Removed 2 rollofs of backfill then began overexcavating 2 feet from floor of grid. All backfill rollofs were dumped and relined.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



R

74

6-6-19

0630 JERRY BRIEF

0700 RADIO CHECKS

0715 REVOLVING OVERHEADS GRID -30,-70.

1224 VOC COLLECTED FOR ROLLOFF 291440.

1358 VOC COLLECTED FOR ROLLOFF 291441

1511 COMPOSITE COLLECTED.

1700 DAY COMPLETE

R  
JR





R

75 6-10-19

0630 SAFETY BRIEF / RADIO CHECKS

0905 DAVID KLINE ON SITE

1015 DAVID KLINE OFF SITE.

1020 SAMPLING COMPLETE FOR GRID -30,-70

1 DAY COMPLETE

*[Handwritten signature]*



# SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 11 June 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 63/80 winds 5-15

## Personnel on Site

PARSONS	ZES		
Courtney, Kenneth	Prate, Warren		
Holloway, April	Wright, David		
Marien, Jedidiah	Yorkshire, Bart		
Matter, Phillip			
Nelms, Bobby			
Oien, Joshua	ACCUPERMIT		
Rider, Matthew	Arteage, Carlos		
Wunschel, Scott	Williams, Angelo		
	CENAB		
	Steelman, Todd		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Backfill 30-50 as results came back with no further arsenic exceedence. Begin intrusive operations on 10-90 and got to sampling depth. Cut up 33 drums for subtitle D. Surveyor took elevation shots on 30-50 before backfilling, also surveyed locations for benzaldahyde resampling grids: 70-30, 70-50, 90-30, 90-50. 4 subtitle D trucks loaded out.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

### Visitors


### Contractors

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



P<sub>2</sub>

76 6-11-19

0630 SAFETY BRIEF

0710 SAM DEMOS W/ CPT ON SITE.

RACE FILING GRID, 30, -58

1300 DIGGING GRID 10-90

ROCK 291439 ' VOC COLLECTED.

1700 END OF DAY.

A handwritten signature, possibly "R. J. Smith", is written across the middle of the page. A large, thin diagonal line is drawn from the left margin, passing through the signature, and extending towards the bottom right corner of the page.



[illegible]

R

77 6-12-19

0630 SAFETY BRIEF

0700 RADIO CHECKS

1700 Day complete

*[Handwritten signature]*



## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 13 June 2019  
 Site Location: 4825 Glenbrook Road

Weather:  
 65/75 rain

Personnel on Site

PARSONS	ZES		
Courtney, Kenneth	Prate, Warren		
Holloway, April	Wright, David		
Marien, Jedidiah	Yorkshire, Bart		
Matter, Phillip			
Nelms, Bobby			
Oien, Joshua	ACCUPERMIT		
Rider, Matthew	Arteage, Carlos		
Wunschel, Scott	Williams, Angelo		
	CENAB		
	Steelman, Todd		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive operations today. Cut up 45 plastic drums for scrap.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors


Contractors

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

Pg

78

6-13-19

0630 SAFETY BRIEF

0700 RA116 CHECKS

1100 CONFERENCE CALL OFFICIAL PROCEEDINGS

1700 DAY COMPLETE

~~Pg 78~~



R

79

6-17-19

0630 SAFETY BRIEF


0700 RADIO CHECKS

0800 WORKING AT FEDERAL PROPERTY.

1700 DAY COMPLETE

*[Handwritten signature]*



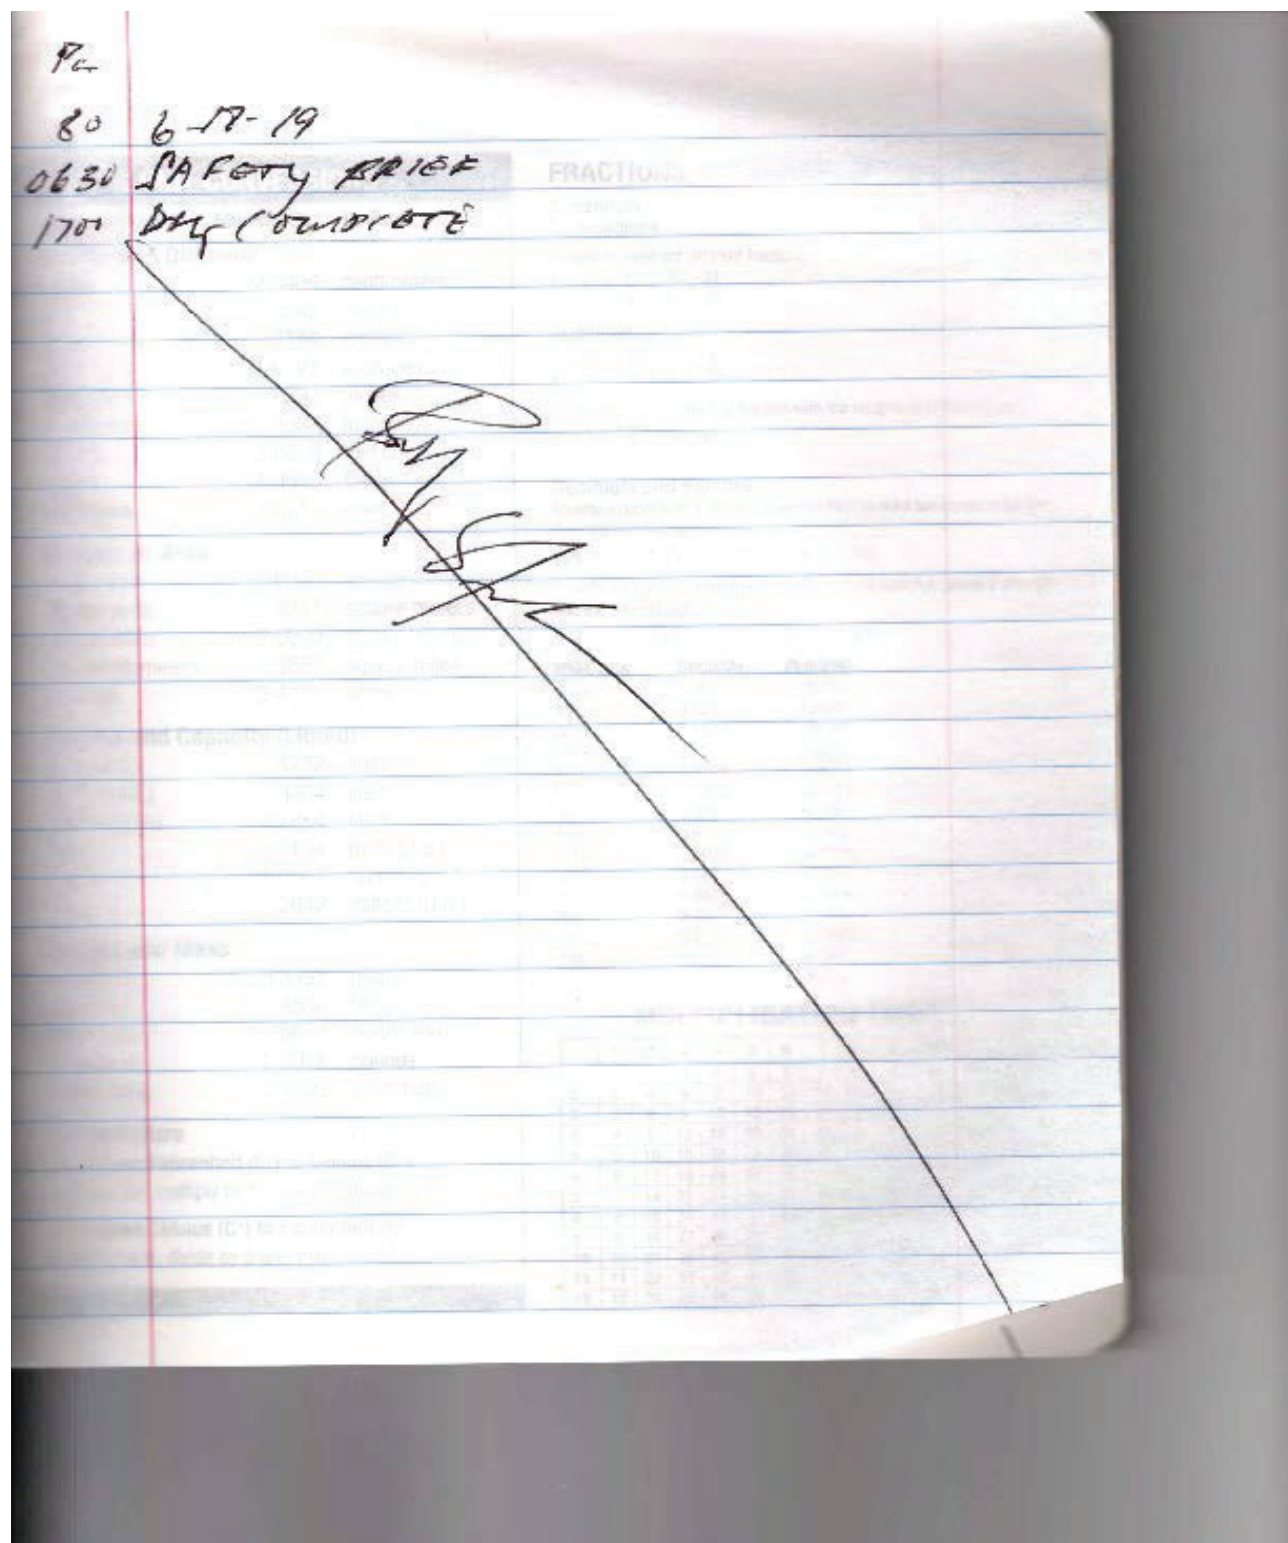







Pg 1 6-20-19

0630 Morning Safety Brief

0645 Team Preparing to go to the Federal property site, teams are dumping cleared Soil drums and Prepping Haz drums for shipment.

1300 Checked on teams, All PPE Good.

1530 Teams performing end of week clean up and maintenance.

1710 Day Complete.

*John M. [Signature]*



PG 2

6-24-19

0630 Morning Safety Brief.

0650 Team working at the Federal Property Site  
loading out Haz shipments.

0900 Checked on teams, one shipment loaded, all  
looks Good.

1200 Lunch Break

1400 Three trucks of Haz waste drums are loaded,  
team will dump drums

1630 Team dumped 22 Non-Haz Soil drums.

1700 Day Complete.

*[Signature]*







PG 3

6-25-19

- 0630 Morning Safety Brief.
- 0640 Team Set up
- 0735 Team Pumping water from Grid -30/-70.
- 0812 Team taking First load of 850 Gal to the Fed prep Site.
- 0915 Team taking the Second load of 850 Gal to the Fed prep for Storage.
- 1030 Team dropped off Roll off # 291441, team will continue Filling the Roll off Box with additional 1 FT North on Grid -30/-70. Dust Monitor Reading 8.2.
- 1045 Additional 1 FT North excavation Complete.
- 1103 North wall Confirmation Sample Complete.
- 1110 Dust Monitor Reading 15.4
- 1135 Roll off out to Fed Site for Storage.
- 1200 Lunch.
- 1230 Team in Dumping cleaned Drums & Roll off Boxes at Fed prep.
- 1630 Site Clean up.
- 1700 Day Complete



# SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 26 June 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 mid 90's overcast, humid. Late rain showers

## Personnel on Site

PARSONS	ZES		
Courtney, Kenneth	Prate, Warren		
Holloway, April	Wright, David		
Marien, Jedidiah	Yorkshire, Bart		
Matter, Phillip			
Oien, Joshua			
Rider, Matthew			
Wunschel, Scott			
	ACCUPERMIT		
	Williams, Donald		
	Williams, Angelo		
	Vargas, Brandon		
	CENAB		
	Steelman, Todd		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive operations today. Surveyed in 10-90 prior to backfilling, surveyed north edge of -10-90 (AC pad) then surveyed in -50-90 for possible upcoming mercury removal. Backfilled 10-90 after arsenic results came back clear. 20 drums dumped. Densel came by for site visit to proposal of moving 4835 AC units to back patio. Replaced deteriorating sandbags along fence perimeter.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

### Visitors


### Contractors

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

PG-4 6-26-19

0630 Safety Brief

0645 Team Prepping to cut grass at 4825, backfill the excavation in the Magenta area.

0705 Surveyor on site.

0833 Dore kline from ECBC is on site, Surveyor off site.

0852 ECBC off site.

1230 Team completed filling in the excavation in the magenta area.

1245 lunch.

1315 Team is at the Federal property site dumping cleared soil drums &amp; Prepping for the next Haz waste shipment.

1630 End of day clean up.

1700 Day Complete.





PG-5

6-27-19

0630 Morning Safety Brief.

0645 Team Trapping to work at the Federal property site dumping cleared Soil Drums.

0900 At The Fed site Setting up the wet Bulb.

0930 50/50 work Rest cycle For light work  
temp 89.3

1028 25/75 work Rest cycle For light work.

1144 93.5 WBGT Suxos ~~sop~~ Suspending work.

1200 Day Complete.





PGB 7-1-19

0630 Morning Briefing

0645 Team prepping to load Haz waste trucks at the Federal property site. Three truck loads of drums going out.

0900 Checked on team activities, 1st load out &amp; waiting for additional trucks to arrive.


1030 Team loading the second truck w/ drums.

1230 lunch.

1300 Team transitioning to cutting old Soil Drums.

1630 End of day clean up.

1700 Day Complete.

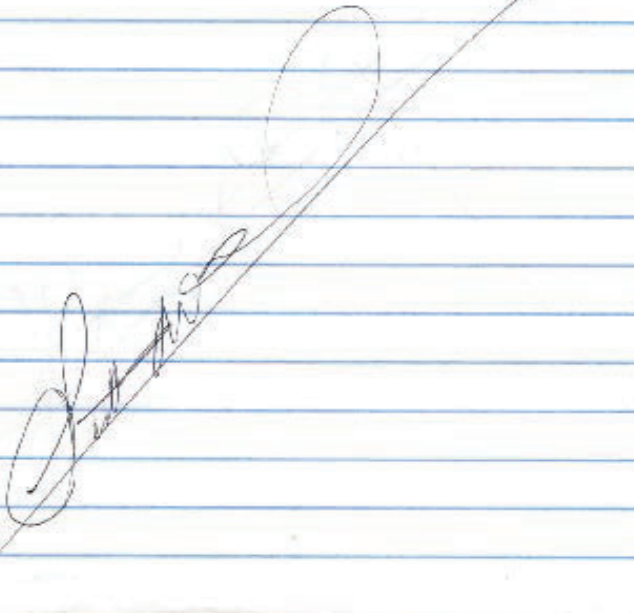



PG 7

7-2-19

0630 Morning Safety Brief

0640 Team Prepping to work at Fed prop Site.  
They will be cutting empty used soil drums.

0800 Checking on team at the Fed property Site.


1000 Team is taking Appropriate Breaks For Heat  
level

1200 Lunch

1230 Team Resuming operations

1630 End of day clean up

1700 Day Complete

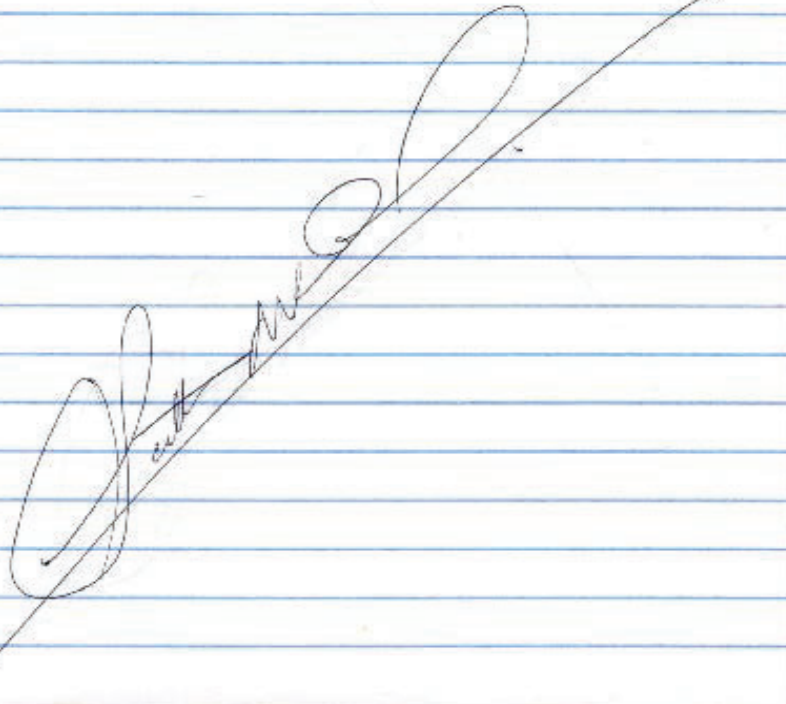



PG 8 7-3-19

0630 Morning Safety Briefing

0645 Team prepping to work at the Federal property  
Site dumping cleared Roll-off Boxes + cutting  
empty Soil drums.

0900 checked on the team, All PPE is Good.

1130 lunch

1215 checked on team, Taking breaks for Heat.

1600 Team Securing the site for the Holiday  
Weekend.

1700 Day Complete.

A large, stylized handwritten signature in black ink, written diagonally across the lower half of the page. The signature is cursive and appears to be "J. J. [unclear]".



# SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 8 July 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 Rain w/ thunderstorms in AM, then sunny high 79.

## Personnel on Site

PARSONS	ZES		
Courtney, Kenneth	Prate, Warren		
Holloway, April	Wright, David		
	Yorkshire, Bart		
Matter, Phillip			
Oien, Joshua			
Rider, Matthew			
Wunschel, Scott	ACCUPERMIT		
	Marin, Naum		
	Williams, Angelo		
	CENAB		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

2 hour lightning hold in the morning then pumped 3650 gallons of water, which took the rest of the day.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information  
 \_\_\_\_\_  
 \_\_\_\_\_

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

7-8-19

0630 Morning Safety Meeting.

0815 Site is on lightning hold.

0845 More lightning strikes &amp; heavy rain.

0900 Still lightning &amp; heavy rain.

0925 lightning &amp; rain continues, 2.4 inches of rain in the last hour.

0935 lightning moving out of the area on 30 min wait.

1005 Site is off lightning hold. Team preparing to pump water from the excavation area at the 4825 site. 2.62 inches so far for this rain event.


1200 Lunch.

1230 Continued pumping water.

1459 Water pumping complete. 5 loads of 850 Gallons &amp; one load of 250 Gallons.

1515 Team working on erosion controls.

1700 Day Complete.

A large, stylized handwritten signature in black ink, written over the bottom portion of the page. The signature is slanted upwards from left to right and appears to be a cursive or semi-cursive name.



PG 10 7-9-19

0630 Morning Safety Brief

0645 Team prepping to work at the Federal property  
Site Dumping Chemical Soil Drums.

0915 Checked on the team, All PPE Good.

1145 Brenda Barber is on site.

1200 Lunch

1300 Checked on team.

1630 End of day Clean up.

1700 Day Complete.

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 10 July 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 Sunny and hot 90's.

**Personnel on Site**

PARSONS	ZES		
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Holloway, April	Yorkshire, Bart		
Marion, Jed			
Matter, Phillip			
Oien, Joshua	ACCUPERMIT		
Rider, Matthew	Marin, Naum		
Wunschel, Scott	Williams, Angelo		
	CENAB		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive operations today. 3 subtitle D loads of soil removed to landfill. Surveyed depth and edges of -30-70 and backfilled hole. Dumped 23 soil drums.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information  
 \_\_\_\_\_  
 \_\_\_\_\_

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
_____	Berkel ( )
_____	DAVEY ( )
_____	ACCUPERMIT ( )
_____	ACI (0)
_____	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

PG 11 7-10-19

0630 Morning Briefing

0645 Team is prepping to Fill in the excavation  
in Grid - 301-70.

0700 Surveyor is on Site

0710 New Sample took is on Site, tracing w/  
April

0815 Team continuing to Fill in grid. All PPE OK.

1030 Glenbrook Rd. closed for Water Main Repair.  
Team using clean Fill from the Site to  
Fill in along 4835 basement wall.


1200 Lunch.

1230 Team continues to Fill along the basement  
wall & also cutting drums at the Ford  
Prop Site.

1430 checked on teams, all looks good.

1630 End of day clean up.

1700 Day Complete.

A large, stylized handwritten signature, likely "J. Smith", is written across the bottom half of the page. The signature is written in dark ink and is somewhat slanted to the right.



## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 11 July 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 Sunny and hot w/ scattered PM storms. High 90's.

Personnel on Site

PARSONS	ZES		
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Holloway, April	Yorkshire, Bart		
Marion, Joe			
Matter, Phillip			
Oien, Joshua	ACCUPERMIT		
Rider, Matthew	Marin, Naum		
Wunschel, Scott	Williams, Angelo		
	CENAB		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive operations today. Finished backfilling -30-70, cleaned off construction pads and repaired super silt fence downrange. Dumped 13 drums and cut up 36. Called Denel to set up schedule for AC relocations.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information  
 \_\_\_\_\_  
 \_\_\_\_\_

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

PS 12 7-11-19

0630 Morning Safety brief.

0645 Team Prepping to continue backfilling Grid  
-301-70.1100 Team is moving to the Federal property site  
to dump cleared soil drums & empty  
drums.


1200 lunch

1230 checked on turn from wet bulb is 50/50  
work 17.5L cycle.

1415 wet bulb is 25/75 work 12.5L cycle.

1630 End of week clean up &amp; Maint.

1700 Day Complete.

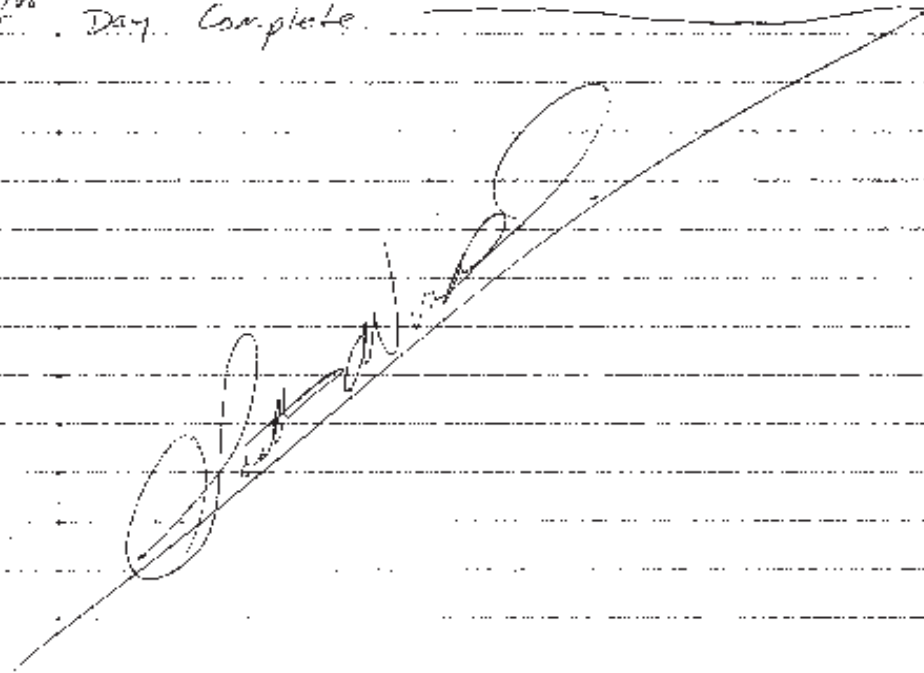

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 15 July 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 mostly clear high 80's, winds 10-15 mph

**Personnel on Site**

PARSONS	ZES		
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Holloway, April	Yorkshire, Bart		
Marion, Joe			
Matter, Phillip			
Oien, Joshua	<b>ACCUPERMIT</b>		
Rider, Matthew	Marin, Naum		
Wunschel, Scott	Williams, Angelo		
	<b>CENAB</b>		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive operations today. Dumped 42 soil drums and cut up 55 for disposal. Scheduled to start AC relocation tomorrow.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information  
 \_\_\_\_\_  
 \_\_\_\_\_

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

PL 13

7-18-19

0630 Morning Safety Brief

0645 Team prepping to work at the Federal property  
Site cutting old Soil drums

0930 Checked on the team, all looks good.

1200 lunch

1335 Very Hot, teams on 25 L75 Work Tool while  
working outside

1630 End of Day, Clean up.

1700 Day Complete

*[Handwritten signature]*  
J. [unclear]

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 16 July 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 Hot and humid, mid 90's. Light winds

**Personnel on Site**

PARSONS	ZES		
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Holloway, April	Yorkshire, Bart		
Marion, Joe			
Matter, Phillip			
Oien, Joshua	ACCUPERMIT		
Rider, Matthew	Marin, Naum		
Wunschel, Scott	Williams, Angelo		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive operations today. Begin AC relocation from 4825 to patio of 4835. Begin to replace rotted door at Fed Prop trailer (door nearest Sibley). 444 pallets were stacked and loaded into a tractor trailer and removed from sight. Inventory of M40 filters, 63 remaining.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information  
 \_\_\_\_\_  
 \_\_\_\_\_

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

PG 11

7-16-19

0630 Morning Safety Brief

0640 Team Prepping for operations


0700 Subcontractors for Denise are on site they  
will be moving the 4835 AC units.0735 Team is at the Federal property site loading  
pallets on a truck for Diaper's team  
also making repairs to one of the exterior  
doors on the Fed prop trailers.

1200 Lunch

1310 Checked on the team, all looks good.

1630 End of Day Clean up.

1700 Day Complete.

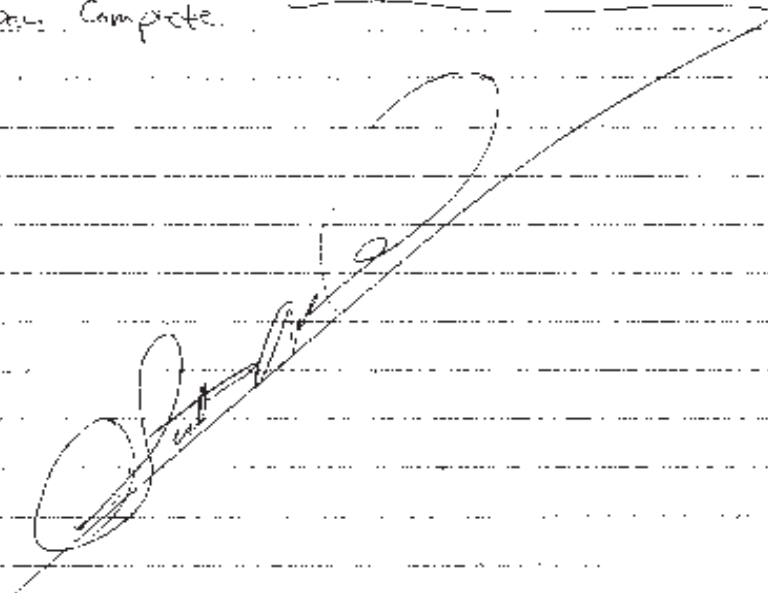



## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 17 July 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 Very hot and humid mid 90's, light winds

**Personnel on Site**

PARSONS	ZES		
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Holloway, April	Yorkshire, Bart		
Marion, Joe			
Matter, Phillip			
Oien, Joshua	ACCUPERMIT		
Rider, Matthew	Marin, Naum		
Wunschel, Scott	Williams, Angelo		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive operations today. AC relocation and Fed Prop door replacement still ongoing. Recovered and remarked 2 HAZ rolloffs at Fed Prop. Water line from temporary street reroute line blew a fitting so I contacted DC Water and it was repaired.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found None

New Equipment on Site: N/A

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

PG 15 7-17-19

0630 Morning Briefing

0645 Team doing Take 5's

0830 Dental Personnel are on site to continue moving  
AC units. Team is working at the Federal  
Property Site.


1010 Checked on the teams, all is ok.

1200 Lunch.

1345 Checked on ~~the~~ team at the Federal property  
Site. Team is on wait/list cycles for hot.

1630 End of Day Clean up.

1700 Day Complete.

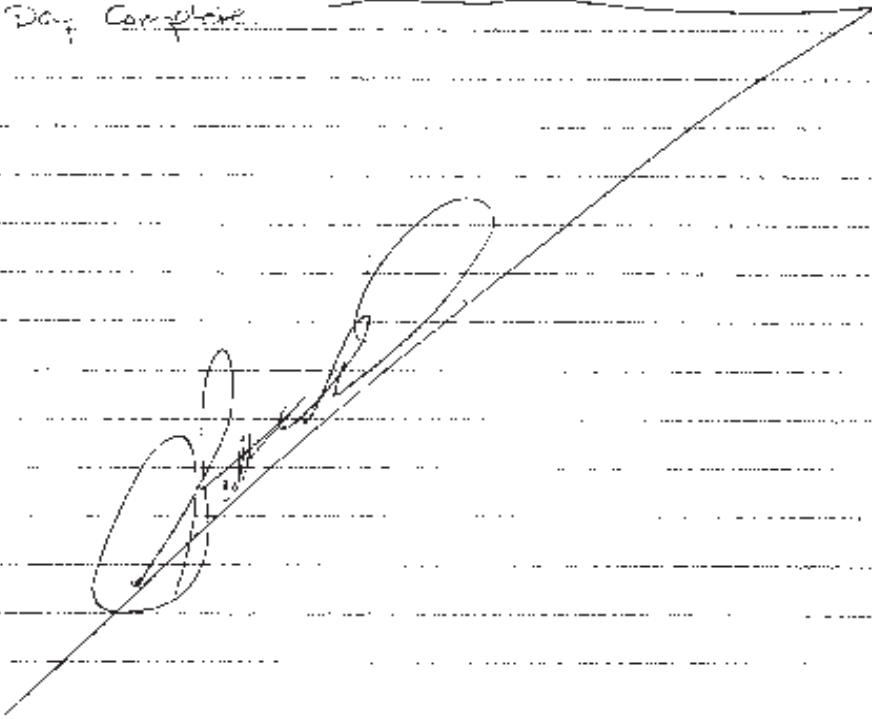



PG 14 7-18-19

0630 Morning Safety Brief

0645 Team Prepping to work at the Federal property.  
Site dumping & cutting drums.

0725 Denset Contractors continuing to work on

4835 AC units. Team is at Fed Site.

1010 Checked on teams, all looks Good.

1230 Lunch.

1355 Starting on the Team.

1600 End of week clear up & Maint.

1700 Day Complete.

*[Handwritten signature]*

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 22 July 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 high 80's partly cloudy, light breeze

**Personnel on Site**

PARSONS	ZES		
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Joe	Yorkshire, Bart		
Matter, Phillip			
Oien, Joshua			
Rider, Matthew			
Wunschel, Scott	<b>ACCUPERMIT</b>		
Banks, Janelle	Marin, Naum		
	Williams, Angelo		
	<b>CENAB</b>		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Removed former AC pad and all associated left over piping and hardware. Placed 550 gallon water tank to catch runoff from south side roof line of 4835 Glenbrook. Begin HTW arsenic dig on north edge of -10-90. Suspect AUES glassware found, PDT notified and excavation mitigatged.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found Possible AUES glass bottle found in -10-90, may have a stopper in mouth of jar.

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

**Problems encountered/resolutions:**

Grid -10-90 mitigated, excavation not complete.

**Instructions given by government personnel:****Activities anticipated for tomorrow:**

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

(17) 7-27-19

0630 Morning Safety Brief

0645 Team prepping to excavate the north wall of Grid -10/-90.

0700 Team setting up Dust Monitor & EPDS.

0900 Team Removing Clean backfill.

1000 Roll off # 291440 Arrived on Site.

1013 Dust Monitor Reading 17.2. Team beginning north wall excavation of -10/-90.

1022 VOC Sample Collected.

1035 Excavation operation suspended for Densest personnel working on 4835 AC units.

1118 Team Resuming excavation ops. Dust Monitor 21.9.

1153 Roll off 291440 Going out.

1225 New Roll off # 291439 on site.

1230 Lunch.

1331 Dust Monitor Reading 17.6

1333 VOC Sample Collected.

1350 Team Finds Suspect Auto Glass at the boundary of Grid -10/-90 & area 2. Team. Suspended excavation operations, mitigated & processed out thru the EPDS.

1400 Excavation area is covered & Roll off removed.

1120 Team has covered the clean soil pile due to expected severe T-storms.



## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 23 July 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_

**Personnel on Site**

PARSONS	ZES		
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Joe	Yorkshire, Bart		
Matter, Phillip			
Oien, Joshua			
Rider, Matthew			
Wunschel, Scott	<b>ACCUPERMIT</b>		
Banks, Janelle	Marin, Naum		
	Williams, Angelo		
	<b>CENAB</b>		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

(19)

7-23-19

0630 Morning Briefing

0645 Team in Preparing to work on the Federal  
projects Site. They will be cutting down  
as weather permits and organizing equipment  
in the quonset hut

0710 Diesel personnel are back to complete the  
AC work at 4335.

0730 Checked on the team they are working  
in the quonset hut due to Rain.

1200 Lunch

1425 Diesel Personnel are finished w/ work &  
off site.

1600 End of day clean up.

1700 Day Complete

*[Handwritten signature]*



(20)


7-24-19

0630 Morning Safety brief

0640 Team preparing to work at the Fed Site  
dumping & cutting drums.1200 Team is on lunch. CP Personnel attending a  
PJT call about the Suspect Russ Bottle found on  
7-22-19.1310 Team is at the 4865 site moving equipment  
in preparation for a Friday operation to  
remove the suspect bottle and collect soil samples.1405 At the Fed site making a general inspection.  
Some of the team extension cords used to  
be repaired due to cuts & cracks.

1600 End of day clean up

1700 Day Complete.

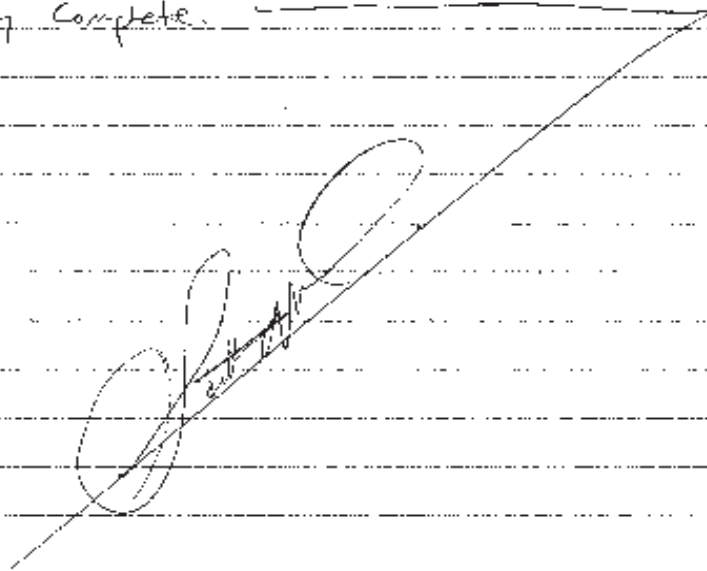

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 25 July 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 high 80's, partly cloudy

**Personnel on Site**

PARSONS	ZES		
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Joe	Yorkshire, Bart		
Matter, Phillip			
Rider, Matthew	ACCUPERMIT		
Wunschel, Scott	Marin, Naum		
	Williams, Angelo		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No monitored/sampled intrusive operations today. Moved clean backfill pile from -10-90 to make room for ramp to area where item is located. Dug ramp to bottom depth of excavation in -10-90, only digging thru clean backfill.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

(21) 7-25-19

0630 Morning Safety Briefing

0645 Team is prepping to excavate on west Ramp  
to grad. -10 ft -90

1015 Team Completed Ramp Construction & Set up  
Exc. tomorrow's ECBC quantities

1100 Team Working at the Federal property side.

1200 Lunch

1500 Checked on the team all good.

1630 End of day clean up.

1700 Day Complete.



# SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 26 July 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 high 88, mostly clear and sunny, light breeze

## Personnel on Site

PARSONS	ZES	CCDC
Bryant, Joe		Henderson, Amos
Courtney, Kenneth		McGill, Andre
Matter, Phillip	Yorkshire, Bart	Wooten, Mike
Rider, Matthew		Jenkins, Troy
Wunschel, Scott		Landers, Brian
	ACCUPERMIT	
	CENAB	
	Steelman, Brian	

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:00

CCDC arrived on site and began recovery of suspect AUES in grid -10-90 and then 3 grab samples. After area was sampled and CCDC left the site we backfilled the sampling area of -10-90 so as not to accumulate standing water. Bottle recovered at 07:05 AM, 07:26 AM all samples complete, 07:55 AM CCDC clear of downrange.

End of day: 12:00

SAMPLES COLLECTED: 3 grab samples taken: one where item was, one 1 foot below where it was and sample

Closed cavity items found Suspect AUES bottle recovered, reported to be closed by a stopper

New Equipment on Site: N/A

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

[illegible]

(22)

7-26-19

0600 Safety Brief E.C.B. on Site Setting up  
Gear & EPDS.

0615 Sample team Dressing out.

0623 Sample team Down Range pulling back mitigation  
plastic.

0630 Sample team looking for the Bottle.

0645 Sample team still looking for the Bottle.  
they are struggling w/ mitigation plastic.

0705 Team Found the Bottle & are packaging.

0716 Sample 1 collected.

0719 Sample 2 collected.

0726 Sample 3 collected.

0730 Team Processing thru EPDS.

0735 Team Picking up equipment.

0755 E.C.B. is off site. Parsons team Preparing  
to Backfill excavation area.

1200 Day Complete.

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 29 July 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 Sunny and hot, mid 90's

**Personnel on Site**

PARSONS	ZES		
Bryant, Joe			
Courtney, Kenneth	Wright, David		
	Yorkshire, Bart		
Matter, Phillip			
Oien, Joshua			
Rider, Matthew	ACCUPERMIT		
Wunschel, Scott	Marin, Naum		
	Williams, Angelo		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive operations today. Finished backfilling -10-90. 41 drums dumped and cut. Cut grass on 4825.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site: N/A

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

(23)

7-29-77

0630 Morning Briefing

0645 Team is working at the Federal property Site


0700 Working w/ Matt Rider, getting him trained up  
to take over the Safety/Env. Job.0830 Team working at 4825 adding backfill soil  
to grid -10/-90.1000 Team back working at the Federal property  
Site.

1230 Lunch

1425 Checking on the Team.

1630 End of day Clean up.

1700 Day Complete.







(24)

7-30-77

0630 Morning Safety Brief

0645 Team Preparing for Soil Shipments to  
Sub-lake ID landfill.

0730 Continuing to work w/ Matt Rider on  
Safety training.

1110 Checked on the team.

1230 Lunch.

1400 End of day clean up.

1700 Day Complete.

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 31 July 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 Sunny and hot mid 90's, PM thunderstorms.

Personnel on Site

PARSONS	ZES		
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Jedidiah	Yorkshire, Bart		
Matter, Phillip			
Oien, Joshua			
	ACCUPERMIT		
Wunschel, Scott	Marin, Naum		
	Williams, Angelo		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive operations today. Cut weeds off of 4825/4801 fenceline. Replaced concrete barrier in parking lot per Brian Steelman's request. Swept excess dirt off of construction mats.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site: N/A

Visitors


Contractors

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

(25) 7-31-19

0630 Morning Briefing

0730 Team is cleaning construction mats and moving tools to the Federal property site for storage.

1200 Lunch.

1445 Checking on the team at the Federal property site.

1630 End of day clean up.

1700 Day Complete.

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 1 August 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 partly cloudy, scattered rain. Lo 90's

**Personnel on Site**

PARSONS	ZES		
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Jedidiah	Yorkshire, Bart		
Matter, Phillip			
Oien, Joshua			
	<b>ACCUPERMIT</b>		
Wunschel, Scott	Marin, Naum		
	Williams, Angelo		
	<b>CENAB</b>		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive operations today. Pumped out rain drum from 4835 roof, 150 gallons removed. 18 drums dumped and cut. Dumped 3 rolloffs.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

(26)

8-1-19

0630 Morning Meeting

0645 Team working at the Federal property site,  
dumping Roll of Boxes & cutting Soil drums.

1015 Checked on team, all ok

1200 Lunch

1500 Checked on team at the Fed prop site.

1630 End of day clean up

1700 Day Complete.

~~Set up~~





(27)

8-5-19

0630 Morning Meeting

0640 Team prepping to work at the Federal Property Site, they are organizing the barrel yard.


0900 Working w/ Matt Pider on Inventory.

1045 Checked on the team, all ok.

1230 Lunch

1630 End of day Clean up.

1700 Day Complete.

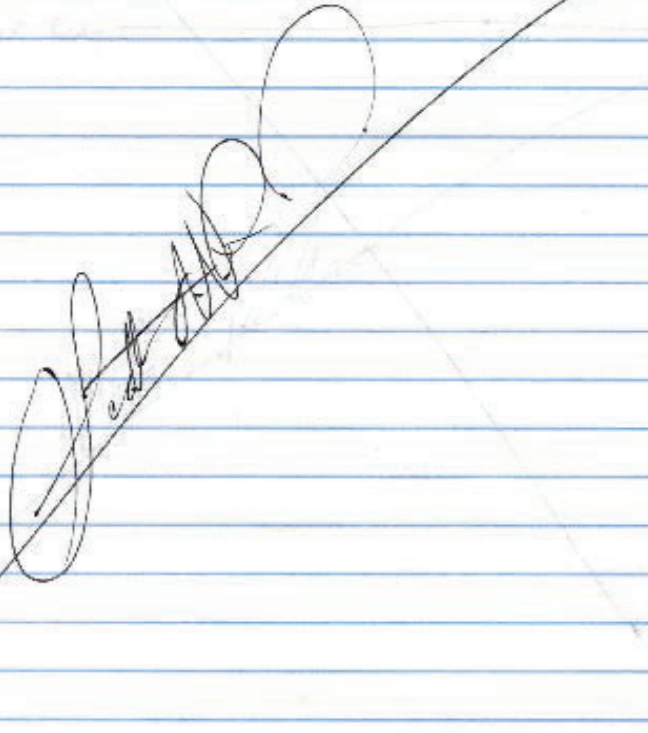



(28)

06 August 2019

0630 Morning Safety Brief

0640 Team went to Federal Property to Dump drums  
And Assist loading Sub title D Trucks

0700 Continued Safety Training And QC training with Scott

1030 Went to Fed Prop to check on Team, Everyone okay

1230 LUNCH BREAK

1300 Returned to work

1445 Went to Fed Prop to check on Team, Everyone okay

1630 Team Returned for End of Day Brief And Clean up

1700 END OF DAY

A large, stylized handwritten signature in black ink, slanted upwards from left to right, spanning across the lower half of the page.



(29)

07 August 2019

- 0630 Morning Safety Brief
- 0645 Team downstairs getting ready to ship out Drums  
And Roll OFF, Also prepping for possible thunderstorm  
Activity with erosion control measures
- 0753 Zimmer Arrives to remove Roll OFF 291439
- 0800 Roll OFF 291439, Drums SCR 604, PPE 472, 672 AQ  
Removed And shipped to Federal Property
- 0820 Team Finishes Erosion Control measures And lock up  
man gate And vehicle gate
- 0830 Team departs for Fed Prop to cut Drums And crush pallets
- 1200 Lunch Break
- 1230 Returned to work
- 1445 Checked on Team At Fed Prop, Everyone OK
- 1630 Team Returned from Fed Prop for End of Day Brief  
And clean up
- 1700 End of Day

A large handwritten signature, possibly "P. L. H.", is written across the bottom of the page. To the left of the signature are several vertical scribbles. A long horizontal line is drawn across the page, starting from the left margin and ending under the signature.



## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 8 August 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 mostly sunny to 90's, winds 5-10 mph

Personnel on Site

PARSONS	ZES		
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Jedidiah	Yorkshire, Bart		
Matter, Phillip			
Oien, Joshua			
Rider, Matt			
	<b>ACCUPERMIT</b>		
	Marin, Naum		
	Williams, Angelo		
	<b>CENAB</b>		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive operations today. Attempted to clean camera lens on IHF but cannot reach them. Measured side stairs on trailers at Fed Prop as they are in need of replacement, went to lumber yard to pick up required lumber for repairs.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site: N/A

Visitors


Contractors

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:


Activities anticipated for tomorrow:

<u>Attachments</u> (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



08 August 2019

(30)

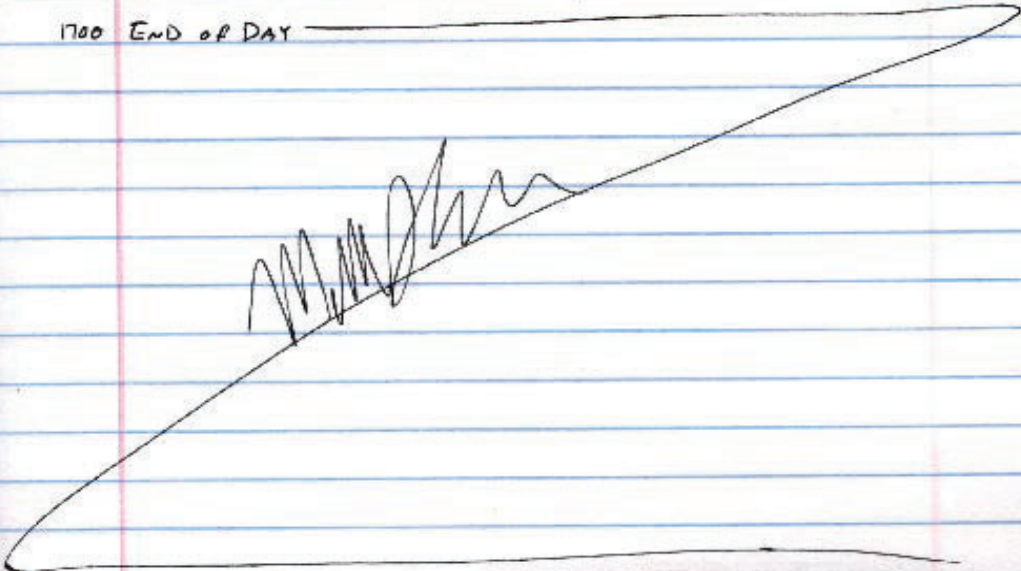- 0630 Morning Safety Brief; Reviewed AHA-15, Heavy Equipment  
And related Safety. HI 91° winds 5-10mph w/w  
Sunny/Partly Sunny
- 0640 Team departed to Fed prop to weigh drums
- 0700 worked to get set up to VPN And set up printers  
And scanners to my computer
- 1045 Went to Fed prop to check on Team. Everyone okay  
Proper PPE being worn
- 1230 Lunch Break
- 1300 Returned to work
- 1400 Checked on Team at Fed Prop, Everyone Okay
- 1530 Team Returned for End of week Briefing, Weekly  
clean up And Vehicle Maintenance
- 1700 END OF DAY
- 

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 12 August 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 mostly clear temps mid 80's.

Personnel on Site

PARSONS	ZES		
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Jedidiah	Yorkshire, Bart		
Matter, Phillip			
Oien, Joshua			
Rider, Matt			
	ACCUPERMIT		
	Williams, Donald		
	Williams, Angelo		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive operations today. Removed large hornets nest from stack of aluminum sheeting. Removed large weeds off of magazines. Removed temporary barrel yard fencing. Begin repair of Fed Prop trailer side door stairs and landing (nearest Sibley). Zimmer rebuilt subtitle D soil loadout area.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site: N/A

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:


Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

12 August 2019

(31)

- 0630 Morning Safety Brief; HI 91° Sunny winds S-10mph  
0640 Team headed to Fed prop to weigh drums, terminate  
Hornets nests, replace back porch on trailers And  
clean cameras for security guards  
0715 Went to Fed prop to assist/observe the destructions  
of large hornets nest built on the Shoring.  
0800 Installed new printer And Submitted PAM request  
to Install Drivers  
1100 Went to Fed Prop to check on Team, Everyone okay  
1230 Lunch Break  
1300 Returned to work  
1430 Went to Fed prop to check on Team, Everyone okay  
1630 Team Returned for End of Day Brief And clean up  
1700 End of Day
- 

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 13 August 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 Cloudy high 88, showers in afternoon.

**Personnel on Site**

PARSONS	ZES		
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Jedidiah	Yorkshire, Bart		
Matter, Phillip			
Oien, Joshua			
Rider, Matt			
	<b>ACCUPERMIT</b>		
	Williams, Donald		
	Williams, Angelo		
	<b>CENAB</b>		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive operations today. Cleaned up down range, stacked sandbags, swept off construction mats. Repaired erosion fence behind dress out trailer. Pulled down camera system on IHF in attempt to clean lenses, lenses were too weathered to clean placed new housings on order. 68 drums weighed. Sent crew home at 12:30 due to constant rain.

End of day: 12:30

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

13 August 2019  
Spring Valley, DC  
Matthew Rider, Safety

(32)

- 0630 Morning Safety Brief. HI 88° wind 5-10mph cloudy  
Thunderstorms likely At noon, Strong Storms At 1400
- 0645 Team downstairs to start general Housekeeping clean  
up to prepare for storms. Setting up any Erosion  
control measures that are necessary
- 0900 Team went to Fed Prop to weigh Drums
- 1045 went to Fed Prop to check on Team
- 1145 Lunch Break
- 1215 Returned to work
- 1230 Team was Released Due to Thunder Storms And  
constant rain
- 1630 Started clean up And Shut Down
- 1700 End of Day



## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 14 August 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 Highs 90 degrees, winds 5-10 mph, isolated  
 thunderstorms late afternoon.

Personnel on Site

PARSONS	ZES		
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Jedidiah	Yorkshire, Bart		
Matter, Phillip			
Oien, Joshua			
Rider, Matt			
	ACCUPERMIT		
	Marin, Naum		
	Vargas, Brian		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No monitored intrusive operations today, we will dig out clean backfill to get original depths of excavation on some limited data areas. Removed ramp over grid 90-90 for surveyors. Davey Tree cut at Federal Property.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site: N/A

Visitors


Contractors

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:


Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



14 August 2019  
Spring Valley, DC  
Matthew Rider, Safety

(33)

- 0630 Morning Safety Brief - HI 89° winds - S-10mph w/w  
Thunderstorms possible Late Afternoon, High Humidity
- 0650 Team went to Fed Prop to gather Tools and equipment  
for moving Dirt Ramp And digging Holes for Survey to  
Shoot Depths
- 0740 DC water working on 4825 water line pump
- 0915 Went to Fed Prop to let Day in to cut the IMF.
- 1145 Went to Enterprise Rental to change out Vehicles  
due to Expired Tags
- 1230 Lunch Break
- 1300 Returned to work
- 1345 visited Team At Fed Prop, They were weighing drums  
And working to replace Deck/Stairs between the office  
Trailers
- 1630 Team returned to office for End of Day Brief And  
Clean up. Alerted me of multiple Wasp nests At End  
of Trailers At Fed prop
- 1700 END of Day
- 

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 19 August 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 Extremely hot and humid 98 degrees.

Personnel on Site

PARSONS	ZES		
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Jedidiah	Yorkshire, Bart		
Matter, Phillip			
Oien, Joshua			
Rider, Matt			
	ACCUPERMIT		
	Vargas, Gustavo		
	Vargas, Brian		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive operations today. Finished tracking in backfill on surveyed holes. Continue working on landing between the two trailer wings. Dumped 2 rolloffs. Excessive heat led to 15/45 work schedule, sent crew home at 13:30.

End of day: 13:30

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site: N/A

Visitors


Contractors

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

19 August 2019 - Monday  
Spring Valley, DC  
Matthew Rider, Safety

(35)

0630 Morning Safety Brief, Partly cloudy HI 97° wind 5-10mph  
Real Feel Low 100's UV Index 9

0640 Team assembled downstairs to go over plan to  
move equipment and track in the base dirt from  
the survey excavations

0915 Team completed work downstairs and headed to  
Fed prop to dump Roll Offs, weigh Drums and  
continue Replacing the Deck/Stair between the  
Trailers

0950 Wet bulb reading 88°, Team went to 75-25 work  
rest cycle

1021 Wet bulb reading was 93.2, Team went to 25-75 work  
rest cycle

1100 Went to Fed Prop to check on Team and bring them  
Gateade, Everyone OKAY

1200 Lunch Break

1230 Returned to work

1330 Team Released for the day due to high heat and  
work Restrictions

1630 End of Day clean up and shut down

1700 End of Day



**SPRING VALLEY, WASHINGTON DC**

**Contract No:** W912DY-09-D-0062  
**Delivery Order:** TO 0006  
**Date:** 20 August 2019  
**Site Location:** 4825 Glenbrook Road

**Weather:**  
 hot, humid mid 90's

**Personnel on Site**

<b>PARSONS</b>	<b>ZES</b>		
Bryant, Joe	Prate, Warren		
Courtney, Kenneth			
Marion, Jedidiah	Yorkshire, Bart		
Matter, Phillip			
Oien, Joshua			
Rider, Matt	<b>ACCUPERMIT</b>		
	Vargas, Gustavo		
	Vargas, Brian		
	<b>CENAB</b>		
	Steelman, Brian		

**ACTIVITIES CONDUCTED** (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive operations today. Dumped 2 rolloffs, weighed 33 drums and continued working on landing between trailer wings. Teams released at 14:00 due to excessive heat.

End of day: 14:00

**SAMPLES COLLECTED:** See DQCR for sample information

Closed cavity items found

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

**Problems encountered/resolutions:**

**Instructions given by government personnel:**

**Activities anticipated for tomorrow:**

<b>Attachments</b> (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	<i>To be included if investigation is using CSS protocols</i>
Dig Sheet	Y/N	<i>To be included at least once every week during intrusive investigation</i>
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	<i>To be included weekly during field activities</i>
Property Management Summary	Y/N	<i>Include complete property inventory once every month</i>
Photographs	Y/N	

20 August 2019, Tuesday  
Spring Valley, DC  
Matt Rider, \*Snaky

(36)

- 0630 Morning Safety Brief, HZ 93 wind 5-10mph Partly Sunny  
High Humidity, Possible T-storms in Afternoon
- 0645 Team went to Fed prop to Dump Roll-offs And continue  
work on the Deck/Stairs between Trailers And possible  
patch work on Trailers
- 0820 Wet bulb set up with Initial reading of 74°
- 0918 Wet bulb reading 87°
- 1030 Visited Team At Fed Prop, Everyone OK
- 1058 wet bulb 89.8 Team on 50 50 work cycle
- 1200 LUNCH BREAK
- 1230 Returned to work
- 1245 Visited Team At Fed Prop, Wet Bulb reading was 93  
Team on 25 75 work cycles
- 1250 Assisted Team in Eliminating wasps nest
- 1400 Team Released due to heat And work cycles
- 1630 End of Day Brief, Clean up
- 1700 End of Day

*[Handwritten signature]*

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 21 August 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 hot, humid mid 90's.

**Personnel on Site**

PARSONS	ZES		
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Jedidiah	Yorkshire, Bart		
Matter, Phillip			
Oien, Joshua			
Rider, Matt			
	<b>ACCUPERMIT</b>		
	Vargas, Gustavo		
	Vargas, Brian		
	<b>CENAB</b>		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive operations today. Pumped out 220 gallons of rainwater from 4835 holding tank. Collected and packed up sensors for calibration. Inventory and inspect Interspiro masks for shipment for annual inspection and testing.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



21 August 2019 Wednesday  
Spring Valley, DC  
Matthew Rider, Safety

(37)

- 0630 Morning Safety Brief, HI-93° wind 10-15mph High Humidity  
Possible T-storms in the Afternoon
- 0640 Team did a clean up of downstairs Area
- 0758 Flatbed Truck Arrived with 300gal Tank to empty 550gal  
Tank used to catch rain next to 4835 residence
- 0816 Pumping Complet, Truck departed to Fed site to empty  
Tank into Baker Tanks
- 0830 Team Departed to Fed Prop to Finish Completion of the new  
Stairs/Dock between the Trailers
- 1045 Went to Fed prop to check on the Team, Everyone OKay
- 1200 Lunch Break
- 1230 Returned to work
- 1240 Team began Total Inventory of SCBA gear to start  
Shipping it out for Certification
- 1500 went to Fed prop to check on the Team, Everyone  
was doing okay
- 1630 Team Returned to CP for End of Day Brief And clean up
- 1700 End of Day

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 22 August 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 Hot and humid 95 degrees.

**Personnel on Site**

PARSONS	ZES		
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
	Yorkshire, Bart		
Matter, Phillip			
Oien, Joshua			
Rider, Matt			
	<b>ACCUPERMIT</b>		
	Vargas, Gustavo		
	Vargas, Brian		
	<b>CENAB</b>		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive operations today. Setp up drums for Mondays HAZMAT shipment. Sudtitle D shipment , 3 truckloads.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

22 August 2019 Thursday  
Spring Valley, DC  
Matthew Rider, Site Safety

(38)

0630 Morning Safety Brief, HI-94° wind-5-10mph UV Index-8

Possible Thunder Storms this evening

0640 Team went to Federal Property to Assist in the  
Sub Title D Soil Shipments And help prep for the  
HAZMAT Shipment on Monday. To Also finish the  
Interspire Inventory for recertification shipment

1000 Went to Fed Prop to check on Team

1100 Conference Call Started

1110 Brenda And Army Partners Auditors Arrived for Site Visit

1137 Auditor Team Departed Site

1200 Lunch Break

1230 Returned to work

1400 Completed Weekly SH&E & QC Weekly Logs (Inspections,  
Zero discrepancies found)

1500 Visited Team At Fed prop, Everyone okay

1630 Team Returned for End of Day Brief And clean up &  
Vehicle maintenance

1700 End of Day

A handwritten signature in black ink, appearing to be 'Matthew Rider', is written over a large, hand-drawn diagonal line that spans across the bottom half of the page.

# SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 26 August 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 78 degrees, p. cloudy

## Personnel on Site

PARSONS	ZES		
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Jed	Yorkshire, Bart		
Matter, Phillip			
Rider, Matt	ACCUPERMIT		
	Vargas, Gustavo		
	Vargas, Brian		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive activities today. HAZMAT shipment of 3 box trucks with 173 drums total and 4 water tankers with approximately 20,000 gallons of water. Last day for Accupermit until they are needed again.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information  
 \_\_\_\_\_  
 \_\_\_\_\_  
 \_\_\_\_\_

Closed cavity items found

New Equipment on Site: N/A

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

26 August 2019 Monday  
Spring Valley, DC  
Matthew Rider, Safety

(39)

- 0630 Morning Safety Brief, HI-78 Wind S-10 E-6 UV Index-7  
cloudy / Partly cloudy
- 0640 Team went to Federal Property to Assist ZES in  
the HAZMAT shipping of Drums and water.
- 0830 First Truck (Soil Drums) Loaded and Departed Fed site
- 0837 First Tanker Truck for Baker Tank 259516 Filled and departs
- 0852 Second Tanker Truck for Baker Tank 259516 Filled and departs
- 0914 Third Tanker Truck for Baker Tank 259516 Filled and departs
- 0931 Second Soil Truck (Soil Drums) is fully loaded and departs
- 0949 Fourth Tanker Truck for Baker Tank 259516 Filled and departs
- 1053 Third Truck (Soil Drums) Arrives loaded and Departs.
- 1100 Clean up from HAZSHIPMENT
- 1200 Lunch Break
- 1230 Returned to work at Fed Prop
- 1300 Team preping Cont Area for clean up
- 1445 Visited Team At Fed Prop, Everyone okay
- 1630 Team Returned for End of Day Brief And clean up
- 1700 End of DAY

*[Handwritten signature]*

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 27 August 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 high 78 degrees, overcast chance of rain

Personnel on Site

PARSONS	ZES		
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Jed	Yorkshire, Bart		
Matter, Phillip			
Oien, Joshua			
Rider, Matt	ACCUPERMIT		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive activities today. Clean up near connex area. Continued work on soffit on trailer. Shipped off Interspiro masks, regualtors and tanks for recertification. Begin cleaning Baker tank that was emptied in last HAZMAT shipment.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site: N/A

Visitors


Contractors

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:


Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



27 August 2019, ~~Wednesday~~<sup>THU</sup> Tuesday,  
Spring Valley, DC  
Matthew Rider, Site Safety

(40)

- 0630 Morning Safety Brief HI-78 WIND-510 ENE Humidity 75%  
Cloudy possible Rain Showers
- 0645 Team went to Fed Prop to Clean Area between  
Gray Conex and Dumpster
- 0800 Clean up complete, Bruce and Jed started doing  
Repair work on Trailer at Fed Prop, Josh began Organizing  
Interspire MASKS and TANKS for Re-cert Shipping
- 1045 Went to Fed Prop to check on the Team and  
Zimmer personnel cleaning out the Baker Tank
- 1200 Lunch BREAK
- 1230 Returned to work
- 1305 Went to Fed Prop to Escort Dary in the IHF to cut  
the grass and Trim Fence Line
- 1335 Moving Forward Meeting with Sean, Phil, Josh, Doug and Bart  
About what will be coming up in the work scope
- 1500 Went to check on Team at Fed Prop, Everyone OKAY
- 1630 Team Returned for End of Day Brief and Clean up
- 1700 End of Day
- 

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 28 August 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 high 84 degrees, scattered showers

Personnel on Site

PARSONS	ZES		
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Jed	Yorkshire, Bart		
Matter, Phillip			
Oien, Joshua			
Rider, Matt	ACCUPERMIT		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive activities today. Continue working on soffit at Federal property. Measured elevations near/around area 4. Begin cleaning emptied Baker tank.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site: N/A

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

28 August 2019, Wednesday  
Spring Valley, DC  
Matthew Ridar, Safety

(41)

- 0630 Morning Safety Brief, H2-84 wind 5-10 GGS Humidity 75%  
Scattered T-storm Possible in Afternoon
- 0640 Team went to Fed prop to continue work on the Trailers
- 0800 Josh went downstairs to shoot Elevations to get  
depths for restoration mapping
- 1100 went to Fed Prop to check on Team And Zimmer  
Personnel cleaning out the Baker Tank
- 1130 SED + Bruce went to Home Depot to get Supplies for  
Fixing Trailers
- 1200 Lunch Break
- 1230 Returned to work
- 1400 Checked on Team at Fed Prop
- 1530 Conference Call
- 1630 Team Returned to Site for End of Day Brief and Clean up
- 1700 END OF DAY

*[Handwritten signature]*

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 29 August 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 high 82 degrees, sunny

**Personnel on Site**

PARSONS	ZES		
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Jed	Yorkshire, Bart		
Matter, Phillip			
Oien, Joshua			
Rider, Matt	ACCUPERMIT		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive activities today. Pumped 200 gallons of water out of 4835 roof catch tank. Finished work on soffit. Erosion control supply inventory in preparation for restoration activities.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:


Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

29 August 2019, Thursday  
Spring Valley, DC  
Matthew Rider, Safety

(42)

- 0630 Morning Safety Brief, HI 82, wind - S to NW Humidity 60%  
Mostly Sunny UV-Index 8
- 0640 Bruce & JED went to Fed Prop to continue working on  
the Trailers
- 0745 Josh went downstairs to assist Zimmer with pumping  
Rain water out of Holding Tank that catches clean  
Roof water Run off
- 0830 Josh went to Fed prop to complete an Erosion Control  
Inventory while JED & Bruce continued working on  
Trailers
- 1100 Conference Call
- 1130 checked on Team At Fed Prop
- 1200 Lunch Break
- 1230 Returned to work
- 1445 went to Fed Prop to check on Team, Everyone OKAY
- 1615 Team Returned to Site for End of WGER brief, Clean up  
And vehicle And Tool maintenance
- 1700 End of Day
- 

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 3 September 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 87 degrees, mostly sunny

**Personnel on Site**

PARSONS	ZES		
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Jed	Yorkshire, Bart		
Matter, Phillip			
Oien, Joshua			
Rider, Matt	ACCUPERMIT		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Fixed Fed Prop security camera lenses, we replaced them. CP Johnson on site collecting a bunch of post excavation elevation shots. Smashed up 47 pallets for disposal.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



03 September 2019, TUESDAY  
Spring Valley, DC  
Matthew Riden, Site Safety

(43)

- 0630 Morning Safety Brief, HI - 87° wind - 5-10 mph ENE  
80% Humidity, Partly Cloudy with ~~light variable~~<sup>mtg</sup> light variable  
winds
- 0640 Bruce began doing yard maintenance around 4825 with  
Electric weed cutter, JED was assisting the Surveyor in  
Shooting Elevation shots around 4825 to coincide with  
the Backfilling/restoration duties.
- 0815 work complete on the site, Team went to Fed Prop to  
Replace the camera cases on the property And  
Prep a UPS shipment, crush Pallets And Prep for  
HAZ Shipment
- 1100 Went to Fed prop to visit Team, Everyone okay
- 1200 Lunch Break
- 1230 Returned To work
- 1430 UPS Arrived to Ship out Pallets
- 1630 Team Returned to site for END of Day Brief  
And Clean up.
- 1700 END of Day

Matthew Riden

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 4 September 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 88 degrees, partly cloudy

**Personnel on Site**

PARSONS	ZES		
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Jed	Yorkshire, Bart		
Matter, Phillip			
Oien, Joshua			
Rider, Matt	ACCUPERMIT		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive activities today. Dumped 2 rollofs and recovered and relabeled both hazardous rollofs.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information  
 \_\_\_\_\_  
 \_\_\_\_\_  
 \_\_\_\_\_

Closed cavity items found

New Equipment on Site: N/A

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

04 September 2019, Wednesday  
Spring Valley, DC  
Matthew Rider, Safety

(214)

- 0630 Morning Safety Brief, Partly cloudy, Possible stray  
Thunderstorm in the Afternoon, H<sub>2</sub> 93 wind-10-15mph SW  
Humidity 60% UV Index- 8
- 0640 Team went to Fed prop to Dump Roll OFFs And  
Continuing to Replace the Camera Housing units for the  
Federal property camera System
- 1030 went to Fed prop to check on Team And ensure they  
Are staying hydrated, Everyone okay
- 1200 LUNCH BREAK
- 1230 Returned to work, Team Continued to work on the  
Camera Housing units And continue Prep for HAZ shipment  
on Monday And Dump Roll offs
- 1445 Checked on Team At Fed Prop, Everyone okay  
- Construction Has Fletcher Gate Closed Along with  
Rockwood Road
- 1630 Team Returned for End of Day Brief And clean up
- 1700 END OF DAY

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 5 September 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 79 degrees, cloudy. Winds 10-15 mph

Personnel on Site

PARSONS	ZES		
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Jed	Yorkshire, Bart		
Matter, Phillip			
Oien, Joshua			
Rider, Matt	ACCUPERMIT		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive operations today. Dumped 2 rollofs of subtitle D soil. Cut up a locust tree that fell on Fed Prop fence. Repaired silt fence around the clean backfill and subtitle D soil piles. Painted and repaired the trailer ceiling at Fed Prop, there were numerous water stains and loose boards.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site: N/A

Visitors


Contractors

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

05 September 2019, Thursday  
Spring Valley, DC  
Matthew Rider, Safety

(45)

- 0630 Morning Safety Brief, Cloudy mostly cloudy, HI 77  
Humidity 60% wind S-10EWS, 20% chance of Rain
- 0645 Team went to Fed Prop to Dump Roll offs and cut  
up Fallen Tree
- 1000 went to Fed Prop to check on Team, Everyone okay, All  
Proper PPE being worn for Tree cutting
- 1100 RD/RA WEEKLY Conference Call
- 1200 LUNCH BREAK
- 1230 Returned to work
- 1300 Team continued to Dump Roll offs and Start to Inspect  
Clean Back Fill pile for Brush Removal
- 1500 went to Fed Prop to check on Team, Everyone OKAY
- 1615 Team Returned for End of week brief, clean up and  
vehicle maintenance
- 1700 End of Day

f

*[Handwritten signature]*



## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 9 September 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 83 degrees, mostly cloudy

Personnel on Site

PARSONS	ZES		
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Jed	Yorkshire, Bart		
Matter, Phillip			
Oien, Joshua			
Rider, Matt	ACCUPERMIT		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive activities today. HAZMAT shipment; 165 drums, and approximately 20,000 gallons of water shipped to treatment facility. Locksmith drilled out lock cylinder on IHF guard shack.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information  
 \_\_\_\_\_  
 \_\_\_\_\_  
 \_\_\_\_\_

Closed cavity items found

New Equipment on Site: N/A

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



09 September 2019, Monday  
Spring Valley, DC  
Matthew Rider, Safety

(46)

- 0630 Morning Safety Brief, HI 83 Humidity 60% Wind S-10 ENE  
Possible stray T-storm in Afternoon, Cloudy to mostly cloudy
- 0640 Team went to Fed Prep to Prepare to the HAZ Shipment
- 0930 Team begins to Load out Trucks for HAZSHIPMENT  
Total of 7 Trucks, 3 Soil/Drum Trucks And 4 water  
Trucks for BAKER TANK # 251613
- 1030 Went to Fed Prep to check on Team And operation, Everyone  
OKAY, All personnel wearing Appropriate PPE
- 1130 Last Truck loaded And Departed site
- 1200 Lunch Break
- 1230 Returned to work
- 1300 Began Testing Monitors And charging them to ensure functionality
- 1330 Mailed in SUMA canister
- 1430 checked on Team At Fed prep, Everyone okay
- 1630 Team Returned to site for End of Day Brief And  
Clean up
- 1700 END of Day

*Matthew Rider*

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 10 September 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 high 88 degrees, mostly sunny.

**Personnel on Site**

PARSONS	ZES		
Bryant, Joe	Prate, Warren		
	Wright, David		
Marion, Jed	Yorkshire, Bart		
Matter, Phillip			
Oien, Joshua			
Rider, Matt	ACCUPERMIT		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive activities today. Begin calibrating HCN monitors. Start cleaning newly emptied Baker tank. Set up barrel yard for next shipment. Packed up Minelab for shipment.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

10 September 2019, Tuesday  
Spring Valley, DC  
Matthew Rider, Safety

(47)

- 0630 Morning Safety Brief, HI 88 Humidity 60% UV-7 Wind - S-10 SSE  
Sunny - Partly cloudy Stay T-storm possible Afternoon
- 0840 Team went to Fed Prep to prep for the next HAZ Shipman  
And wash out Baker Tank 251613. Also to gather Tools  
for Turn in And Calibrate HCN monitors
- 1030 Davy Arrived At Fed Prep. Went to Sign them in And  
open up the IHF for them to cut
- 1200 Lunch Break
- 1230 Resume work
- 1245 Davy Departed Fed Prep
- 1400 Team Released, End of Day Brief
- 1630 Began clean up
- 1700 END of DAY

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 11 September 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 high 94 degrees, sunny, winds 7mph

Personnel on Site

PARSONS	ZES		
Bryant, Joe	Prate, Warren		
Courtney, Kenneth			
Marion, Jed	Yorkshire, Bart		
Matter, Phillip			
Oien, Joshua			
Rider, Matt	ACCUPERMIT		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive activities today. 3 subtitle D truck loads of soil sent to landfill. Cleaned out IHF guard shack, continued cleaning of empty Baker tank, and cleaning out quonset hut.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site: N/A

Visitors


Contractors

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

11 September 2019, Wednesday  
Spring Valley, DC  
Matthew Rider, Safety

(48)

0630 Morning Safety Brief, HI 94 - Humidity 60% - Wind S-10 SSW  
Sunny to Partly Cloudy

0640 Team went to Federal Property to Assist with the  
Sub Title 3 Shipment (5 Trucks). Clean out old guard shack  
Organize And Clean Hut And Finish cleaning the Baker Tank

1100 Went to Fed prop to check on the Team, Everyone okay

1200 Lunch Break

1230 Returned to work

1430 Went to Fed Prop to check on Team, Everyone okay

1630 Team Returned to Site for End of Day Brief And  
Clean up

Matthew Rider

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 12 September 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 95 degrees, winds 10-15mph, possible  
 thunderstorms in afternoon.

Personnel on Site

PARSONS	ZES		
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, Dave		
Marion, Jed	Yorkshire, Bart		
Matter, Phillip			
Oien, Joshua			
Rider, Matt	ACCUPERMIT		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive activities today. Sampled Baker tank # 257767, Completed calibration of HCN monitors.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site: N/A

Visitors


Contractors

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:


Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



12 September 2019, Thursday  
Spring Valley, DC  
Matthew Rider, Safety

(49)

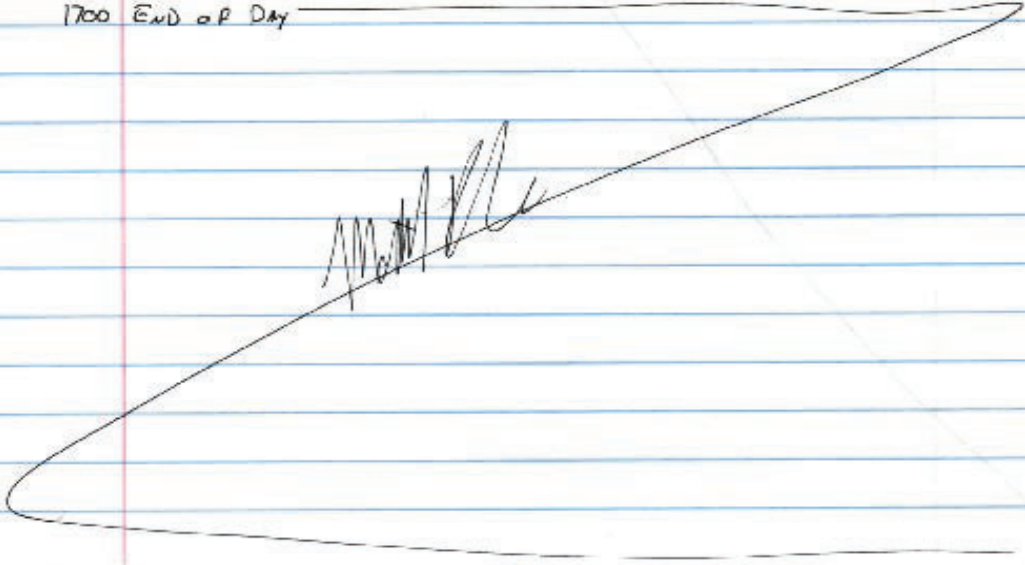- 0630 Morning Safety Brief, H<sub>2</sub> 93 Humidity 60% wind 10-15 SW  
Mostly to partly sunny, possible T-storm
- 0640 Team went to Fed Prep to Sample Baker Tank And  
do a Drum count for next HAZ Shipment
- 0730 Joe began the recalibration of the HCN monitors
- 1030 Went to Fed prep to check on Team And Make Sure they  
were staying hydrated
- 1200 Lunch Break
- 1230 Returned to work
- 1245 Team Returned to Site for Vehicle Inspections, Clean up  
And End of Week Brief
- 1300 Team Released due to Heat
- 1600 Completed Back Log of Receipts
- 1700 End of Day
- 

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 16 September 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 91 degrees, winds 5-10 mph

Personnel on Site

PARSONS	ZES		
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, Dave		
	Yorkshire, Bart		
Matter, Phillip			
Oien, Joshua			
Rider, Matt	ACCUPERMIT		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive operations today. Calibrated HCN monitors. Inventoried supplies in Fed Prop office and assembled reaining SCBA gear.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site: N/A

Visitors


Contractors

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:


Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

16 September 2019, Monday  
Spring Valley, DC  
Matthew Ridwan, Safety

(50)

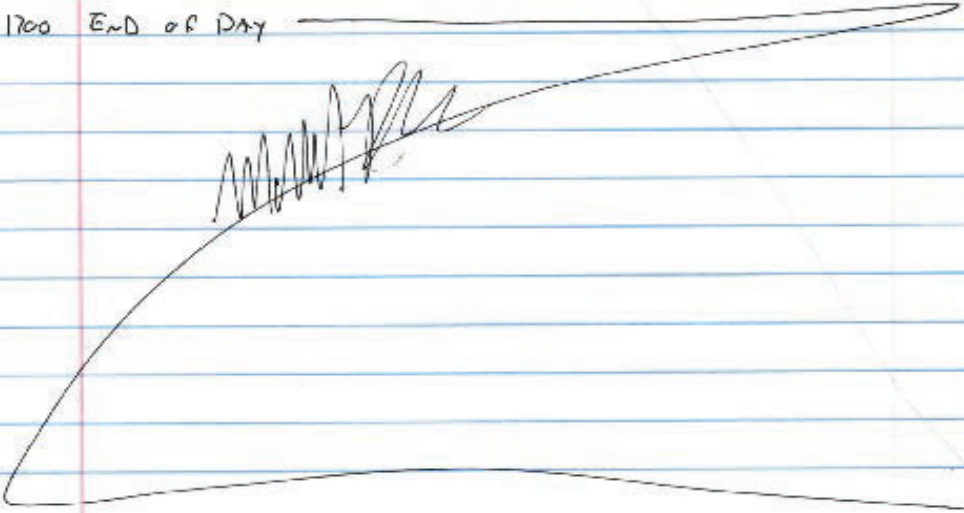- 0630 Morning Safety Brief, HI 91, Humidity 50% wind 5-10mph SW  
Sunny to Mostly Sunny, 20% chance T-storms Afternoon (JED OUT)
- 0645 Sat Down with Team to go over Inventory procedures And  
what and where to start. Starting in office 3 at Fed  
Prop Doing SCBA and M40 Equipment
- 1000 Went to Fed Prop to check on Team, Everyone  
is doing okay
- 1200 Lunch Break
- 1230 Returned to work
- 1330 Team Finished Item Inventory in office 3, moving onto  
the Cones for Inventory
- 1445 Went to Fed Prop to check on Team, Everyone okay
- 1630 Team Returned to Site for End of Day Brief And  
Clean up
- 1700 END OF DAY
- 

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 17 September 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 79 degrees, winds 10-15 mph

Personnel on Site

PARSONS	ZES		
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, Dave		
	Yorkshire, Bart		
Matter, Phillip			
Oien, Joshua			
Rider, Matt	ACCUPERMIT		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive operations today. Inventory of tools, stairs, shoring and Porta-Sens monitors. Broken AC at Fed Prop called in and repaired. Met with Zimmer management to discuss Proctor digging.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site: N/A

Visitors


Contractors

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

17 September 2019, Tuesday  
Spring Valley, DC  
Matthew Rider, Safety

(51)

- 0630 Morning Safety Brief, HI-78 wind 10-15 ENE Mostly  
Sunny to Partly Cloudy (JED, DAVE OUT)
- 0640 Team Went to Fed prep to continue with the  
Equipment Inventory
- 1030 Went to Fed Prep to check on the Team,  
Everyone okay
- 1200 Lunch Break
- 1230 Returned to work
- 1300 Team Completed Inventory of Camp Items, moved to  
Site to continue Inventory.
- 1630 Team Started Clean up, End of Day Brief
- 1700 End of Day

Matthew Rider

# SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 18 September 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 78 degrees, winds 5-10 mph

## Personnel on Site

PARSONS	ZES		
Bryant, Joe	Prate, Warren		
Courtney, Kenneth			
	Yorkshire, Bart		
Matter, Phillip			
Oien, Joshua			
Rider, Matt	ACCUPERMIT		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No monitored intrusive digging today, but did dig 6 proctor sample from clean backfill areas. Collected soil in clean bucket liners for pickup. All holes were backfilled after samples were taken.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site: N/A

### Visitors


### Contractors

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



18 September 2019, Wednesday  
Spring Valley, DC  
Matthew Rider, Safety

(52)

- 0630 Morning Safety Brief, HI-76° Humidity 55%  
Wind 5-10mph ENE Mostly Sunny / Partly Cloudy (JED, Dave out)
- 0635 Reviewed Lesson Learned About Excavation Cave In on  
Different Parsons Site
- 0640 Team gathered 5gal bucket liners to Take down range  
for the Collection of Proctor Samples, Radio checks Complete
- 0700 Team conducts <sup>Task</sup> Job specific Safety Brief before beginning  
Operations
- 0755 Team Starts Area B2 Hole B for Proctor Samples
- 0808 Team Completes Proctor Sample Gather Hole B Area B2
- 0822 Area B2 Hole B backfilled And Complete
- 0827 Area B2 Hole A Started for Proctor Sample
- 0845 Area B2 Hole A Proctor Sample Completed
- 0854 Area B2 Hole A Backfilled And Completed
- 0920 Area B1 Hole B Started for Proctor Sample
- 0931 Area B1 Hole B Proctor Sample Complete
- 0935 Area B1 Hole B Backfilled And Completed
- 0942 Area B1 Hole A Started for Proctor Sample
- 0948 Area B1 Hole A Proctor Sample Completed
- 0955 Area B1 Hole A Backfilled And Completed
- 1000 Area B3 Hole A Started for Proctor Sample
- 1010 Area B3 Hole A Proctor Sample Completed
- 1015 Area B3 Hole A Backfilled And Completed
- 1017 Area B3 Hole B Started for Proctor Sample
- 1025 Area B3 Hole B Proctor Sample Completed

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 19 September 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 75 degrees, winds 5-10 mph, mostly sunny

**Personnel on Site**

PARSONS	ZES		
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, Dave		
	Yorkshire, Bart		
Matter, Phillip			
Rider, Matt	ACCUPERMIT		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive digging today. Maintenance on heavy equipment. Gathered up equipment for inventory.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

19 September 2019, Thursday  
Spring Valley, DC  
Matthew Rider, Safety

(54)

- 0630 Morning Safety Brief - H<sub>2</sub> 75 wind - S-10 ENE Humidity 45%  
Sunny / Mostly Sunny (JED, JOSH OUT)
- 0650 Team unlocked bottom gate and Assisted Zimmer with  
Fueling and greasing machines
- 1130 Lunch Break
- 1200 Continued Gathering Items for Inventory
- 1200 Returned to work
- 1300 Continued Inventory work
- 1600 Vehicle Maintenance
- 1630 End of work hour
- 1700 End of Day

*Matthew Rider*

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 23 September 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 93 degrees, hot and humid, mostly sunny

Personnel on Site

PARSONS	ZES		
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, Dave		
Marion, Jed	Yorkshire, Bart		
Matter, Phillip			
Oien, Josh			
Rider, Matt	ACCUPERMIT		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive digging today. Turned on water supply to AU ball field. Moved construction mats in preparation for compaction next week. Shipped out arsenic monitors. Organized fence panels and shoring panels.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site: N/A

Visitors


Contractors

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

23 September 2019, Monday  
Spring Valley, DC  
Matthew Ridar, Safety

(55)

0630 Morning Safety Brief, HI 93; wind 10-15 mph SW, Humidity 50%.  
Mix of Sunny And Cloudy

0640 Team went downstairs to begin moving ALL construction pads  
out of the way for preparation of digging And  
Compacting

1200 Lunch Break


1230 Returned to work

1240 Shipped out HCX monitors And went to Home depot  
for a Supply Run

1430 Boxed up the BM-25 monitors for shipment

1630 End of Day Brief And Clean up

1700 End of Day

A handwritten signature in black ink, appearing to read 'Matthew Ridar', is written over a large, hand-drawn loop that spans across the bottom half of the page.

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 24 September 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 81 degrees, winds 10-15 mph, mostly sunny

Personnel on Site

PARSONS	ZES		
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, Dave		
Marion, Jed	Yorkshire, Bart		
Matter, Phillip			
Oien, Josh			
Rider, Matt	ACCUPERMIT		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive digging today. Cut the grass at 4825. Organized drums for Hazardous shipment (marked with red paint).

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site: N/A

Visitors


Contractors

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:


Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



24 September 2019, Tuesday  
Spring Valley, DC  
Matthew Ruler, Safety

(54)

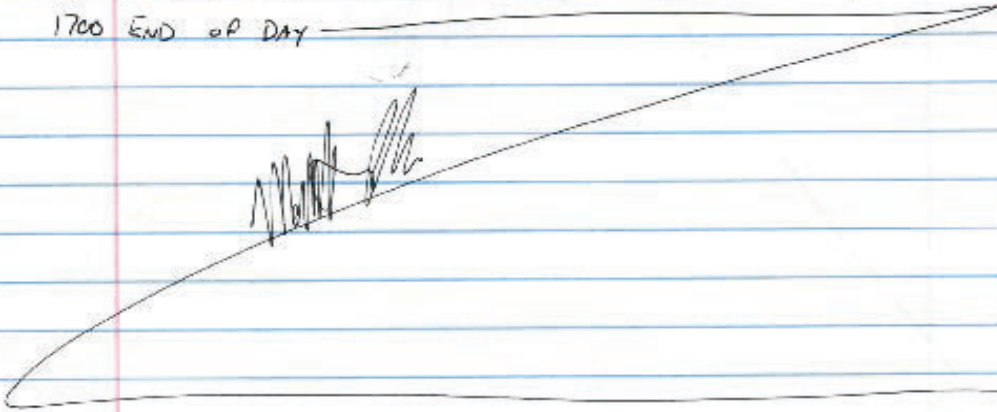- 0630 Morning Safety Brief. HI 85 wind 10-15 NW Humidity 45%  
Sunny to Mostly Sunny
- 0640 Team went to Fed prop to Consolidate Drums  
for next HAZ Shipment and to Consolidate  
Aluminum Shoring material into Organized piles
- 1030 Me and Josh went to Parsons HQ (Arlington) to  
pick up the updated copy of the Equipment  
inventory
- 1200 Lunch Break
- 1230 Returned to work
- 1240 Took Boxes to UPS (BM-2S) to have them packaged  
for Shipment. (order to Express must schedule pick up)
- 1300 Trimmed grass downstairs for general Housekeeping
- 1430 Reinforced monitor stands at Fed prop
- 1630 Team Returned for End of Day Brief and clean up
- 1700 END OF DAY
- 

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 25 September 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 82 degrees, winds 5-10 mph, mostly sunny

**Personnel on Site**

PARSONS	ZES		
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, Dave		
Marion, Jed	Yorkshire, Bart		
Matter, Phillip			
Oien, Josh			
Rider, Matt	ACCUPERMIT		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive excavation. Dumped and cut up 31 drums at the Federal Property. Shipped out BM 25 monitors for calibration.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

25 September 2019, Wednesday  
Spring Valley, DC  
Matthew Rider, Safety

(57)

- 0630 Morning Safety Brief, HI 83 wind S-10 SW Humidity 44%  
Mostly to Abundance of Sunshine
- 0640 Team went to Fed Prep to Dump and Cut Drums
- 0930 Joe and Jed went to Drop off (BM-2S) monitors at  
UPS Store
- 1045 went to Fed Prep to check on Team, Everyone OKAY
- 1200 Lunch Break
- 1230 Returned to work
- 1240 Team Returned to Fed Prep to continue cutting and  
carefully Dumping Drums
- 1430 Went to Fed Prep to check on Team, Everyone OKAY
- 1630 Team Returned to site for End of Day Brief and Cleanup
- 1700 End of Day

Matthew Rider

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 26 September 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 91 degrees, winds 5-10 mph, mostly sunny

**Personnel on Site**

PARSONS	ZES		
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, Dave		
Marion, Jed	Yorkshire, Bart		
Matter, Phillip			
Oien, Josh			
Rider, Matt	ACCUPERMIT		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive excavation. Collected water sample from Baker Tank #257767. Dumped and cut up 29 drums.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site: N/A

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:


Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

26 September 2019, Thursday  
Spring Valley, DC  
Matthew Rider, Safety

(58)

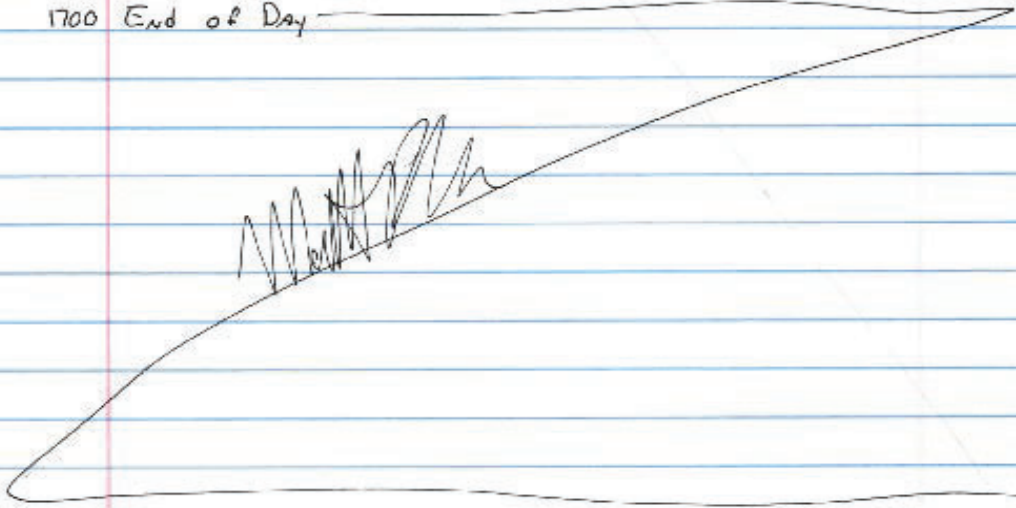- 0630 Morning Safety Brief, HI 88 wind-10-15mph NW Humidity 55%  
Sunny to Partly cloudy
- 0640 Team went to Fed Prop to continue Pumping/cutting Drums
- 0710 Joe Au SED went to Take water samples to send out  
with CCBC personnel
- 1030 CCBC Arrived on site. They were here to collect our  
water samples And to Take samples from the basement of  
4835 Au President's house
- 1200 Lunch Break
- 1230 Returned to work
- 1245 CCBC Done with Basement Samples And House is Sealed
- 1445 went to Fed Prop to check on Team. Everyone OK.
- 1600 Team Returned for Vehicle maintenance And clean up  
And End of week brief.
- 1700 End of Day
- 

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 30 September 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 74 degrees, winds 5-10 mph, overcast, light rain

Personnel on Site

PARSONS	ZES		
Bryant, Joe			
Courtney, Kenneth	Wright, Dave		
	Yorkshire, Bart		
Oien, Josh			
Rider, Matt	ACCUPERMIT		
	Williams, Donald		
	Amaya, Kevin		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Began excavating clean backfill to competent saprolite for final compaction activities. Dumped and cut up drums for subtitle d load out at the Federal Property.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site: Dozer, Roller

Visitors


Contractors

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



30 September 2019, Monday  
Spring Valley, DC  
Matthew Rider, Safety

(59)

- 0630 Morning Safety Brief, HI 74 Humidity 50% wind S-10 ESE  
Overcast with Rain Showers likely, chance of Rain 45%  
(JED OUT) (WARREN OUT)
- 0645 Radio checks
- 0700 Operations Brief covering the Safety And work being  
performed while Excavating, Compacting And backfilling  
Area
- 0800 Team Started digging
- 0902 Team Halted digging to get out of the Rain Storm
- 0953 Roller Arrived on site
- 1033 Dozer Arrived on site
- 1100 Team breaks for Lunch to let rain pass
- 1130 Team returns to work
- 1145 Digging done for the day due to rain, went to Fed  
prop to dump and cut drums
- 1330 Went to Fed Prop to check on the Team
- 1630 Team Returned to site to Secure downstairs And clean up  
And End of Day Brief
- 1700 End of Day

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 01 October 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 86 degrees, partly cloudy, winds 5-10 mph

**Personnel on Site**

PARSONS	ZES		
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, Dave		
	Yorkshire, Bart		
Oien, Josh			
Rider, Matt	ACCUPERMIT		
	Williams, Donald		
	Vargas, Gustavo		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Continued excavating clean backfill. Excavated first compaction area to competent saprolite. Backfilled first compaction lift.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site: Dozer, Roller

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:


Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

01 October 2019, Tuesday  
Spring Valley, DC  
Matthew Rider, Safety

(60)

- 0630 Morning Safety Brief, HI 86 Wind S-10S Humidity 65%  
Partly cloudy skies 0% chance of Rain  
(JED OUT)
- 0645 Radio checks
- 0650 Team checked Fire Extinguishers And First Aid Kits  
First Aid Kits need Replaced
- 0720 Team begins prep for excavating Soil for compaction
- 0750 Dust monitor Initial Reading 3.4/12.0
- 0800 Team begins digging operations
- 0850 Dust Monitor reading 19.9/15.4
- 0950 Dust Monitor reading 15.5/12.0
- 1050 Digging Completed Starting to compact Spills pile
- 1130 Lunch Break
- 1200 Returns to work
- 1205 Bruce goes to Home Depot for Roll of plastic for Spills
- 1300 Team begins to put first Lift Down in the Hole
- 1415 Compaction of Soil begins
- 1510 Compaction Complete
- 1520 Clean up started and prep begins for Troxler testing
- 1630 End of Day Brief And Clean up
- 1700 End of Day



## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 02 October 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 96 degrees, partly cloudy

**Personnel on Site**

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren	Haldane, Andrew	
Courtney, Kenneth	Wright, Dave		
Marion, Jed	Yorkshire, Bart		
Oien, Josh			
Rider, Matt	<b>ACCUPERMIT</b>		
	Williams, Donald		
	Marin, Naun		
	<b>CENAB</b>		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Backfilled and compacted 9 soil lifts. All 9 lifts reached at least 95% compaction.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information  
 \_\_\_\_\_  
 \_\_\_\_\_  
 \_\_\_\_\_

Closed cavity items found \_\_\_\_\_

New Equipment on Site: Dozer, Roller

Visitors	Contractors
_____	Berkel ( )
_____	DAVEY ( )
_____	ACCUPERMIT ( )
_____	ACI (0)
_____	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



02 OCTOBER 2019, Wednesday  
Spring Valley, DC  
Matthew Rider, Safety

(61)

- 0630 Morning Safety Brief, HI-96 wind S-10w Humidity 55%  
Partly cloudy / Record High Temps Today
- 0815 Radio checks Completed
- 0700 Team begins Prep for the Arrival of the Troxler
- 0750 Troxler Tester Arrives, Comes to CP to Sign in And for  
Site Specific Safety Brief
- 0811 Troxler Test of first Area of first Lift Complete - 99% Compaction
- 0822 Second Troxler Test of first Lift Complete - 98% Compaction  
(↑ will Be Referred To AS Lift Zero 01)
- 0825 Team begins Laying And Compaction of Lift 2 (Troxler Lift 1)
- 0858 Lift 2 is completed being laid (Troxler Lift 1)
- 0904 Troxler Testing of Lift 2 (Troxler Lift 2) Complete - 99.7% Compaction
- 0910 Team begins Laying And Compaction of Lift 3 (Troxler Lift 2)
- 0930 Dust Monitor Reading 21.1
- 0939 Troxler Testing of Lift 3 (Troxler Lift 2) Complete - 97.8% Compaction
- 0941 Team begins Laying And compaction of Lift 4 (Troxler 3)
- 1015 Troxler Testing of Lift 4 (Troxler Lift 3) Complete - 98% Compaction
- 1020 Team begins Laying Lift And Compaction Lift 5 (Troxler 4)
- 1057 Troxler Testing of Lift 5 (Troxler 4) Complete - 97% Compaction
- 1115 Lunch Break
- 1150 Returned to work
- 1200 Team begins Laying And compacting Lift 6 (Troxler 5)
- 1252 Troxler Testing of Lift 6 (Troxler 5) Complete. FAILED 92% Compaction
- 1254 Team begins to ReRoll Lift 6 (Troxler 5) to get Adequate Compaction
- 1305 Troxler Testing of Lift 6 (Troxler 5) Complete - 100% Compaction

## Page 2

PROJECT: Remedial Action @ Global JOB NO: 50200P

COUNTY: D.C.

STREET/LOT: 4815 Glenbrook Rd NW DC

DATE: 10/2/19 MS DS

GAUGE MODEL#: 3440


SERIAL#: \_\_\_\_\_

METHOD OF COMP: Shaggs Foot

MATERIAL: Soil

PRODUCER: on site

PLANT: Honey BW 1450

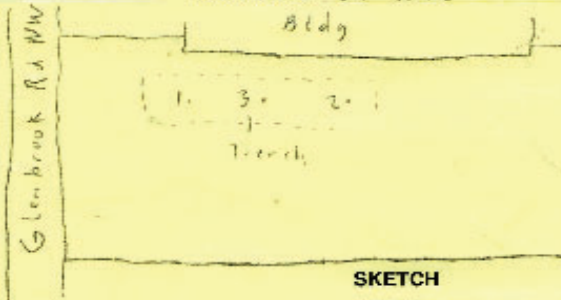

SKETCH

RETEST NUMBER	1	2	3	4	5	6	7	8	9	10
TEST NUMBER	1	2	3	4	5	6	7	8	9	10
STREET/LOT										
STATION	1	2	3	3	3	3	3	3	3	3
REFERENCE TO CENTERLINE										
ELEVATION	0	0	1	2	3	4	5	6	7	8
DEPTH OF LIFT	6"	6"	6"	6"	6"	6"	6"	6"	6"	6"
DEPTH SETTING	6"	6"	6"	6"	6"	6"	6"	6"	6"	6"
<b>DENSITY DETERMINATION</b>										
MOISTURE COUNTS	229	211	218	230	223	233	227	219	221	214
DENSITY COUNTS	1361	1440	1380	1411	1400	1450	1371	1454	1408	1472
(A) WET DENSITY pcf	130.4	127.9	128.8	128.7	129.1	137.5	133.5	127.1	128.9	126.8
(B) MOISTURE WT pcf	18.8	17.7	18.3	19.4	18.9	19.7	18.1	18.9	18.5	18.9
(C) DRY DENSITY pcf (A-B)	111.6	110.2	110.5	109.3	110.4	107.8	114.4	109.0	110.3	108.9
(D) PERCENT MOISTURE (B/C)	16.9	16.0	16.4	17.7	17.4	18.2	16.7	16.9	16.8	16.5
(E) MAXIMUM DRY DEN. pcf										
(F) OPT. MOISTURE CONT.										
(G) CORRECTED MAX DRY DEN	111.8	111.8	111.8	111.8	111.8	111.8	111.8			
(H) CORRECTED OPT. MOISTURE	15.3	15.3	15.3	15.3	15.3	15.3	15.3			
(I) % DENSITY (C/G X 100)	99.8	98.6	99.7	97.8	98.7	96.4	102.3	97.5	99.7	97.4
(J) % DENSITY REQUIRED										
PROCTOR CONTROL										
<b>PLUS 4 DETERMINATION</b>										
(A) WT TOTAL SAMPLE & PAN										
(B) WT OF PAN										
(C) WT OF TOTAL SAMPLE (A-B)										
(D) WT +4 MATERIAL (D-E)										
(E) WT OF PAN										
(F) WT OF -4 MATERIAL (D-E)										
(G) % OF -4 MATERIAL (F/C X 100)										

REMARKS: 11 tests on 10 lifts. All lifts passed at conclusion of day.

SIGNATURE: Andrew Tisdale



## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 03 October 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 81 degrees, mostly cloudy, winds 5-10 mph

**Personnel on Site**

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, Dave		
Marion, Jed	Yorkshire, Bart		
Oien, Josh			
Rider, Matt	<b>ACCUPERMIT</b>		
	Valle, Marvin		
	Marin, Naun		
	<b>CENAB</b>		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Backfilled and compacted 3 soil lifts. All 3 lifts reached at least 95% compaction. Measured and prepared next compaction area.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site: Dozer, Roller

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

03 OCTOBER 2019, Thursday  
Spring Valley, DC  
Matthew Rider, Safety

(3)

- 0630 Morning Safety Brief, HI - 81 WIND 5-10 S Humidity 70%  
Partly to Mostly cloudy (Breeze out)
- 0640 Radio checks Completed
- 0710 Team gets downrange to prep for laying first <sup>Lift</sup> layer of  
the Day for Troxler Testing Compaction
- 0715 Team Takes measurements to mark out next dig Area
- 0813 Troxler Test Completes Sand cone Test
- 0845 Team begins laying And Compacting Lift 11 (Troxler 10)
- 0850 Dust Monitor Reading 23.9
- 0916 Troxler Test of Lift 11 (Troxler 10) Completed - 96% Compaction
- 0920 Team begins laying And Compaction of Lift ~~10~~ (Troxler 11)
- 0956 Troxler Test of Lift 12 (Troxler 11) Completed - 108.6 Compaction
- 1000 Team begins laying And Compaction of Lift 13 (Troxler 12)
- 1042 Troxler test of Lift 13 (Troxler 12) completed - 99.7% Compaction
- 1100 CP Conference Call
- 1200 Lunch Break
- 1230 Returned to Work
- 1240 Team began Prep of Next dig Area (measured And  
Painted out lines)
- 1530 Team set up erosion control measures for possible weekend  
Rain event
- 1630 End of week Brief, Clean up, Vehicle Inspection
- 1700 End of Day





CONSULTING ENGINEERS, SOIL SCIENTISTS AND GEOLOGISTS  
9502 CENTER STREET, MANASSAS, VIRGINIA 20110-5547

## SOIL DAILY FIELD REPORT

(703) 366-3000  
FAX (703) 366-3400  
www.soilconsultants.net

THIS REPORT IS A PRELIMINARY SUMMARY OF WORK PERFORMED. ALL ITEMS CHECKED AND COMMENTS MADE ARE SUBJECT TO REVIEW AND VERIFICATION PENDING THE ENGINEER'S EVALUATION.

Date: 10/3/19  
Project #: 50000 P Project Name: Remedial actions @ Glenbrook Rd. NW/  
Client: Parsons - Envision More  
Technician's Name: Andrew Haldane Emp. #: HALA  
Person in Charge, and their Company: Bart, Parsons / Bryant  
Weather: Overcast Temp: 74°F

### TYPE OF SERVICE

### TIME IN SERVICE

☒ Density Tests, quantity: 3 Start Time: 5:30 AM Break from  
☐ Sample Pickup: Time On Site: 6:30 AM 6:30 AM  
Proctor: Location Time Off Site: 7:30 AM  
1-PT: Location  
CBR: Location  
☐ Delivery ☒ Other 1 sand cone test End Time:  
Total Time:

☒ Lots ☐ Street (☐ Sanitary ☐ Storm ☐ Water ☐ Subgrade/Subbase)

Building Address(es) 4325 Glenbrook Road NW, DC

Survey Stakes Provided by: ☐ Civil ☐ Contractor Name:

Proctors Used On Site (Lab Control #'s) 111.9 @ 15.3

Quarry Proctor: Name/Location Corrected for +4 ☐ Yes ☐ No

Erosion Controls Present? ☒ Yes ☐ No

IN COMPLIANCE ☐ NOT IN COMPLIANCE ☐ WITH GEOTECHNICAL PLANS ☐  
WITH COMPACTION REQUIREMENTS ☐

Non-compliance items:

### Remarks:

Compaction at remediation site on Glenbrook Road North west.  
1 sand cone test and 3 density tests. All results passed.

Signature of Technician Andrew Haldane

Signature of Site Representative

Project Manager Review

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 07 October 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 81 degrees, mostly cloudy, winds 5-10 mph

**Personnel on Site**

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, Dave		
	Yorkshire, Bart		
Oien, Josh			
Rider, Matt	<b>ACCUPERMIT</b>		
	Vargas, Brandon		
	Amaya, Kevin		
	<b>CENAB</b>		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No Intrusive excavation today. Dumped and cut up drums. Loaded out 3 trucks for subtitle D landfill. Covered 2 hazardous roll-offs with plastic sheeting as extra layer of protection. Installed and tested new conference phone at the Federal Property. CPJA surveyor marked boundaries of backfill Area 1.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



07 OCTOBER 2019  
Spring Valley, DC  
Matthew R. der, Safety

(64)

0630 Morning Safety Brief, HI-80 wind 10-15 SSW Humidity 65%

Mostly cloudy chance of Rain Afternoon

(JED OUT)

0645 Team goes to Fed prep to help Zimmer Prep for Subtitle  
D Shipments (3 Truck)

1045 went to check on Team, Everyone OK

1120 Surveyor showed up to shoot in Competition Area and  
Area 4

1125 Team Recovered the HAZ Roll OFFS

1200 Lunch Break


1230 Returned to work

1245 Team went to Fed Site to Finish Dumping And cutting  
Soil Drums

1500 went to Fed Prep to check on the Team Everyone okay

1630 Team Returned for End of Day Brief And Clean up

1700 End of Day



## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 08 October 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 69 degrees, mostly cloudy/overcast, winds 10-20 mph

**Personnel on Site**

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, Dave		
Marion, Jed	Yorkshire, Bart		
Oien, Josh			
Rider, Matt	<b>ACCUPERMIT</b>		
	Williams, Donald		
	Marin, Naun		
	<b>CENAB</b>		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Began excavation of clean backfill for compaction in backfill area 2. Weighed soil drums at the Federal Property for Hazardous Shipment on 10/17.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



08 OCTOBER 2019  
Spring Valley, DC  
Matthew Rider, Safety

(65)

- 0630 Morning Safety Brief, HI-69 wind 10-15 NE Gust to 30mph  
Humidity 65% Mostly cloudy chance of Rain showers late
- 0645 Radio checks completed
- 0700 Team went downstairs to go over Excavation plan
- 0745 Zimmer checked out machines and warmed them up
- 0800 Dust Monitor Reading 8.1
- 0805 Excavation started on the East side of the Strip going  
Towards Glenbrook
- 0900 Dust Monitor reading 8.7
- 1000 Dust Monitor Reading ~~16.9~~ 16.9
- 1100 Dust Monitor Reading 5.0
- 1145 First Lift layed down in excavation and compacted
- 1200 Lunch Break
- 1230 Returned to work
- 1240 Team went to Fed Prop to weigh Drums to Prep for HAZ  
Shipman on 17 OCT
- 1500 Visited Team At Fed Prop, Everyone okay
- 1630 End of Day Brief And clean up
- 1700 End of Day

*Matthew Rider*

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 09 October 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 69 degrees, partly cloudy, winds 10 mph

**Personnel on Site**

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren	Haldane, Andrew	
Courtney, Kenneth	Wright, Dave		
Marion, Jed	Yorkshire, Bart		
Oien, Josh			
Rider, Matt	ACCUPERMIT		
	Marin, Naun		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Backfilled and compacted 10 soil lifts. Erosion and sediment controls were inspected and updated around command post.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

09 OCTOBER 2019  
Spring Valley, DC  
Matthew Rider, Safety

(CC)

0630 Morning Safety Brief HI-69 wind 10-15 NE Humidity 59%

Partly to Mostly Cloudy Slight chance of Rain Shower

(DAVE OUT)

0640 Radio checks completed

0700 Team begins Prep for the first Troxler Test

0748 Dust monitor Reading 9.2

0753 Lift Zero Tested by Troxler Completed 100.7% Compaction

14.8% moisture content

0810 Team begins to lay And compaction of Lift (1)

0815 Dave Arrives on site

0908 Troxler Test of Lift 1 Completed 99% Compaction

16.6% moisture content

0910 Team begins laying And compaction of Lift 2

0940 Dust Monitor Reading 9.1

0943 Troxler Test of Lift 2 completed 99.6% Compaction

16% moisture content

0945 Team begins to lay And compact Lift 3

1015 Troxler Test of Lift 3 Completed 100.1% Compaction rate

16.6% moisture content

1017 Team begins to Lay Lift 4 And compact it

1055 Troxler Test of Lift 4 Comple - Troxler - 96.5% Compaction

17.7% moisture

1100 Team begins to lay And compact Lift 5

1129 Troxler Test of Lift 5 completed - 98% Compaction

17.8% moisture content



CONSULTING ENGINEERS, SOIL SCIENTISTS AND GEOLOGISTS  
9903 CENTER STREET, MANASSAS, VIRGINIA 20110-5547

## SOIL DAILY FIELD REPORT

(703) 366-3400  
FAX (703) 366-3400  
www.soilconsultants.net

THIS REPORT IS A PRELIMINARY SUMMARY OF WORK PERFORMED. ALL ITEMS CHECKED AND COMMENTS MADE ARE SUBJECT TO REVIEW AND VERIFICATION PENDING THE ENGINEER'S EVALUATION.

Date: 10/9/19  
Project #: 50000 P Project Name: Remedial Action @ Glenbrook  
Client: Parsons

Technician's Name: Andrew Holdens Emp.#: 4141

Person in Charge, and their Company Bart, Parsons

Weather Sunny Temp. 70

### TYPE OF SERVICE

### TIME IN SERVICE

☒ Density Tests, quantity: 9 nuclear gauge Start Time: 5:30  
☐ Sample Pickup: Time On Site: 7:30  
Proctor Location: Time Off Site: 3:30  
1-PT Location: End Time:  
CBR Location: Total Time:  
☐ Delivery ☒ Other 1 sand cone

☒ Lots ☐ Street (☐ Sanitary ☐ Storm ☐ Water ☐ Subgrade/Subbase)

Building Address(es): 4825 Glenbrook Road NW, DC

Survey Stakes Provided by: ☐ Civil ☐ Contractor Name:

Proctors Used On Site (Lab Control #'s): 114.0 @ 15.0

Quarry Proctor: Name/Location: Corrected for +4 ☐ Yes ☐ No

Erosion Controls Present? ☒ Yes ☐ No

IN COMPLIANCE ☐ NOT IN COMPLIANCE ☐ WITH GEOTECHNICAL PLANS ☐  
WITH COMPACTION REQUIREMENTS ☐

Non-compliance Items:

Remarks:

Compaction testing of ten lifts in trench B. All lifts passed. Progress halted in lower portion of the pile owing to increasing moisture.

Signature of Technician Andrew Holdens

Signature of Site Representative [Signature]

Project Manager Review [Signature]

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 10 October 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 74 degrees, partly cloudy, winds 5 - 10 mph

**Personnel on Site**

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren	Haldane, Andrew	
Courtney, Kenneth	Wright, Dave		
Marion, Jed	Yorkshire, Bart		
Oien, Josh			
Rider, Matt	<b>ACCUPERMIT</b>		
	Valle, Marvin		
	Marin, Naun		
	<b>CENAB</b>		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Backfilled and compacted 5 soil lifts. Replaced 4 VCT floor tiles in command post.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



10 OCTOBER 2019  
Spring Valley, DC  
Mazhen Rider, Safety

(68)

- 0630 Morning Safety Brief - HS-74 wind S-10W Humidity 59%  
Partly cloudy skies
- 0700 Radio checks completed
- 0730 Team began mixing soil around to let the moisture levels  
Dry out
- 0840 Team began to Re Compact Lift 10 that Failed End of Day  
Yesterday (95% Compaction 19% moisture)
- 0905 Troxler Test Completed for Lift 10 Re-compaction 97.7% Compaction  
16.2% moisture content
- 0910 Troxler Tested the north end of Lift 10, moisture content was  
High, Re-fluffed Ditt and waiting for it to Dry out
- 1030 Dust monitor 47
- 1031 Team Compacting Lift 10 again to achieve passing 9%
- 1044 Troxler Testing Completed for Lift 10 Completed 97.7% Compaction  
15.2% moisture content
- 1047 Team begins laying And Compacting Lift 11
- 1109 Troxler Tested for Lift 11 Completed 96.7 Compaction  
17.5 moisture content
- 1115 Lunch Break
- 1145 Returned to work
- 1150 Team began laying And Compacting Lift 12
- 1224 Troxler Testing for Lift 12 Completed 99.8% Compaction  
13.9% moisture content
- 1226 Team begins laying Lift 13 for compaction
- 1235 Team starts compaction on Lift 13





CONSULTING ENGINEERS, SCIENTISTS AND GEOLOGISTS  
9303 CENTER STREET, MANASSAS, VIRGINIA 20110-5547

## SOIL DAILY FIELD REPORT

(703) 366-3000  
FAX (703) 366-3400  
www.soilconsultants.net

THIS REPORT IS A PRELIMINARY SUMMARY OF WORK PERFORMED. ALL ITEMS CHECKED AND COMMENTS MADE ARE SUBJECT TO REVIEW AND VERIFICATION PENDING THE ENGINEER'S EVALUATION.

Project #: 50000P Project Name: Remedial Action @ Glenbrook Date: 10/10/19  
Client: Parsons  
Technician's Name: Andrew Haldane Emp.#: HALA  
Person in Charge, and their Company: Bryant, Parsons  
Weather: Sunny Temp. 70° F

### TYPE OF SERVICE

### TIME IN SERVICE

☒ Density Tests, quantity: 5 Start Time: 6:00 AM Breaks  
☐ Sample Pickup: Time On Site: 8:00 AM 7:30-8:00  
Proctor: Location Time Off Site: 11:30-12:00  
1-PT: Location  
CBR: Location  
☐ Delivery ☐ Other Total Time:

☒ Lts ☐ Street ☐ Sanitary ☐ Storm ☐ Water ☐ Subgrade/Subbase

Building Address(es) 4875 Glenbrook Rd NW, D.C

Survey Stakes Provided by: ☐ Civil ☐ Contractor Name:

Proctors Used On Site (Lab Control #'s) 1814.0 @ 15.0

Quarry Proctor: Name/Location: Corrected for +4 ☐ Yes ☐ No

Erosion Controls Present? ☒ Yes ☐ No

IN COMPLIANCE ☐

NOT IN COMPLIANCE ☐

WITH GEOTECHNICAL PLANS ☐

WITH COMPACTION REQUIREMENTS ☐

Non-compliance Items:

Remarks:

Compaction testing in area B-2. Five lifts tested once each.  
All passed.

Signature of Technician Andrew Haldane

Signature of Site Representative

Project Manager Review

40100-9-100

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 15 October 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 73 degrees, Sunny

**Personnel on Site**

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, Dave		
Marion, Jed	Yorkshire, Bart		
Oien, Josh			
Rider, Matt	<b>ACCUPERMIT</b>		
	Valle, Marvin		
	Marin, Naun		
	<b>CENAB</b>		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive digging today. The team weighed and organized soil drums for hazardous waste shipment on 10/17. Cut the grass at 4825 Glenbrook Road. Removed geotextile cloth scraps from downrange area.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

15 OCTOBER 2019 Tuesday  
Spring Valley, DC  
Matthew Rider, Safety

(70)

0630 Morning Safety Brief - HI-73 wind S-10E Humidity 50%

Mostly Sunny / Sunny

0640 Team went to Fed Prep to weigh Drums in Prep  
for HAZ Shipment on the 17th Oct

0825 Informed the Camera System at Fed Prep not Working  
Properly by Todd (Corps Rep) STEGLER

0900 Josh Reset cameras manually, System back online

0907 CP Noticed Frost build up on the A/C Lines used  
for 483S Property (Au Pros House)

1000 Called Densel to Request Service for A/C Units

1100 Bruce Ran Weed Eater on 482S Area

1200 Lunch Break

1230 Returned to work


1240 Team Relocated Drums in Prep for HAZ Shipment

1345 Densel called said No Record of Service History  
Not Coming Today

1415 Team Downstates Prepping Site for Rain Event

1630 End of Day Brief and Clean up

1700 End of Day



## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 16 October 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 63 degrees, Rain showers, windy

**Personnel on Site**

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, Dave		
	Yorkshire, Bart		
Rider, Matt	ACCUPERMIT		
	Valle, Marvin		
	Marin, Naun		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive digging today. The team cleaned and organized dress out trailer.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

16 OCTOBER 2019, Wednesday  
Spring Valley, DC  
Matthew Rider, Safety

(71)

0630 Morning Safety Brief - HI 63 Wind 10-20W Humidity 88%

Strong Rains And winds Rain up to 1", heavier locally

And wind Gusts up to 30mph

(JOSH OUT) (JED OUT)

0640 Zimmer went to Fed Prop to prep for the Rain Event

And organize Areas

0700 Bruce went downstairs to organize the Dress out

Trailer And Map the Floors

1045 Heavy Rains start in Area, work put on Hold

1130 Lunch Break

1200 Returned to work

1201 (Bruce changes Time Card Head's Home)

1400 Heavy Rains continue in Area

1600 Rain starts to Taper off

1630 End of Day Brief

1700 End of Day

*Matthew Rider*



## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 17 October 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 59 degrees, Partly Cloudy and windy, WNW 20-30 mph

**Personnel on Site**

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, Dave		
Marion, Jed	Yorkshire, Bart		
Oien, Josh			
Rider, Matt	<b>ACCUPERMIT</b>		
	Valle, Marvin		
	Marin, Naun		
	<b>CENAB</b>		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive digging today. Hazardous shipment loaded out. Pumped out rainwater tank from 4835 roofline.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



17 October 2019, Thursday  
Spring Valley, DC  
Matthew Rider, Safety

(12)

- 0630 Morning Safety Brief - H163 wind 20-30mph w/w Humidity 50%  
Partly cloudy with Strong winds 20-30mph Gusts over 40mph
- 0640 Team heads to Fed Prop to prepare for the HAZ  
Shipment
- 0730 Team begins loading out Drums onto the Trucks
- 0740 Water Trucks arrive to pump out Baker Tank 257767
- 1100 Last Drums Loaded on Truck (Total of 131 Drums loaded)  
2 Trucks
- 1145 Last water Truck Filled (4 Total Trucks)  
Baker Tank 257767 Emptied
- 1200 Lunch Break
- 1230 Returned to work
- 1315 Team went Downrange to Pump water out of the water  
Storage Tank collecting Rain water from 4835
- 1530 Team began Trailer clean up And vehicle maintenance
- 1630 End of work Brief
- 1700 End of Day

# SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 21 October 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 68 degrees, Partly Cloudy, Winds NE 5-10 mph

## Personnel on Site

PARSONS	ZES	SCE	
Bryant, Joe			
	Wright, Dave		
Marion, Jed			
Oien, Josh			
Rider, Matt	ACCUPERMIT		
	Valle, Marvin		
	Marin, Naun		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive digging today. Densel A/C technician visited 4835 GR and confirmed the frozen refrigerant line was caused by a leak. Discovered a leak in the roof of 4835 while in attic inspecting A/C units. Prepared bottleware for backfill sample. Prepared rolloffs for clean out and return. Pumped out rainwater tank from 4835 roofline.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

21 October 2019, Monday  
Spring Valley, DC  
Matthew Rider, Safety

(73)

0630 Morning Safety Brief, HZ-68, wind S-10-16 Humidity 70%

Mostly cloudy chance of showers Afternoon

(Bruce out) (Warren out) (Bart out)

0640 Team went downstairs to set up for pumping out SS901

Water container catching rain water

0745 Team begins pumping water from Rain Catch container

1045 Team Inspected perimeter Fence, made Repairs where needed

1200 Lunch Break

1230 Returned to work

1245 Team went to Fed Prop to set up for washing to Roll offs

To prep for Turn in

1630 Team Returned for End of Day Brief And clean up

1700 End of Day

Matthew Rider

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 22 October 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 68 degrees, Rain, Winds W 10-15 mph

**Personnel on Site**

PARSONS	ZES	SCE	
Bryant, Joe			
Courtney, Kenneth	Wright, Dave		
Marion, Jed	Yorkshire, Bart		
Oien, Josh			
Rider, Matt	<b>ACCUPERMIT</b>		
	Vargas, Brian		
	Marin, Naun		
	<b>CENAB</b>		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive digging today. Densel technician found the leak in A/C unit coming from condensor coil in basement of 4835 GR. Visited backfill site in Bethesda. William Scottsman technician fixed lights in CP trailer.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

22 OCTOBER 2019, Tuesday  
Spring Valley, DE  
Matthew Rider, Safety

(74)

- 0630 Morning Safety Brief, HI-68 wind 10-15 NE Humidity 75%  
Patchy Showers in Afternoon, chance of Rain 100% .25" possible
- 0640 Went over Items needed for Supply Run to handle water  
Issue for 4835 Glenbrook
- 0845 PM Sean Buckley Arrived for meeting About DOB And upcoming  
Operations
- 0915 Bruce And JED went to Home Depot on A Supply Run
- 0920 Josh And Joe Escorted the Diesel person working  
on the ACs At 4835 Glenbrook
- 1100 Joe, Doug, Bart went to Bethesda to look At An Area  
for Potential backfill Import
- 1200 Lunch Break
- 1230 Returned to work
- 1240 Got Info to Send to Jenna to get new insurance for  
the Replacement Truck (F-150 Recalled) now Have Dodge
- 1300 Williams Scottsman Showed up to Replace the ballast on the lights  
In the CP Trailer
- 1310 Team Set up new Rain Water Drainage System for the  
Side of 4835 (Corrugated Tube) Running to gravel bed
- 1430 Steady Rain begins
- 1630 End of Day Brief And clean up
- 1700 End of Day

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 23 October 2019  
 Site Location: 4825 Glenbrook Road

Weather:  
 High 67 degrees, Sunny and Breezy, Winds NW 10-15 mph

## Personnel on Site

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, Dave		
Marion, Jed	Yorkshire, Bart		
Oien, Josh			
Rider, Matt	ACCUPERMIT		
	Vargas, Brian		
	Marin, Naun		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Clean out rolloffs at the Federal Property.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

## Visitors


## Contractors

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:


Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



23 OCTOBER 2019, Wednesday  
Spring Valley, DC  
Matthew Rider, Safety

(75)

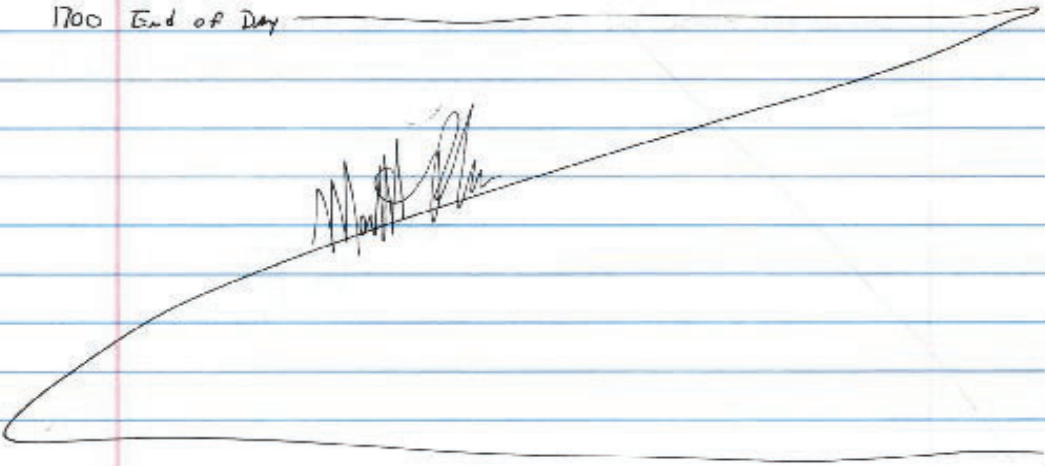- 0630 Morning Safety Brief, HI 67 wind 10-15mph WNW  
Humidity 50% Sunny / Mostly Sunny
- 0640 Team changes light bulbs in Break Trailer
- 0730 Team Heads to Federal Property to Set up for the  
cleaning of Roll offs
- 1030 Went to Fed Prop to check on Team, Everyone okay
- 1200 Lunch Break
- 1230 Returned to work
- 1245 Team Continued to clear Roll offs And conducted An  
Inventory of Tyvek gloves And Hand warmers in the  
Back office At Fed Prop Trailer
- 1430 Went to check on Team At Fed Prop, Everyone okay
- 1530 Team returned to site to "Fluff" ground dirt in order  
to let it Dry faster
- 1630 End of Day Brief & clean up
- 1700 End of Day
- 

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 24 October 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 70 degrees, Sunny

**Personnel on Site**

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, Dave		
Marion, Jed	Yorkshire, Bart		
Oien, Josh			
Rider, Matt	<b>ACCUPERMIT</b>		
	Vargas, Brian		
	Marin, Naun		
	<b>CENAB</b>		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Brought three rollofs of clean backfill downrange to fill in slope next to 4835 GR. Sloped soil away from 4835 GR.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

24 OCTOBER 2019, Thursday  
Spring Valley, DC  
MATTW Riden, Safety

(16)

- 0630 Morning Safety Brief, HI-70 wind 5-10 SSE Humidity 50%  
Partly / Mostly Sunny Sunny Afternoon
- 0645 Radio check completed
- 0710 Team went downrange to open gates And Prep for  
Loads of Dirt from Roll OFF Truck
- 0730 Roll OFF Truck Arrives with 1<sup>st</sup> Load of Dirt
- 0740 Dave Begins Spreading Dirt out To fill in Low Areas And  
Ramp up towards House
- 0830 Two More Roll OFF Loads Are Dumped And Dave to continues  
to Spread and Compact Dirt
- 1020 Team Finishes Pumping Dirt to House with Shovels And Rakes
- 1200 Lunch Break
- 1230 Returned to Work
- 1235 Team went to Fed Prop to continue Roll OFF cleaning
- 1500 went to Fed Prop to check on Team, Everyone OKay
- 1600 Team Returned to Site to clean up And Vehicle Maintenance
- 1700 End of Day

Mattw Riden

# SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 28 October 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 68 degrees, Sunny

## Personnel on Site

PARSONS	ZES	SCE	
	Prate, Warren		
Courtney, Kenneth	Wright, Dave		
Marion, Jed	Yorkshire, Bart		
Oien, Josh			
Rider, Matt	<b>ACCUPERMIT</b>		
	Vargas, Brian		
	Marin, Naun		
	<b>CENAB</b>		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Took grade point elevation shots to determine if foundation drain of 4835 GR could be daylighted in the front yard. Cleaned roll-offs at the Federal Property. Checked 4835 GR for water damage (none observed). Dug along 4835 GR foundation to verify drain pipe location.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

### Visitors


### Contractors

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

28 OCTOBER 2019, Monday  
Spring Valley, DC  
Matthew Ridgway for

(77)

- 0630 Morning Safety Brief, HI 68 Wind S-OWE Humidity 65%  
Mostly Sunny All day. Plentiful Sunshine (JOE OUT)
- 0640 Radio checks completed
- 0700 Team went Downstairs to shoot grade points for any future  
Drainage work that might need done
- 0830 Team went to Federal property to clean/wash out  
Roll offs to prep for Turn In
- 1200 Lunch Break
- 1230 Returned to work
- 1240 Team went Downstairs to check the 4835 House (Au Pros)  
for signs of water damage. Also dug down to verify  
location of the drainage pipe
- 1400 Team went to Fed prop to grease and lube washed  
Roll offs for Turn in prep
- 1630 Team Returned to Site for End of Day Brief  
And clean up
- 1700 End of Day

Matthew Ridgway

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 29 October 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 69 degrees, Cloudy

**Personnel on Site**

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, Dave		
Marion, Jed	Yorkshire, Bart		
Oien, Josh			
Rider, Matt	<b>ACCUPERMIT</b>		
	Vargas, Brian		
	Vargas, Gustavo		
	<b>CENAB</b>		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Brought clean backfill downrange to grade slope on back corner of site near 4835. Collected backfill samples from construction site in Bethesda, MD.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



29 OCTOBER 2019, Tuesday  
Spring Valley, DC  
Matthew Riden, Safety

(78)

- 0630 Morning Safety Brief, H<sub>2</sub>-67 wind - 5-10 mph NE Humidity 75%,  
cloudy to <sup>partly</sup> cloudy,  
0640 Radio Checks Completed  
0700 Team heads downstairs to open the gate and prep to  
bring over dirt filled Roll OFFs  
0800 JOE and JED Depart for Bethesda for samples of the new  
proposed backfill area. Roll OFFs begin to arrive to  
Bring in dirt to slope (blend) area around the back  
of the house  
0930 First Baker Tank shipped out (25951C)  
1120 Mechanical Issue with DOZER Sun Belt Tech Called  
1130 One More Roll OFF Truck Before Lunch (41 Total so far)  
1200 Lunch Break  
1230 Returned to work  
1245 Continued to bring dirt in on Roll OFFs to build the slope  
around the house  
1530 Second Baker Tank being Removed (251613)  
1630 End of Day Brief And Clean up  
1700 End of Day

Matthew Riden

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 30 October 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 66 degrees, Cloudy

**Personnel on Site**

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, Dave		
Marion, Jed	Yorkshire, Bart		
Oien, Josh			
Rider, Matt	<b>ACCUPERMIT</b>		
	Vargas, Brian		
	Vargas, Gustavo		
	<b>CENAB</b>		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Loaded out trucks for subtitle D landfill. Cleaned roll-offs. Purchased heat trace wrapping for water line. Fueled excavators.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

30 OCTOBER 2019, Wednesday  
Spring Valley, DC  
Matthew Rider, Safety

(19)

- 0630 Morning Safety Brief, HI-67 wind 5-10 ESE Humidity 80%  
Foggy/cloudy in the morning 60% chance of Rain in the  
Afternoon turning to 100% at night
- 0700 Team went to Fed Prep to Prep for Subtitle D Shipments  
going out 4 Trucks Total
- 0930 JED And Bruce went on Shopping Run to buy Heat Trace Lines  
And Hose Sections
- 1145 Last Truck loaded out for Subtitle D Shipment
- 1200 Lunch Break
- 1230 Returned to work
- 1240 Team did walk around to see if Any Erosion Control  
measures were needed before the Rain Event
- 1300 Team went to Fed Prep to wash Roll OFFs And do  
A Randoming Police Call
- 1630 Team Returned to Site for End of Day Brief And  
Clean up
- 1700 End of Day

Matthew Rider

# SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 31 October 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 77 degrees, Rain

## Personnel on Site

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren		
Courtney, Kenneth			
Marion, Jed	Yorkshire, Bart		
Rider, Matt	ACCUPERMIT		
	Marin, Naun		
	Bartchah, Johnathan		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive digging. Started cleaning Baker Tank.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

31 OCTOBER 2019, Thursday  
Spring Valley, DC  
Matthew Rider, Safety

(80)

0630 Morning Safety Brief, HI 77 wind - 15-25mph Humidity 85%

Rain Showers on/OFF in the morning with strong winds followed by thunderstorms moving into the evening and night.

Strong Storms Expected wind gusts up to 40mph, 2 inches of Rain Expected, may be heavier locally. (DAVE OUT) (JOSH OUT)

0700 Team went to Fed Prep to begin Prep for cleaning out the last remaining Baker Tank

0800 Team began washing out BAKER Tank

1030 Went to Fed Prep to check on the Team, Everyone OK

1200 LUNCH BREAK (JED OUT EARLY)

1230 Returned to work


1300 Bruce cleaned Trailers and mapped them

1400 Bruce Ran delivery to UPS Store

1500 Rain started to become heavy, Gasline Controls were double checked down Range

1600 Vehicle Maintenance And End of Week Brief

1700 End of Day



## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 04 November 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 60 degrees, Sunny

**Personnel on Site**

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Jed	Yorkshire, Bart		
Oien, Josh			
Rider, Matt	<b>ACCUPERMIT</b>		
	Marin, Naun		
	Bartchak, Johnathan		
	<b>CENAB</b>		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

CCDC arrived to dig in Area 2. Moved excavation equipment and placed construction MATS for CCDC operation. Cleaned Baker Tank at the Federal Property. Inspected and repaired privacy fence around perimeter of 4825 GR. Wrapped water supply stems with heat trace cords.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:


Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



04 NOVEMBER 2019  
Spring Valley, DC  
Matthew Ricker, Safety

(81)

- 0630 Morning Safety Brief, HI 61 Wind 10-15mph S Humidity 60%  
Sunshine in the Morning followed by a cloudy Afternoon
- 0645 Radio checks completed
- 0710 Team heads downrange to open gate and get Ready to  
Assist Zimmer bringing over CCBC's Equipment for the  
project of Digging Area 2 Along the House 4835
- 0805 First load shows up from Fed Prop Team Moving Machines  
And Re-Packing Drain Gutter Tbr.
- 0900 Team Installed 3 heat Trace Cords on the Hose and Water Stems  
And Relocated the Fence Line to Free Space for ECBC
- 1030 Team Reconnected the water Line Running through Area 2  
Also Laid down Mats And brought over Drums
- 1200 Lunch Break
- 1230 Returned to Work
- 1240 JED and Bruce went to Fed Prop to assist in cleaning the  
Baker Tank
- 1420 Inspected the Au President's house for Water Entry/Damage
- 1630 Team Returned to CP for clean up And End of Day Brief
- 1700 END of Day
- 

# SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 05 November 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 64 degrees, Sunny

## Personnel on Site

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Jed	Yorkshire, Bart		
Oien, Josh			
Rider, Matt	<b>ACCUPERMIT</b>		
	Marin, Naun		
	Bartchak, Johnathan		
	<b>CENAB</b>		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Helped CCDC transport drums to and from the Federal Property. Cleaned and greased roll-offs. Cleaned Baker Tank. 2 subtitle D trucks loaded out.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

### Visitors


### Contractors

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

05 NOVEMBER 2019, Tuesday  
Spring Valley, DC  
Matthew Rider, Safety

①

- 0630 Morning Safety Brief HX-64 WIND S-10mph S Humidity - 60%  
Cloudy Morning, Sunshine in the Afternoon
- 0645 Radio checks Completed
- 0645 CCBC Arrives on Site, Sign in on Visitors Log  
Begin Morning Set up for Area 2 digging
- 0745 Stake body Truck Arrives with Set of Drums, CCBC begins  
Drumming Soil And taking Samples of Area 2
- 0800 All Drums Filled, Zimmer Arrives with a new set of Drums  
(12) And load up first set of Drums on Stake body Truck.
- 0930 CCBC Resumes Digging And Sampling of Area 2
- 1000 Went to check on Team At Fed Prop cleaning And Lubricating  
Roll OFFs
- 1130 Lunch Break
- 1200 Returned to work
- 1225 CCBC Resumed Digging And Sampling of Area 2
- 1350 Zimmer Arrived on the Stake body Truck with a new shipment  
of Drums for CCBC (12)
- 1530 CCBC STOP Operations to begin End of Day
- 1630 Team Returned from Fed Prop (Baker Tank cleaned And 2  
Sub Title D Trucks loaded And shipped out) For End of Day  
Brief And clean up
- 1700 End of Day

Matthew Rider

# SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 06 November 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 50 degrees, Partly Cloudy

## Personnel on Site

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Jed	Yorkshire, Bart		
Oien, Josh			
Rider, Matt	ACCUPERMIT		
	Amaya, Kevin		
	Vargas, Brandon		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Helped CCDC transport drums to and from the Federal Property. Returned CCDC equipment and supplies to the Federal Property. Made a supply run for water supply stem winterization activities.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information  
 \_\_\_\_\_  
 \_\_\_\_\_  
 \_\_\_\_\_

Closed cavity items found

New Equipment on Site:

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

06 NOVEMBER 2019, Wednesday  
Spring Valley, DC  
Matthew Rider, Safety

(2)

- 0830 Morning Safety Brief, HI 50 wind 5-10 SSW Humidity 60%  
Sunny to Partly cloudy in the Afternoon
- 0845 Radio checks completed
- 0900 CCBC Began Work downrange on Area 2
- 0900 JED And Bruce went on Shopping Run to purchase Equipment  
needed for Installation of J channel And drains
- 0920 CCBC Completed digging Operations in Area 2
- 0930 Zimmer And Josh Arrived on site to sling out Drums  
And load out Equipment to take to Fed Prop
- 1130 Lunch Break
- 1200 Returned to work
- 1210 Team went Downrange to begin the Restoration of the  
Site prior to Area 2 Operations And begin prepping for  
the Installation of the J channel drain
- 1500 Gathered All necessary Equipment needed to Drain AU  
Water lines And wrap them in A Heat Trace Cord.
- 1630 Clean up And End of Day Brief
- 1700 End of Day

Matthew Rider

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 07 November 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 62 degrees, Partly Cloudy, Afternoon Rain

**Personnel on Site**

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Jed	Yorkshire, Bart		
Oien, Josh			
Rider, Matt	<b>ACCUPERMIT</b>		
	Amaya, Kevin		
	Lovitte, Reginald		
	<b>CENAB</b>		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive digging today. Turned off, drained, and capped water supply line. Winterized water supply stems with insulation and plastic coverings. Began preparation for foundation waterproofing activities.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:


Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



07 November 2017, Thursday  
Spring Valley, DE  
Matthew Rider, Safety

(3)

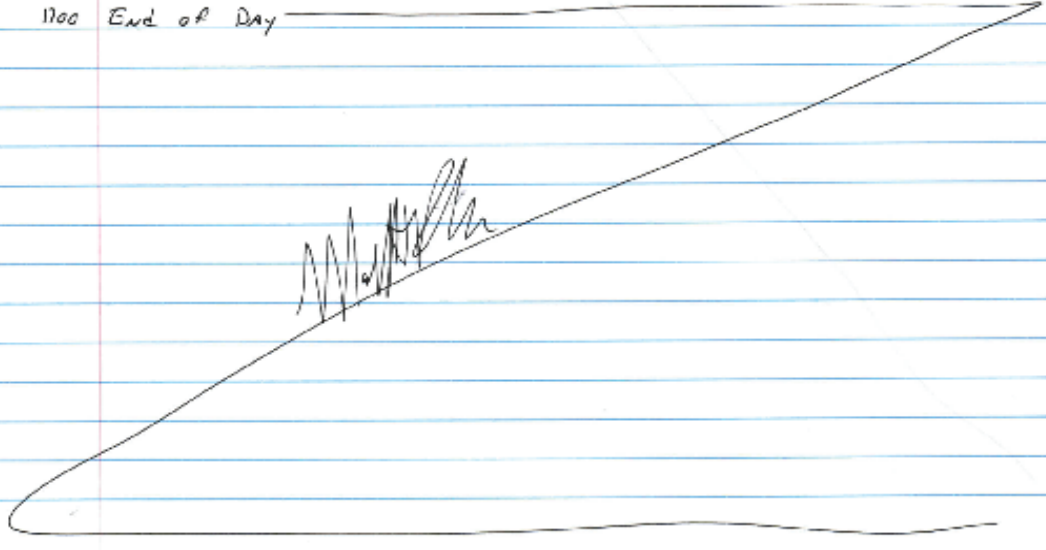- 0630 Morning Safety Brief, HI-64 wind: 5-10mph SW Humidity - 80%
- 0640 Radio checks completed
- Weather - Cloudy in the Morning with Rain developing in the Afternoon possible Snow
- 0700 Team went to Fed Prop to gather the Insulation for the water stems
- 0730 Team begins wrapping the water stems with the Heat Trace Cord And Insulation After they shut off And Drained the Lines
- 1000 Team Completes Vehicle Inspections
- 1230 Lunch Break
- 1300 Returned to work
- 1310 Team Continued to prep downrange Area for the waterproofing And installation of the Jchannel And French drain on the AU Pres House (4835 Glenbrook)
- 1600 Team begins weekly clean up And maintenance
- 1630 End of week brief
- 1700 End of Day
- 

**SPRING VALLEY, WASHINGTON DC**

**Contract No:** W912DY-09-D-0062  
**Delivery Order:** TO 0006  
**Date:** 12 November 2019  
**Site Location:** 4825 Glenbrook Road

**Weather:**  
 High 52 degrees, Rain, Winds 15-20 mph

**Personnel on Site**

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Jed	Yorkshire, Bart		
Oien, Josh			
Rider, Matt	<b>ACCUPERMIT</b>		
	Marin, Naun		
	Vargas, Gustavo		
	<b>CENAB</b>		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Excavated clean backfill around foundation of 4835 for waterproofing. Pressure washed 4835 foundation wall in preparation for waterproofing coating.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

**Problems encountered/resolutions:**

**Instructions given by government personnel:**

**Activities anticipated for tomorrow:**

<b>Attachments</b> (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	<i>To be included if investigation is using CSS protocols</i>
Dig Sheet	Y/N	<i>To be included at least once every week during intrusive investigation</i>
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	<i>To be included weekly during field activities</i>
Property Management Summary	Y/N	<i>Include complete property inventory once every month</i>
Photographs	Y/N	

12 November 2019, Tuesday  
Spring Valley, DC  
Matthew Rider, Safety

①

- 0630 Morning Safety Brief, HI-52 Wind 15-20nm Humidity- 80%  
Temp dropping throughout Day till it reaches mid 30's. 90% chance  
of Rain Till Noon  $\frac{1}{4}$ " expected, Turning cloudy And cold  
in the Afternoon
- 0700 Radio checks Completed
- 0710 Team went downrange to get gate open to begin  
Prep for J channel Installation
- 0800 Team began digging out Dirt next to the foundation of  
4835 for J channel Installation
- 1130 Lunch Break
- 1200 Returned to work
- 1210 Digging Complete, Zimmer Brings over Pressure Washer  
to clean outside walls for J channel set up
- 1230 Team Begins to Remove Dirt And other debris from wall  
to begin pressure washing the walls for waterproofing  
Application
- 1630 Team begins Clean up and end of Day Briefs
- 1700 End of Day —

~~Matthew Rider~~

# SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 13 November 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 39 degrees, Partly Sunny

## Personnel on Site

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Jed	Yorkshire, Bart		
Oien, Josh			
Rider, Matt	ACCUPERMIT		
	Marin, Naun		
	Vargas, Gustavo		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Applied waterproof coating to 4835 foundation wall.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

### Visitors


### Contractors

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

13 November 2019, Wednesday  
Spring Valley, DC  
Matthew Rider, Safety

(5)

- 0630 Morning Safety Brief, HI 38 wind 10-15 Humidity 45%  
Sunny Morning turning Partly cloudy winds 10-15nmw
- 0700 Radio checks completed
- 0715 Team began set up for the Application of the Waterproofing  
on the foundation of the 4835 House.
- 0730 Team begins Application of Waterproof Paint Seal
- 0745 Zimmer brings over 2 portable ~~heat~~ heaters to keep paint  
from forming to quickly
- 1115 Team Ran out paint, trip to Home Depot and Mitco  
To purchase more Supplies
- 1200 Lunch Break
- 1230 Returned to work
- 1310 Waterproofing Paint Completely gone, waiting for Bruce & JED  
to get back with Resupply
- 1330 Team cleaned up And Organized downrange while waiting  
for Supplies to Arrive
- 1445 Team got more paint on site and began applying more  
paint to the 4835 foundation.
- 1630 End of Day Clean up And Brief
- 1700 End of Day

Matthew Rider

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 14 November 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 47 degrees, Partly Sunny

**Personnel on Site**

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Jed	Yorkshire, Bart		
Oien, Josh			
Rider, Matt	<b>ACCUPERMIT</b>		
	Vargas, Brandon		
	<b>CENAB</b>		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Finished applying waterproof coating to 4835 foundation wall. Expanded the excavated trench around 4835 foundation by 8 feet horizontally for compaction testing effort.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:


Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



14 November 2019, Thursday  
Spring Valley, DC  
Matthew Rider, Safety

(6)

- 0630 Morning Safety Brief, Ht 42 Wind 10-15mph S Humidity 50%  
Mix of Sun And Clouds All Day
- 0645 Radio checks Complete
- 0700 Team begins set up for the Application of the waterproof  
Paint on the foundation of the 4835 House
- 0800 Team begins Applying the waterproof paint on the foundation  
of the 4835 property
- 1130 Lunch Break
- 1200 Returned to work
- 1210 Began Removing Soil from Around the footer Trench to see  
if A 95% compaction rate can be Achieved without the  
Vibrating Shells foot next week
- 1415 Team began Installing the new French Drain System at the  
Base of the footer and the foundation of 4835 property
- 1600 Vehicle maintenance And End of work clean up And Brief
- 1700 End of Day

Matthew Rider

# SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 18 November 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 49 degrees, Cloudy

## Personnel on Site

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Jed	Yorkshire, Bart		
Oien, Josh			
Rider, Matt	ACCUPERMIT		
	Vargas, Brian		
	Vargas, Gustavo		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive digging. Began installing J-Drain. Painted door trim at the Federal Property.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information  
 \_\_\_\_\_  
 \_\_\_\_\_  
 \_\_\_\_\_

Closed cavity items found \_\_\_\_\_

New Equipment on Site: \_\_\_\_\_

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

18 November 2019, Monday  
Spring Valley, DC  
Matthew Rider, Safety

(7)

- 0630 Morning Safety Brief, HI-49 wind ~ 5-10mph, new humidity, 75%  
Mostly cloudy throughout the Day
- 0700 Radio checks complete
- 0720 Team gathers J-Drain materials to put on the foundation  
wall of 4835. Began prepping area while waiting for  
Temps to Rise.
- 0830 Team began to Attach J-Drain to the foundation wall  
of 4835 House
- 1130 Lunch Break
- 1200 Returned to work
- 1245 Team Completed what Actions could be Done with the  
J-Drain
- 1300 Team prepped Area for Trier Test in the Morning
- 1430 Bruce Painted Door on Trailer at Fed Prop
- 1445 Team Started to build mock set up for our Concept of  
Operations Plan at Fed Prop
- 1630 Team Returned for End of Day Brief And Clean up
- 1700 End of Day

Matthew Rider

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 19 November 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 54 degrees, Partly Sunny

**Personnel on Site**

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Jed	Yorkshire, Bart		
Oien, Josh			
Rider, Matt	<b>ACCUPERMIT</b>		
	Marin, Naun		
	Bartchak, John		
	<b>CENAB</b>		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Compaction test. Finished installation of J-Drain. Backfilled trench next to 4835 foundation.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

19 November 2019, Tuesday  
Spring Valley, DC  
Matthew Rider, Safety

(8)

- 0630 Morning Safety Brief, H<sub>i</sub> 54 wind S-10 warmer Humidity 70%  
Partly cloudy Morning, cloudy Afternoon
- 0700 Radio Checks Completed
- 0730 Team heads down range to Prep Area to Spread Dirt for  
the Troxler Test
- 0835 Troxler Test completed for Test soil by House foundation  
Failed - Compaction 93% and 22% moisture
- 0900 Team began to backfill the hole next to the House in Order  
to hold the J-Drain in Place while its being finished
- 1130 Lunch Break
- 1200 Returned to Work
- 1210 Team Installed the upper portion of the J-Drain on the  
foundation wall of the 4835 House
- 1400 Team began back fill Against the foundation to cover the  
rest of the exposed foundation
- 1630 Team begins clean up and comes to CP for End of Day Brief
- 1700 End of Day

Matthew Rider





CONSULTING ENGINEERS, SOIL SCIENTISTS AND GEOLOGISTS  
9303 CENTER STREET, MANASSAS, VIRGINIA 20110-5547

## SOIL DAILY FIELD REPORT

(703) 366-3400  
FAX (703) 366-3400  
www.soilconsultants.net

THIS REPORT IS A PRELIMINARY SUMMARY OF WORK PERFORMED. ALL ITEMS CHECKED AND COMMENTS MADE ARE SUBJECT TO REVIEW AND VERIFICATION PENDING THE ENGINEER'S EVALUATION.

Date: 11/19/19  
Project #: 50000P Project Name: Remedial Action @ Glenbrook  
Client: Parsons - Evison Moore  
Technician's Name: Andrew Haldane Emp.#: HALA  
Person in Charge, and their Company: Joe Bryant, Parsons  
Weather: Sunny Temp. 42° F

### TYPE OF SERVICE

### TIME IN SERVICE

10

☒ Density Tests, quantity: 1 Start Time: 5:30 AM  
☐ Sample Pickup: Time On Site: 7:00 AM  
Proctor: \_\_\_\_\_ Location: \_\_\_\_\_ Time Off Site: \_\_\_\_\_  
1-PT: \_\_\_\_\_ Location: \_\_\_\_\_ End Time: \_\_\_\_\_  
CBR: \_\_\_\_\_ Location: \_\_\_\_\_ Total Time: \_\_\_\_\_  
☐ Delivery ☐ Other \_\_\_\_\_

☒ Lots ☐ Street (☐ Sanitary ☐ Storm ☐ Water ☐ Subgrade/Subbase)

Building Address(es) 4825 Glenbrook Rd, NW, D.C.

Survey Stakes Provided by: ☐ Civil ☐ Contractor Name: \_\_\_\_\_

Proctors Used On Site (Lab Control #'s) 11.9 @ 15.2

Quarry Proctor: \_\_\_\_\_ Name/Location: \_\_\_\_\_ Corrected for +4 ☐ Yes ☐ No

Erosion Controls Present? ☒ Yes ☐ No

IN COMPLIANCE ☐ NOT IN COMPLIANCE ☐ WITH GEOTECHNICAL PLANS ☐  
WITH COMPACTION REQUIREMENTS ☐

Non-compliance Items:

Remarks:

Testing to determine if vibration is necessary. High moisture content made testing problematic.

Signature of Technician Andrew Haldane

Signature of Site Representative Joe Bryant

Project Manager Review \_\_\_\_\_

Form No. 10-2019



# SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 20 November 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 54 degrees, Partly Cloudy

## Personnel on Site

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Jed	Yorkshire, Bart		
Oien, Josh			
Rider, Matt	ACCUPERMIT		
	Amaya, Kevin		
	Vargas, Brandon		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Pressure washed 10 construction MATS.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

20 November 2019, Wednesday  
Spring Valley, DC  
Matthew Risher, Safety

(9)

- 0630 Morning Safety Brief, HI-54 WIND-10-20mph Humidity - 70%  
Mix of clouds And Sun, Mostly cloudy in the Afternoon
- 0700 Radio Checks completed
- 0730 Team went Downrange to begin Set up for the Days  
Operation of Moving And Cleaning And Storing the  
28 Construction Pads located at 4525 Glenbrook property
- 0800 Team begins moving the Pads with Heavy Equipment to get  
it into position
- 0830 Washing Operation begins
- 1015 Team Takes Break
- 1030 Team Returns to work
- 1230 Lunch Break
- 1300 Returned to work washing the Pads
- 1630 Team Ends work for clean up And End of Day Brief
- 1700 End of Day

Matthew Risher

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 21 November 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 53 degrees, Cloudy

**Personnel on Site**

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Jed	Yorkshire, Bart		
Oien, Josh			
Rider, Matt	<b>ACCUPERMIT</b>		
	Vargas, Brian		
	Vargas, Gustavo		
	<b>CENAB</b>		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Transported 10 cleaned construction MATS and 6 concrete barriers to the Federal Property.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

41 November 2017, Thursday  
Spring Valley, DC  
Matthew Riden, Safety

(10)

- 0630 Morning Safety Brief, IIR-53 wind S-10 wvw Humidity 70%  
Cloudy And Sunny mix in the morning giving way to  
Mostly cloudy in the Afternoon.
- 0700 Radio checks completed
- 0730 Team went downrange to prep for the Days operation  
of Moving Cement Anchor blocks And Surplus Construction  
pads to Federal property
- 0800 Gates opened for Roll OFF Truck to pull in And Load  
out Concrete Anchor blocks
- 1000 Team Finished loading Concrete Anchor blocks into  
the back of the Roll OFF Truck
- 1005 Team Takes break
- 1035 Team Returns to work (Loading Surplus Construction Pads)
- 1130 Lunch Break
- 1200 Resumed work
- 1245 Team Completes moving Surplus Pads to Fed Prop
- 1300 Team Assists moving Roll OFFs At Fed Prop
- 1330 BAKER Tank Removed From Fed Prop (257767)
- 1415 Roll OFF Removed from Site (7 Total Removed)
- 1500 Me And Josh worked on the Concept Drawing As Bruce  
did Vehicle maintenance And checkouts
- 1630 End of week Brief And clean up
- 1700 End of Day

Matthew Riden

# SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 25 November 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 54 degrees, Partly Sunny

## Personnel on Site

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Jed	Yorkshire, Bart		
Oien, Josh			
Rider, Matt	ACCUPERMIT		
	Vargas, Brian		
	Vargas, Gustavo		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive digging.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

25 November 2019, Monday  
Spring Valley, DC  
Matthew Rider, Safety

(1)

- 0630 Morning Safety Brief HI-54 Wind-5-10sw Humidity 65%  
Partly Cloudy in the morning Sunny in the Afternoon
- 0700 Radio checks completed
- 0730 Team downrange to Prep for the Days operation  
Police Call, clean break Trailer (Dress out) see what  
Erosion control measures will be needed for the site  
over the long holiday break
- 0800 Gates opened And Company Truck brought in to load  
out Items to be transferred to Federal Property
- 1030 Team Takes a break
- 1045 Returned to work
- 1130 Lunch Break
- 1200 Returned to work
- 1300 Police Call And cleaning up of Dress out Tent Complete
- 1315 Repaired And or fortified existing erosion control measures  
for the long holiday weekend
- 1430 Team went to Fed Prop to conduct a police call And  
clean up/organize Anything that needs it
- 1630 Team Returns to the CP for clean up And End of Day Brief
- 1700 End of Day

Matthew Rider



# SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 26 November 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 60 degrees, Sunny

## Personnel on Site

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Jed	Yorkshire, Bart		
Oien, Josh			
Rider, Matt	ACCUPERMIT		
	Vargas, Brian		
	Vargas, Gustavo		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive digging.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:


Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

26 November 2019, Tuesday  
Spring Valley, DC  
Matthew Rider, Safety

②

- 0630 Morning Safety Brief H<sub>2</sub>-Co<sup>2</sup> wind S-10mph S Humidity 70%  
Mix of cloudy to partly cloudy, Sunny Afternoon
- 0700 Radio Checks Completed
- 0730 Team went to Federal Property to complete the Updated  
Inventory Page And count Shoring
- 1030 Visited Team At Fed Prop, Everyone is Okay
- 1130 Lunch Break
- 1200 Returned to work
- 1215 went over Any other Erosion Control measures that needed  
Addressed
- 1300 Team And Zimmer Tracked in All loose And wet soil  
to prevent water Run off over the holiday break
- 1500 Went over the Inventory Results found missing items that  
were previously Accounted for. Apparently Weston is  
Using Shoring And Construction Mats on our Inventory
- 1630 End of Day Brief And Cleanup
- 1700 End of Day

 Rider

# SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 27 November 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 61 degrees, Light Rain, Winds 10-15 mph

## Personnel on Site

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Jed	Yorkshire, Bart		
Oien, Josh			
Rider, Matt	ACCUPERMIT		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive digging.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

27 November 2019, Wednesday  
Spring Valley, DC  
Matthew Rider, Safety

(13)

- 0630 Morning Safety Brief - HX-61 Wind 10-20 SSW Humidity 80%  
Moist and Damp in the morning with 90% chance of  
Rain. Mostly cloudy in the Afternoon
- 0700 Radio checks completed
- 0715 Team Went Downrange to Inspect ENS measures to  
Ensure long weekend Weather durability
- 0930 Break
- 0945 Resumed work
- 1100 Cleaned up machines and completed vehicle maintenance
- 1130 End of week and Holiday weekend Safety Brief  
and clean up
- 1200 End of Day

Matthew Rider

# SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 02 December 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 44 degrees, Cloudy

## Personnel on Site

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Jed	Yorkshire, Bart		
Oien, Josh			
Rider, Matt	ACCUPERMIT		
	Vargas, Brian		
	Vargas, Gustavo		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive digging.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:


Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

02 December 2019, Monday  
Spring Valley, DC  
Matthew Rider, Safety

(14)

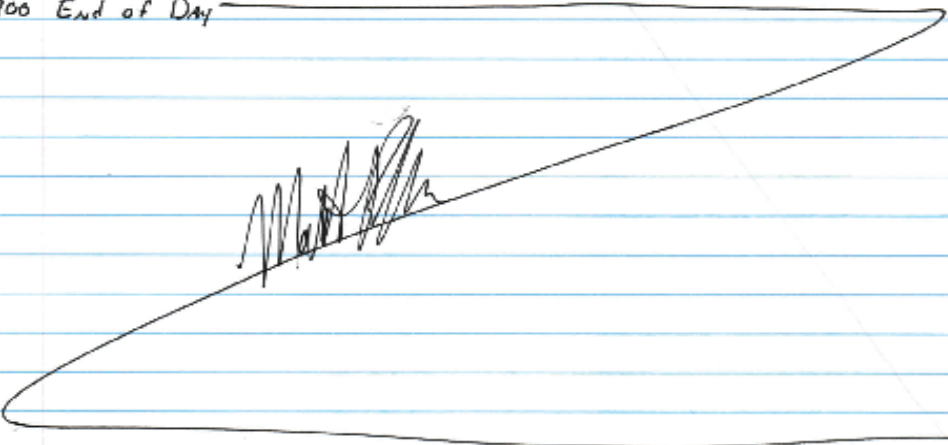- 0630 Morning Safety Brief, HI-45° Wind 10-15NW  
75% Humidity, Cloudy in the morning with Rain Showers  
on and off in the Afternoon
- 0700 Radio checks completed
- 0715 First of the month Inspections of fire extinguishers  
And First Aid Kits completed
- 0730 Team went to Fed Prop to conduct an Inventory of  
the Remaining Ems Measure Items
- 1000 Went to Fed Prop to check on the Team, Everyone  
doing well
- 1130 Inventory Completed
- 1200 Lunch Break
- 1230 Resumed work
- 1245 Team went back to Fed Prop to help Zimmer ship out  
Roll OFF's
- 1500 Roll OFF's Picked up (Total of 4 Roll OFF's left, 2 filled  
with Dirt, One set for Pick up And one Empty Remaining  
on site for General purpose)
- 1630 End of Day Brief And clean up
- 1700 End of Day
- 



## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 03 December 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 48 degrees, Sunny, Winds 10-20 mph

**Personnel on Site**

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Jed	Yorkshire, Bart		
Oien, Josh			
Rider, Matt	<b>ACCUPERMIT</b>		
	Vargas, Brandon		
	Amaya, Kevin		
	<b>CENAB</b>		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Dug an excavation for compaction activities.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

03 December 2019, Tuesday  
Spring Valley, DC  
Matthew Rider, Safety

(15)

0630 Morning Safety Brief HI 47 Wind 15-20mph NW with  
Gusts up to 30-35mph. Humidity 60%. Sunny in the  
Morning turning Mostly Cloudy in the Afternoon

0700 Radio checks completed

0730 Team went to Fed Prop to help with the Sub title D  
Shipments

0930 Dewzel! Arrives to replace/repair Heating And Air unit  
Located on the Trailers at Fed Prop

1100 Team Arrives back From Fed Prop to Install new Parking  
barriers to Replace the missing ones

1130 Last Sub title D Truck loaded

1200 Lunch Break

1230 Resumed work

1245 Team began excavating the Area between the stairs And  
the AU Prrs house (4835) for compaction trial

1330 Portable Remote compactor Arrived At Gate

1530 Began Compacting Spoils pile to prevent Run off

1630 Clean up And End of Day Brief

1700 End of Day

*Matthew Rider*

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 04 December 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 48 degrees, Cloudy, Winds 15-20 mph

**Personnel on Site**

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren	Haldane, Andrew	
Courtney, Kenneth	Wright, David		
Marion, Jed	Yorkshire, Bart		
Oien, Josh			
Rider, Matt	<b>ACCUPERMIT</b>		
	Marin, Naun		
	Ramirez, Maria		
	<b>CENAB</b>		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Compaction testing.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:


Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

041 DECEMBER 2017, Wednesday  
Spring Valley, DC  
Matthew Rider, Safety

(16)

- 0630 Morning Safety Brief, HI 48 Wind 10-20mph WSW  
Humidity 70% cloudy to mostly cloudy All Day
- 0700 Radio checks Completed
- 0730 Troxler man Arrived on site, Team began prepping hole  
for first lift compaction
- 0800 First lift Started being put in hole
- 0820 Compaction of first lift
- 0840 First lift Troxler Reading, 97% compaction 18.9% moisture  
(Testing Softer Area to double check Test)
- 0850 Second Troxler Test Failed
- 0850 Scratching up the Dirt to let the moisture Content Dry out  
(optimum Moisture Content is under 18%)
- 0900 Torpedo heaters brought from Fed prep to Dry out the moisture  
Content of the hole 98.7%
- 1120 Retest of Lift 1 - ~~99%~~ 97% compaction 17.7% moisture content
- 1125 Second lift laid in hole to let dry out
- 1130 Lunch Break
- 1200 Returned to work
- 1210 Second Lift compacted for testing
- 1230 Troxler test for 2<sup>nd</sup> Lift 93% compaction 21% moisture
- 1235 Torpedo heaters placed back into hole for drying soil
- 1250 Maintenance Man for the Bulldozer Arrived on site for  
Repairs to the machine
- 1430 Troxler Test of Lift 2 97% compaction 21% moisture
- 1435 Team "Fluffing" the hole to help it Dry out And Spreading  
the Spoils Pile out to help eliminate High moisture
- 1500 Team Doing Police Call to pick up Any Trash And Debris
- 1630 Clean up And End of Day Brief
- 1700 End of Day
- 



CONSULTING ENGINEERS, SOIL SCIENTISTS AND GEOLOGISTS  
9303 CENTER STREET, MANASSAS, VIRGINIA 20110-5517

## SOIL DAILY FIELD REPORT

(703) 366-3000  
FAX (703) 366-3100  
www.soilconsultants.net

THIS REPORT IS A PRELIMINARY SUMMARY OF WORK PERFORMED. ALL ITEMS CHECKED AND COMMENTS MADE ARE SUBJECT TO REVIEW AND VERIFICATION PENDING THE ENGINEER'S EVALUATION.

Date: 12/4/19  
Project #: 50000 Project Name: Remedial Action @ Glenbrook  
Client: Pursons Emission Mgmt  
Technician's Name: Andrew Haldane Emp. #: HALA  
Person in Charge, and their Company: Joe Bryant, Pursons Emission Mgmt  
Weather: Cloudy Temp: 49°F

### TYPE OF SERVICE

### TIME IN SERVICE

☒ Density Tests, quantity: 4 Start Time: 5:30 Break  
☐ Sample Pickup: Time On Site: 7:00 7:00-7:30  
Proctor: \_\_\_\_\_ Location: \_\_\_\_\_ Time Off Site: 11:30-12:00  
1-PT: \_\_\_\_\_ Location: \_\_\_\_\_ End Time: \_\_\_\_\_  
CBR: \_\_\_\_\_ Location: \_\_\_\_\_ Total Time: \_\_\_\_\_  
☐ Delivery ☐ Other \_\_\_\_\_

☒ Lots ☐ Street (☐ Sanitary ☐ Storm ☐ Water ☐ Subgrade/Subbase)

Building Address(es): 4825 Glenbrook Road, DC

Survey Stakes Provided by: ☐ Civil ☐ Contractor Name: \_\_\_\_\_

Proctors Used On Site (Lab Control #'s): 112-1 @ 16.5 #49230

Quarry Proctor: \_\_\_\_\_ Name/Location: \_\_\_\_\_ Corrected for +4 ☐ Yes ☐ No

Erosion Controls Present? ☒ Yes ☐ No

IN COMPLIANCE ☒ NOT IN COMPLIANCE ☐ WITH GEOTECHNICAL PLANS ☐  
WITH COMPACTION REQUIREMENTS ☐

Non-compliance items:

Remarks:

Compaction in area. Wet conditions required re-testing and drying time.

Signature of Technician: Andrew Haldane

Signature of Site Representative: John Bryant

Project Manager Review: \_\_\_\_\_

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 05 December 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 46 degrees, Sunny/Windy, Winds 10-20 mph

**Personnel on Site**

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren	Haldane, Andrew	
Courtney, Kenneth	Wright, David		
	Yorkshire, Bart		
Oien, Josh			
Rider, Matt	<b>ACCUPERMIT</b>		
	Marin, Naun		
	Ramirez, Maria		
	<b>CENAB</b>		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

Compaction testing.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



25 December 2019, Thursday  
Spring Valley, DC  
Matthew Riker, Safety

(17)

0630 Morning Safety Brief, HI-46 wind - 15-20 wvw Humidity 50%  
Sunny to Partly Cloudy  
(\* JED out \*)  
0700 Radio checks completed  
0730 Team begins to dig open hole down to Saprolite to begin  
backfilling for compaction (Clear out loose gravel and dry hole)  
0900 Team relaid first lift and compacted it  
1032 Troxler Test of 2<sup>nd</sup> Lift - 98% compaction and 18.7% moisture  
(Failed) Re Scratch:ing 1<sup>st</sup> Lift and moving Torpedo heaters  
into the hole to lower moisture level  
1200 Second Troxler Test on 1<sup>st</sup> Lift - 98.4% compaction 19.6% moisture  
1230 LUNCH BREAK  
1300 Resume work  
1310 Team began to back fill the hole due to failure to achieve  
compaction and or moisture level was too high  
1515 Heavy Equipment used to track in the dirt to  
prevent run off  
1615 Team cleaned Break Trailers and work area and  
completed vehicle maintenance  
1640 End of Week Brief  
1700 End of Day

*Matthew Riker*

# SOIL DAILY FIELD REPORT

Date: 12/5/19

Project #: 50000A Project Name: Remedial Action @ Glenbrook

Client: Parsons - Envision More

Technician's Name: Andrew Haldane Emp.#: HALA

Person in Charge, and their Company Joe Bryant, Parsons

Weather: Partly Cloudy Temp: 40

<input checked="" type="checkbox"/> Density Tests, quantity: <u>1</u>	Start Time: <u>5:30</u>	<u>Breaks</u>
<input type="checkbox"/> Sample Pickup:	Time On Site: <u>7:00</u>	<u>7:00 - 7:30</u>
Proctor: _____ Location _____	Time Off Site: _____	_____
1-PT: _____ Location _____	End Time: _____	_____
CBR: _____ Location _____	Total Time: _____	_____
<input type="checkbox"/> Delivery <input type="checkbox"/> Other _____		

Confection in area #4. High moisture content. No tests passed.  
Observed installation of 52 stone and geocloth over bedrock.

Signature of Technician Arvin T. White  
Signature of Site Representative [Signature]  
Project Manager Review \_\_\_\_\_

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 09 December 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 52 degrees, Rain, Winds 10-15 mph

**Personnel on Site**

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Jed	Yorkshire, Bart		
Oien, Josh			
Rider, Matt	<b>ACCUPERMIT</b>		
	Vargas, Brian		
	<b>CENAB</b>		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive digging. Cleaned bulldozer and rollers to be returned.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

09 DECEMBER, 2019 Monday  
Spring Valley, DC  
Matthew Rider, Safety

(18)

- 0630 Morning Safety Brief HI 52 Wind 10-15 mph WSW  
Humidity 90% Rain Most of the Day becoming cloudy at  
night chance of Rain 100%  $\frac{1}{8}$ " to  $\frac{3}{4}$ " expected
- 0700 Radio checks completed
- 0730 Team went downrange to prep for the washing of  
the Dozer and Rollers for Turn in
- 0800 Construction Mats in place, Team began cleaning  
Heavy Equipment for Turn in
- 0900 Myself And Josh went to Fed Prep to locate And gather  
information about our CCTV System used in the ECS
- 1130 Lunch Break
- 1200 Returned to work
- 1230 Bruce Took Rental Jeep back to Enterprise for oil change  
Exchanged vehicles. Sent Jenna Email to update Insurance
- 1400 Completed washing the Dozer and Rollers for Turn in
- 1430 Had A Sit Down About How to accomplish the Removal  
of the Soldier Pile Retaining wall
- 1630 Clean up And End of Day Brief
- 1700 End of Day

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 10 December 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 57 degrees, Rain, Winds 10-15 mph

**Personnel on Site**

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Jed	Yorkshire, Bart		
Oien, Josh			
Rider, Matt	<b>ACCUPERMIT</b>		
	Vargas, Brian		
	Williams, Donald		
	<b>CENAB</b>		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive digging. Installed super silt fence. Helped load CCDC connex. Drum inventory.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	



10 DECEMBER 2019, Tuesday  
Spring Valley, DC  
Matthew Rider, Safety

(1)

- 0630 Morning Safety Brief HI 57° Wind 10-15mph WSW  
Humidity 85% Rain possible 90% chance of Rain
- 0700 Radio checks completed
- 0800 Team began Replacing/removing old Silt Fence by the  
Vehicle gate to Replace it with A Super Silt Fence  
To help with Erosion Control when digging out the Solvent  
Piles
- 0915 ECBC Arrived At Federal Property to Pick up A Storage  
Container Full of PPE, Zimmer Assisted them with  
loading it onto the Truck
- 1100 Lunch Break
- 1130 Returned to work
- 1215 Todd called About the Trailer Roof leaking At Fed Prop  
Bruce went to Check it out
- 1300 Team Completed An inventory of Drums At Fed Prop  
Total Soil Drum Count is 365 And water Drums 12
- 1630 Clean up And End of Day Brief
- 1700 End of Day

~~Matthew Rider~~



## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 11 December 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 39 degrees, Partly Cloudy

**Personnel on Site**

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren		
	Wright, David		
Marion, Jed	Yorkshire, Bart		
Oien, Josh			
Rider, Matt	<b>ACCUPERMIT</b>		
	Vargas, Brian		
	Williams, Donald		
	<b>CENAB</b>		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive digging. Equipment pick-up. Started removal of flowable fill from soldier piles.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

11 December 2017, Wednesday  
Spring Valley, DC  
Matthew Rider, Safety

(20)

- 0630 Morning Safety Brief - HI 39 Wind 10-15 WNW Humidity 50%  
Snow Flurries early turning to Partly cloudy Afternoon (BRUCE OUT)
- 0700 Radio checks complete
- 0715 Team went down stairs to prep for the loading of the  
Dozer, Roller and mini Roller
- 0800 Put together a map diagram of the possible upcoming  
Level B operations
- 1030 Low boy Truck Arrives to load up the Dozer
- 1115 Lunch Break
- 1145 Returned to work
- 1200 Team Began to Set up to hammer out Fillerble Flow between  
the I-beams
- 1330 Hammer broke and needed changed out with one at  
Fed Prop
- 1400 New Hammer set up Resumed work
- 1445 Hydraulic line broke on Hammer
- 1515 Both Hammers Removed from site Shipped back to Fed Prop
- 1630 Clean up End of Day Brief
- 1900 End of Day

Matthew Rider

# SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 12 December 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 40 degrees, Sunny

## Personnel on Site

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren		
Courtney, Kenneth			
Marion, Jed	Yorkshire, Bart		
Rider, Matt	ACCUPERMIT		
	Vargas, Brian		
	Amaya, Kevin		
	CENAB		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive digging. Continued removing flowable fill from soldier piles. Pick-up parts for jackhammer.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

12 DECEMBER 2019, Thursday  
Spring Valley, DC  
Matthew Rider, Safety

(21)

0630 Morning Safety Brief, HI 40 WIND S-10mph E Humidity 50%  
Mostly Sunny with periods of cloudiness in the Afternoon  
(JOSH OUT) (DAVE OUT)  
0700 Radio checks complete  
0730 Team went downstairs to prep for the Roller to be  
Removed from the site on A Low Boy Truck  
0800 Team Resumed Jack Hammering / Hammer Drilling out the  
Flexible Fill  
0900 1030 Operations halted, both hammers are inoperable And  
Zimmer is out getting necessary Parts  
1130 Lunch Break  
1200 Resumed work  
1230 Vehicle maintenance is completed  
1245 Bruce went back over to reinspect the looking rock on  
the trailer At Fed Prop  
need to buy A Spreable patch  
1530 Completed Inventory for Items that will be needed for  
the winter. (need (Salt, ICE MELT) Shovel, Spreader)  
1630 End of WEEK Brief And Clean up  
1700 END of DAY

Matthew Rider

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 16 December 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 39 degrees, Snow/Rain

**Personnel on Site**

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Jed	Yorkshire, Bart		
Oien, Joshua			
Rider, Matt	<b>ACCUPERMIT</b>		
	Vargas, Brian		
	Vargas, Gustavo		
	<b>CENAB</b>		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30  
 No intrusive digging. Federal supplies inventory.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

16 DECEMBER 2019, Monday  
Spring Valley, DC  
Matthew Rider, safety

(22)

- 0630 Morning Safety Brief HI-39 wind S-10mph Humidity 95%  
Mix of wintry precipitation turning to Rain in the  
Afternoon. Chance of precipitation 100%
- 0700 Radio checks completed
- 0800 Team went to Federal property to conduct a police call  
of the Area to get it ready for the Holiday Break.
- 1030 Me and Josh began going through to conduct an Inventory  
Review of Accountable Items
- 1130 Lunch Break
- 1200 Returned to work
- 1330 JED and Warren went on a shopping run to Home Depot  
to purchase a pallet of ICE MELT for the upcoming winter  
work season
- 1500 Team went downstairs to prep for pick up of the  
mini walk behind Roller.
- 1545 Sun Belt called and canceled the pick up for the Roller  
due to Traffic
- 1630 Clean up and End of Day Brief
- 1700 End of Day

Matthew Rider



## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 17 December 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 46 degrees, Rain, Wind 10-20 mph

**Personnel on Site**

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Jed	Yorkshire, Bart		
Oien, Joshua			
Rider, Matt	<b>ACCUPERMIT</b>		
	Vargas, Brian		
	Vargas, Gustavo		
	<b>CENAB</b>		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30  
 No intrusive digging. Equipment pick-up.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

Visitors	Contractors
	Berkel ( )
	DAVEY ( )
	ACCUPERMIT ( )
	ACI (0)
	CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

17 DECEMBER, 2019 Tuesday  
Spring Valley, TX  
Mission Ridge Safety

(2)

- 0630 Morning Safety Brief - HZ-47 Wind 10-20mph NW Humidity 90%  
Showers in the morning becoming Steady Rain in the  
Afternoon
- 0700 Radio checks completed
- 0800 Team Conducted A police Call downstairs And repaired  
Replaced Inspected All Ems measures to make sure  
Everything is Ready to go for winter break
- 0915 Hertz Arrives to Pick up the mini walk behind  
Trench Roller
- 1110 Sun Belt Arrives to pick up Big Green Roller (Road  
was lined with Geo cloth And construction mats to  
prevent all damage)
- 1200 Lunch Break
- 1300 Team went to Fed Prop to organize the Hut to  
Allow Adequate Storage of ICE MELT And Additional  
Ems control measures
- 1630 End of Day Brief And Clean up
- 1700 End of Day

Matthew Poles

## SPRING VALLEY, WASHINGTON DC

Contract No: W912DY-09-D-0062  
 Delivery Order: TO 0006  
 Date: 18 December 2019  
 Site Location: 4825 Glenbrook Road

Weather: \_\_\_\_\_  
 High 38 degrees, Sunny/Breezy, Wind 10-20 mph

**Personnel on Site**

PARSONS	ZES	SCE	
Bryant, Joe	Prate, Warren		
Courtney, Kenneth	Wright, David		
Marion, Jed	Yorkshire, Bart		
Oien, Joshua			
Rider, Matt	<b>ACCUPERMIT</b>		
	Vargas, Brandon		
	Vargas, Brian		
	<b>CENAB</b>		
	Steelman, Brian		

ACTIVITIES CONDUCTED (include site mobilization/demobilization, brush/tree clearing, geophysical survey, intrusive excavation, contaminated soil excavation, sampling, and restoration activities)

Safety Briefing: 6:30

No intrusive digging. Prepared site for holiday leave.

End of day: 17:00

SAMPLES COLLECTED: See DQCR for sample information

Closed cavity items found

New Equipment on Site:

**Visitors**


**Contractors**

Berkel ( )
DAVEY ( )
ACCUPERMIT ( )
ACI (0)
CPJ (0)

Problems encountered/resolutions:

Instructions given by government personnel:

Activities anticipated for tomorrow:

Attachments (include as appropriate)		
	Y/N	
Geophysical Summary	Y/N	
Excavation Summary	Y/N	
Air Monitoring Summary	Y/N	To be included if investigation is using CSS protocols
Dig Sheet	Y/N	To be included at least once every week during intrusive investigation
Sample Chains-of-Custody (COCS)	Y/N	
Contingency Plan Initiation Summary	Y/N	
Health and Safety Report	Y/N	To be included weekly during field activities
Property Management Summary	Y/N	Include complete property inventory once every month
Photographs	Y/N	

18 DECEMBER 2011, Wednesday  
Spring Valley, DC  
Matthew Rider, Safety

(24)

- 0630 Morning Safety Brief - HI-40 wind - 10-20 w/w Humidity 50%  
Sunny Turning Partly Cloudy in the Afternoon Wind Gusts  
up to 30mph
- 0700 Radio checks completed
- 0800 Team went to Federal Property, to clean the Track And Tires  
And wash to Equipment Positioned there
- 1030 Went to check on Team make sure Everyone is okay
- 1100 Lunch Break
- 1130 Returned to work
- 1145 Team went downstairs to clean Tracks And wash Heavy  
Equipment Positioned at 4825 site
- 1500 Team did one last walk Around downstairs to ensure  
Site will be okay during Holiday Shutdown
- 1600 Clean up Trailers And Vehicle Maintenance
- 1630 End of week, Prior to break Safety Brief
- 1700 End of Day

Matthew Rider
